

**CONSTRUCTION DOCUMENTS  
AND TECHNICAL SPECIFICATIONS FOR  
2026 MERIWETHER CO LMIG RESURFACING PROJECT – PH II**

FOR

**MERIWETHER COUNTY BOARD OF COMMISSIONERS**  
17234 ROOSEVELT HIGHWAY, BUILDING B  
GREENVILLE, GEORGIA 30222


EMC PROJECT NO: 26-7011

MAY 2026



**PREPARED BY**

**EMC ENGINEERING SERVICES, INC.**



ENVIRONMENTAL  
MARINE  
CIVIL  
SURVEY

3575 MACON ROAD, SUITE 15  
COLUMBUS, GEORGIA 31907  
(706) 565-5985  
[www.emc-eng.com](http://www.emc-eng.com)

ALBANY, ATLANTA, AUGUSTA, BRUNSWICK, COLUMBUS, SAVANNAH, STATESBORO, & VALDOSTA

**CONTRACT DOCUMENTS  
&  
TECHNICAL SPECIFICATIONS**

**2026 MERIWETHER COUNTY  
LMIG RESURFACING PROJECT – PH 2**

**RESURFACING OF:  
ALVATON ROAD**

**MERIWETHER COUNTY  
BOARD OF COMMISSIONERS**

**MAY 2026**

**EMC PROJECT NO. 26-7011**

Prepared By:  
**EMC Engineering Services, Inc.**  
3575 Macon Rd # 15  
Columbus, GA 31907

## **TABLE OF CONTENTS**

**Advertisement for Bids**

**Information for Bidders**

**Immigration and Security Form**

**SAVE Program Affidavit**

**Bid**

**Bid Form**

**Bid Bond**

**Non-Collusion of Bidders**

**Certification Regarding Debarment**

**Agreement**

**Payment Bond**

**Performance Bond**

**Notice of Award**

**Notice to Proceed**

**General Conditions**

**Project Drawings**

**ADVERTISEMENT FOR BIDS FOR  
CONSTRUCTION OF  
  
2026 LMIG RESURFACING PROJECT  
  
FOR THE  
MERIWETHER COUNTY BOARD OF  
COMMISSIONERS**

Meriwether County Board of Commissioners  
17234 Roosevelt Highway, Building B  
Greenville, GA 30222

Sealed BIDS for the 2026 Meriwether County LMIG Resurfacing Project Phase II will be received by Meriwether County at the Meriwether County Board of Commissioners Office located at 17234 Roosevelt Highway, Building B, Greenville GA 30222 until **11:00 AM, Local Time on July 9, 2026**, and then at said office will be publicly opened and read aloud. The project includes the resurfacing and associated work of Alvaton Road from Hwy 85 to 2 miles west of Hwy 85 to Luthersville Road – the total project mileage is approximately 3.5 miles. All roads will receive asphalt patching as required, leveling/ crack relief layer, and asphalt as final surface, striping, and shoulder building.

The CONTRACT DOCUMENTS may be examined at the following locations:  
Meriwether County Board of Commissioners at 17234 Roosevelt Highway, Building B, Greenville GA 30222.

A mandatory pre-bid conference will be held at **11:00 AM on June 18, 2026**, at the Board of Commissioners' Office located 17234 Roosevelt Highway, Building B, Greenville GA 30222. Project scheduling, coordination requirements, and questions of interpretation will be addressed at this time.

All bids must be accompanied by a Bid Bond in an amount not less than five percent (5%) of the Base Bid. Performance Bond and Payment Bond, each in the amount of one hundred percent (100%) of the contract amount, will be required of the successful bidder. Bonds must be written by an acceptable Surety Company licensed to do business in the State of Georgia and listed in the Department of the Treasury, Circular 570, latest edition.

NOTE: Contractor and all subcontractors must obtain a business license in Georgia, be fully insured, and be a Licensed Contractor in the State of Georgia.

INSURANCE: Contractor shall maintain the following insurance (a) comprehensive general liability, including blanket contractual, covering bodily injuries with limits of no less than \$1,000,000 per occurrence, and property damage with limits of no less than \$1,000,000 per occurrence; and (b) commercial automobile liability, including blanket contractual, covering bodily injuries with limits of no less than \$1,000,000 per

occurrence, and property damage with limits of no less than \$1,000,000 per accident (c) statutory worker's compensation insurance, including \$1,000,000 employer's liability insurance (d) employee dishonesty and/or crimes coverage with respect to personnel of Contractor having access to County buildings, with limits of no less than \$50,000 per occurrence. All insurance shall be provided by an insurer(s) acceptable to the County, and shall provide for thirty (30) days prior notice of cancellation to the County. Upon request, Contractor shall deliver to the County a certificate or policy of insurance evidencing Contractor's compliance with this paragraph. Contractor shall abide by all terms and conditions of the insurance and shall do nothing to impair or invalidate the coverage.

The successful bidder shall secure and pay for all permits, assessments, charges or fees required in connection with the proposed construction. Answers to all questions shall be provided a minimum of 72 hours prior to the time of the bid.

All work to be performed under this project must be completed within 120 consecutive calendar days following receipt of Notice to Proceed.

Meriwether County reserves the right to reject any or all bids, including without limitation, the right to reject any and all nonconforming, non-responsive, unbalanced or conditional bids and to reject the bid of any bidder whom the Owner believes would not be in the best interest of the Project to make an award to that bidder whether because the bid is not responsive, the bidder is unqualified, or of doubtful financial ability or fails to meet any other pertinent standard or criteria established by the Owner.

Qualified Bidders may obtain digital copies of the CONTRACT DOCUMENTS, Specifications, and upon a non-refundable payment of \$100.00 for each set at the Columbus office of EMC Engineering Services, Inc. Please contact Karlee Jenks at (706) 565-5985, [columbus@emc-eng.com](mailto:columbus@emc-eng.com).

John Gorton, County Administrator  
Meriwether County Board of Commissioners

## INFORMATION FOR BIDDERS

BIDS will be received by the Meriwether County Board of Commissioners (herein called the "OWNER"), at 17234 Roosevelt Highway, Building B, Greenville GA 30222 Georgia until 11:00 AM. Local Time, July 9, 2026, and then at said office publicly opened and read aloud.

Each BID must be submitted in a sealed envelope, addressed to the Meriwether County Board of Commissioners 17234 Roosevelt Highway, Building B, Greenville, GA. Each sealed envelope containing a BID must be plainly marked on the outside as BID for 2026 Meriwether County LMIG Resurfacing Project and the envelope should bear on the outside the name of the BIDDER, his address, his license number. If forwarded by mail, the sealed envelope containing the BID must be enclosed in another envelope addressed to the OWNER at 17234 Roosevelt Highway, Building B, Greenville, GA.

All BIDS must be made on the required BID form. All blank spaces for BID prices must be filled in, in ink or typewritten, and the BID form must be fully completed and executed when submitted. Only one copy of the BID form is required.

The OWNER may waive any informalities or minor defects or reject any and all BIDS. Any BID may be withdrawn prior to the above scheduled time for the opening of BIDS or authorized postponement thereof. Any BID received after the time and date specified shall not be considered. No BIDDER may withdraw a BID within 60 days after the actual date of the opening thereof. Should there be reasons why the contract cannot be awarded within the specified period, the time may be extended by mutual agreement between the OWNER and the BIDDER.

### Tentative Bid Schedule

|                      |                          |
|----------------------|--------------------------|
| First Advertisement  | June 5, 2026             |
| Second Advertisement | June 12, 2026            |
| Pre-Bid Conference   | June 18, 2026 (11:00 AM) |
| Bids Due             | July 9, 2026 (11:00 AM)  |

Georgia Department of Transportation Standard Specifications for Construction of Transportation Systems, Current Edition, to include most recent revisions, are the governing standards for this project. All striping shall be in accordance with current MUTCD Standards.

BIDDERS must satisfy themselves of the accuracy of the estimated quantities in the BID Schedule by examination of the site and a review of the drawings and specifications including ADDENDA. After BIDS have been submitted, the BIDDER shall not assert that there was a misunderstanding concerning the quantities of WORK or of the nature of the WORK to be done.

The OWNER shall provide to BIDDERS prior to BIDDING, all information that is pertinent to, and delineates and describes, the land owned and rights-of-way acquired or to be acquired.

The CONTRACT DOCUMENTS contain the provisions required for the construction of the PROJECT. Information obtained from an officer, agent, or employee of the OWNER or any other person shall not affect the risks or obligations assumed by the CONTRACTOR or relieve him from fulfilling any of the conditions of the contract.

Attorneys-in-fact who sign BID BONDS or payment BONDS and performance BONDS must file with each BOND a certified and effective dated copy of their power of attorney.

The party to whom the contract is awarded will be required to execute the Agreement within ten (10) calendar days from the date when NOTICE OF AWARD is delivered to the BIDDER. The NOTICE OF AWARD shall be accompanied by the necessary Agreement form. In case of failure of the BIDDER to execute the Agreement, the OWNER may at his option consider the BIDDER in default.

The OWNER, within ten (10) days of receipt of acceptable Agreement signed by the party to whom the Agreement was awarded, shall sign the Agreement and return to such party an executed duplicate of the Agreement. Should the OWNER not execute the Agreement within such period, the BIDDER may by WRITTEN NOTICE withdraw his signed Agreement. Such notice of withdrawal shall be effective upon receipt of the notice by the OWNER.

The NOTICE TO PROCEED shall be issued within ten (10) days of the execution of the Agreement by the OWNER. Should there be reasons why the NOTICE TO PROCEED cannot be issued within the ten (10) day period or within the period mutually agreed upon, the CONTRACTOR may terminate the Agreement without further liability on the part of either party.

The OWNER may make such investigations as he deems necessary to determine the ability of the BIDDER to perform the WORK, and the BIDDER shall furnish to the OWNER all such information and data for this purposed as the OWNER may request. The OWNER reserves the right to reject any BID if the evidence submitted by, or investigation of, such BIDDER fails to satisfy the OWNER that such BIDDER is properly qualified to carry out the obligations of the Agreement and to complete the WORK contemplated therein.

A conditional or qualified BID will not be accepted. Award will be made to the lowest responsible BIDDER.

OWNER reserves the right to award project based on base bid only or any combination of alternates, if applicable, at their sole discretion.

All applicable laws, ordinances, and the rules and regulations of all authorities having jurisdiction over construction of the PROJECT shall apply to the contract throughout.

Each BIDDER is responsible for inspecting the site and for reading and being thoroughly familiar with the CONTRACT DOCUMENTS. The failure or omission of any BIDDER to do any of the foregoing shall in no way relieve any BIDDER from any obligation in respect to his BID.

The low BIDDER shall supply the names and addresses of major material SUPPLIERS and SUBCONTRACTORS when requested to do so by the OWNER. All bidders must have a State of Georgia Utility Contractors License.

## **Georgia Security and Immigration Compliance Act**

CONTRACTOR must execute an affidavit verifying that CONTRACTOR has registered and participates in the federal work authorization program to verify information of all new employees, per O.C.G.A. 13-10-90, et.seq., and Georgia Department of Labor Regulations Rule 300-10-1-02, and must execute an affidavit verifying residency status per O.C.G.A. 50-36-1, et.seq. The appropriate affidavits are attached to these contract documents, and are incorporated herein by reference and made a part of this contract.

The CONTRACTOR further certifies that any SUBCONTRACTOR employed by CONTRACTOR for the performance of this agreement has executed appropriate SUBCONTRACTOR affidavits verifying its registration and participation in the federal work authorization program and compliance with O.C.G.A. 13-10-90, et.seq., and Georgia Department of Labor Regulations Rule 300-10-1-02, and verifying residency status per O.C.G.A. 50-36-1, et.seq, and that all such affidavits are incorporated into and made a part of every contract between the CONTRACTOR and each SUBCONTRACTOR.

CONTRACTOR'S compliance with O.C.G.A. 13-10-90, et. seq., Georgia Department of Labor Regulations Rule 300-10-1-02, and O.C.G.A. 50-36-1 et. seq is a material condition of this agreement and Contractor's failure to comply with said provisions shall constitute a material breach of this agreement.

All BIDS must be accompanied by a BID Bond in an amount not less than five percent (5%) of the Base BID. Performance Bond and Payment Bond, each in the amount of one hundred percent (100%) of the contract amount, will be required of the successful BIDDER. Bonds must be written by an acceptable Surety Company licensed to do business in the State of Georgia and listed in the Department of the Treasury, Circular 570, latest edition.

NOTE: Contractor and subcontractor must obtain a business license in Georgia, be fully insured, and be a Licensed Contractor in the State of Georgia.

The successful BIDDER shall secure and pay for all permits, assessments, charges or fees required in connection with the proposed construction.

The following items must be submitted in the sealed bid package:

- 1) Bid
- 2) Bid form
- 3) Bid Bond
- 4) Non-Collusion Affidavit
- 5) Current Business License

Meriwether County reserves the right to reject any or all bids, including without limitation, the right to reject any and all nonconforming, non-responsive, unbalanced or conditional bids and to reject the bid of any bidder whom Owner believes would not be in the best interest of the Project to make an award to that bidder whether because the bid is not responsive, the bidder is unqualified, or of doubtful financial ability or fails to meet any other pertinent standard or criteria established by the Owner.

## IMMIGRATION AND SECURITY FORM

O.C.G.A. § 13-10-91 requires contractors interested in public works contracts to file an affidavit that the contractor and its subcontractors have registered and participate in a federal work authorization program intended to insure that only lawful citizens or lawful immigrants are employed by the contractor or subcontractor.

In order to insure compliance with the Immigration Reform and Control Act of 1986 (IRCA), D.L. 99-603 and the Georgia Security and Immigration Compliance Act OCGA 13-10-90 et.seq., Contractor must warrant and affirm that Contractor has complied with the Immigration Reform and Control Act of 1986 (IRCA), D.L. 99-603 and the Georgia Security and Immigration Compliance Act by registering at <https://e-verify.uscis.gov/enroll/StartPage.aspx?JS=YES>; and verifying information of all new employees; and by executing any affidavits required by the rules and regulations issued by the Georgia Department of Labor set forth at Rule 300-10-1-.01 et.seq.

By executing this affidavit, the undersigned Contractor verifies its compliance with O.C.G.A. § 13-10-91, stating affirmatively that the individual, firm, or corporation which is contracting with MERIWETHER County, Georgia has registered with and is participating in a federal work authorization program [any of the electronic verification of work authorization programs operated by the United States Department of Homeland Security or any equivalent federal work authorization program operated by the United States Department of Homeland Security to verify information of newly hired employees, pursuant to the Immigration Reform and Control Act of 1986 (IRCA), P.L. 99-603], in accordance with the applicability provisions and deadlines established in O.C.G.A. § 13-10-91, and Contractor warrants that it will continue to use the federal work authorization program throughout the contract period.

The undersigned further agrees that, should it employ or contract with any subcontractor(s) in connection with the physical performance of services pursuant to this contract with MERIWETHER County, Georgia, Contractor will secure from such subcontractor(s) similar verification of compliance with O.C.G.A. § 13-10-91 on the Subcontractor Affidavit provided in Georgia Department of Labor Rule 300-10-01-.08 or a substantially similar form. Contractor further agrees to maintain records of such compliance and provide a copy of each such verification to MERIWETHER County, Georgia at the time the subcontractor(s) is retained to perform such service.

\_\_\_\_\_  
Signature

\_\_\_\_\_  
Title

Firm Name: \_\_\_\_\_

Street/Mailing Address: \_\_\_\_\_

City, State, Zip Code: \_\_\_\_\_

Telephone Number: \_\_\_\_\_

Email: \_\_\_\_\_

User Identification Number: \_\_\_\_\_

Date of Authorization: \_\_\_\_\_

## Exhibit B

### Affidavit Verifying Status for County Public Benefit Application

By executing this affidavit under oath, as an applicant for the award of a contract with Meriwether County, Georgia, I \_\_\_\_\_. [Name of natural person applying on behalf of individual, business, corporation, partnership, or other private entity] am stating the following as required by O.C.G.A. Section 50-36-1:

1) \_\_\_\_\_ I am a United States citizen

**OR**

2) \_\_\_\_\_ I am a legal permanent resident 18 years of age or older or I am an otherwise qualified alien or non-immigrant under the Federal Immigration and Nationality Act 18 years of age or older and lawfully present in the United States.\*

In making the above representation under oath, I understand that any person who knowingly and willfully makes a false, fictitious, or fraudulent statement or representation in an affidavit shall be guilty of a violation of Code Section 16-10-20 of the Official Code of Georgia.

Signature of Applicant:      Date

\_\_\_\_\_

Printed Name:

\_\_\_\_\_

SUBSCRIBED AND SWORN  
BEFORE ME ON THIS THE  
\_\_\_\_ DAY OF \_\_\_\_\_, 20\_\_\_\_.

\* \_\_\_\_\_  
Alien Registration number for non-citizens

\_\_\_\_\_  
Notary Public  
My commission Expires:

**\*Note:** O.C.G.A. § 50-36-1(e)(2) requires that aliens under the federal Immigration and Nationality Act, Title 8 U.S.C., as amended, provide their registration number. Because legal permanent residents are included in the federal definition of “alien”, legal permanent residents must also provide their alien registration number. Qualified aliens that do not have an alien registration number may supply another identifying number below.

\_\_\_\_\_

## BID

Proposal of \_\_\_\_\_ (hereinafter called "BIDDER"), organized and existing under the laws of the State of \_\_\_\_\_  
Doing business as\* \_\_\_\_\_.  
To the Meriwether County Board of Commissioners (hereinafter called "OWNER").

In compliance with your Advertisement for Bids, BIDDER hereby proposes to perform all WORK for the construction of Meriwether County 2026 LMIG Resurfacing Project in strict accordance with the CONTRACT DOCUMENTS, within the time set forth therein, and at the prices stated below.

By submission of this BID, each BIDDER certifies, and in the case of a joint BID each party thereto certifies as to his own organization, that this BID has been arrived at independently, without consultation, communication, or agreement as to any matter relating to this BID with any other BIDDER or with any competitor.

BIDDER hereby agrees to commence WORK under this contract on or before a date to be specified in the NOTICE TO PROCEED and to fully complete the PROJECT within 120 consecutive calendar days thereafter. BIDDER further agrees to pay as liquidated damages, the sum of \$ 250.00 for each consecutive calendar day thereafter as provided in Section 15 of the General Conditions.

BIDDER acknowledges receipt of the following ADDENDUM:

---

---

---

\*Insert "a corporation", "a partnership", or "an individual" as applicable.

| 2026 MERIWETHER COUNTY LMIG PROJECT |            |
|-------------------------------------|------------|
| ALVATON ROAD                        | 3.5        |
| <b>RESURFACING TOTAL=</b>           | <b>3.5</b> |

| NO.                             | ITEM NO. | ITEM DESCRIPTION                                                                                          | QTY  | UNIT | UNIT PRICE | TOTAL       |
|---------------------------------|----------|-----------------------------------------------------------------------------------------------------------|------|------|------------|-------------|
| 1                               | 150-1000 | TRAFFIC CONTROL                                                                                           | 1    | LS   |            | \$ -        |
| 2                               | 210-1000 | SHOULDER BACKFILLING (BOTH SIDES), GRADE, COMPACT, TEMP & PERM GRASS                                      | 3.5  | ML   |            | \$ -        |
| 3                               | 432-0205 | MILL ASPH CONC PVMT, AT TRANSITIONS & BRIDGES (150 FT ON EACH SIDE)                                       | 1000 | SY   |            | \$ -        |
| 4                               | 402-9901 | RECYCLED ASPHALT CONCRETE PATCHING COURSE (19 MM SP, 440 LBS/ SY MAX) - MISCELLANEOUS AS NECESSARY        | 50   | TN   |            | \$ -        |
| 4                               | 402-1812 | RECYCLED ASPHALT CONCRETE LEVELING COURSE (OGI) INCL BITUM MATERIAL, H LIME, TYPE I (85 LBS/SY)           | 2150 | TN   |            | \$ -        |
| 5                               | 402-3121 | 1.5" RECYCLED ASPHALT CONCRETE WEARING COURSE (12.5 MM TYPE II) INCL BITUM MATERIAL, H LIME, (165 LBS/SY) | 4200 | TN   |            | \$ -        |
| 6                               | 652-2501 | SINGLE WHITE SOLID STRIPE, 5" HIGH BUILD PAINT                                                            | 7    | LM   |            | \$ -        |
| 7                               | 652-2502 | CENTERLINE YELLOW SOLID STRIPE, 5" HIGH BUILD PAINT                                                       | 3.5  | RM   |            | \$ -        |
| 8                               | 413-1000 | BITUMINOUS TACK COAT                                                                                      | 8000 | GL   |            | \$ -        |
| 9                               | 653-1000 | THERMO PLASTIC SOLID TRAFFIC STRIPE, 24 INCH, WHITE (STOP BAR)                                            | 3    | EA   |            | \$ -        |
| <b>BASE CONSTRUCTION TOTAL:</b> |          |                                                                                                           |      |      |            | <b>\$ -</b> |

Submitted By: \_\_\_\_\_

Title: \_\_\_\_\_

Company: \_\_\_\_\_

Date: \_\_\_\_\_

Signature: \_\_\_\_\_

## Bid Bond

KNOW ALL MEN BY THESE PRESENTS, that we, the undersigned, \_\_\_\_\_  
\_\_\_\_\_ as Principal, and  
\_\_\_\_\_ as Surety, are hereby held and firmly  
bound unto \_\_\_\_\_ Meriwether County Board of Commissioners \_\_\_\_\_ as OWNER in  
the penal sum of \_\_\_\_\_ 5 Percent of Amount Bid \_\_\_\_\_ for the payment of which, well  
and truly to be made, we hereby jointly and severally bind ourselves, successors and assigns.  
Signed, this \_\_\_\_\_ day of \_\_\_\_\_, 20\_\_\_\_\_.  
The Condition of the above obligation is such that whereas the Principal has submitted to  
\_\_\_\_\_ Meriwether County Board of Commissioners \_\_\_\_\_ a certain BID, attached  
hereto and hereby made a part hereof to enter into a contract in writing, for the \_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

NOW, THEREFORE,

(a) If said BID shall be rejected, or  
(b) If said BID shall be accepted and the Principal shall execute and deliver a  
contract in the Form of Contract attached hereto (properly completed in  
accordance with said BID) and shall furnish a BOND for his faithful  
performance of said contract, and for the payment of all persons performing labor or furnishing  
materials in connection therewith, and shall in all other respects perform the agreement created  
by the acceptance of said BID, then this obligation shall be void, otherwise the same shall remain  
in force and effect; it being expressly understood and agreed that the liability of the Surety for any  
and all claims hereunder shall, in no event, exceed the penal amount of this obligation as herein  
stated.

The Surety, for value received, hereby stipulates and agrees that the obligations of said Surety  
and its BOND shall be in no way impaired or affected by any extension of the time within which the  
OWNER may accept such BID; and said SURETY does hereby waive notice of any such tensions.

## Bid Bond

IN WITNESS WHEREOF, the Principal and the Surety have hereunto set their hands and seals, and such of them as are corporations have caused their corporate seals to be hereto affixed and these presents to be signed by their proper officers, the day and year first set forth above.

\_\_\_\_\_(L.S.)  
Principal

\_\_\_\_\_  
Surety

By: \_\_\_\_\_

IMPORTANT - Surety companies executing BONDS must appear on the Treasury Department's most current list (Circular 570 as amended) and be authorized to transact business in the state where the project is located.

### Non-Collusion Affidavit of Prime Bidder/Subcontractor

State of Georgia  
Meriwether County, Georgia

\_\_\_\_\_, being the first duly sworn, deposes and says that:

1. He/she is \_\_\_\_\_ of \_\_\_\_\_  
(Owner, partner, etc.) (Company)

the Bidder that has submitted the attached Bid;

2. He/she is fully informed respecting the preparation and contents of the attached Bid and of all pertinent circumstances respecting such Bid;

3. Such Bid is genuine and is not a collusive or sham Bid;

4. Neither the said Bidder nor any of its officers, partners, owners, subcontractors, agents, representatives, employees or parties in interest including this affiant, has in any way colluded, conspired, connived or agreed, directly or indirectly, with any other Bidder, firm or person to submit a sham Bid in connection with the Contract for which the attached Bid has been submitted or to refrain from bidding in connection with such Contract, or has in any manner, directly or indirectly sought by agreement or collusion or communication or conference with any other Bidder, firm or person to fix price or prices in the attached Bid or of any other Bidder, or to fix overhead, profit or cost element of the bid price or the bid price of any other bidder, or to secure through any collusion, conspiracy, connivance or unlawful agreement and advantage against Meriwether County or any person interested in the proposed contract;

5. The price or prices quoted in the attached Bid are fair and proper and are not tainted by any collusion, conspiracy, connivance or unlawful agreement on the part of the Bidder or any of its agents, representatives, owners, employees or parties in interest including this affiant;

Signature: \_\_\_\_\_

Date: \_\_\_\_\_

Name & Title: \_\_\_\_\_

Notary: \_\_\_\_\_

My Commission Expires: \_\_\_\_\_

---

CERTIFICATION REGARDING DEBARMENT SUSPENSION, AND OTHER  
RESPONSIBILITY MATTERS - PRIMARY COVERED TRANSACTIONS

---

INSTRUCTIONS FOR CERTIFICATION

1. By signing and submitting this proposal, the prospective primary participant is providing the certification set out below.
2. The inability of a person to provide the certification required below will not necessarily result in denial of participation in this covered transaction. The prospective participant shall submit an explanation of why it cannot provide the certification set out below. The certification or explanation will be considered in connection with the department or agency's determination whether to enter into this transaction. However, failure of the prospective primary participant to furnish a certification or an explanation could disqualify such person from participation in this transaction.
3. The certification in this clause is a material representation of fact upon which reliance was placed when the department or agency determined to enter into this transaction. If it is later determined that the prospective primary participant knowingly rendered an erroneous certification, in addition to other remedies available, the County may terminate this transaction for cause or default.
4. The prospective primary participant shall provide immediate written notice to the department or agency to which this proposal is submitted if at any time the prospective primary participant learns that its certification was erroneous when submitted or has become erroneous by reason of changed circumstances.
5. The terms covered transaction, debarred, suspended, ineligible, lower tier covered transaction, participant, person, primary covered transaction, principal, proposal, and voluntarily excluded, as used in this clause, have the meanings set out in the Definitions and Coverage sections of the rules implementing Executive Order 12549. You may contact the department to which this proposal is being submitted for assistance in obtaining a copy of those regulations.
6. The prospective primary participant agrees by submitting this proposal that should the proposed covered transaction be entered into, it shall not knowingly enter into any lower tier covered transaction with a person who is proposed for debarment under 48 CFR part 9, subpart 9.4, debarred, suspended, declared ineligible, or voluntarily excluded from participation in this covered transaction, unless authorized by the department or agency entering into this transaction.
7. The prospective primary participant further agrees by submitting this proposal that it will include the clause titled "Certification Regarding Debarment, Suspension, Ineligibility and Voluntary Exclusion-Lower Tier Covered Transaction," provided by the department or agency entering into this covered transaction, without modification, in all lower tier covered transactions and in all solicitations for lower tier covered transactions.
8. A participant in a covered transaction may rely upon a certification of a prospective participant in a lower tier covered transaction that it is not proposed for debarment under 48 CFR part 9, subpart 9.4, debarred, suspended, ineligible, or voluntarily excluded from the covered transaction, unless it knows that the certification is erroneous. A participant may decide the method and frequency by which it determines the eligibility of its principals. Each participant may, but is not required to, check the list of Parties Excluded from Federal Procurement and Non-procurement Programs.

9. Nothing contained in the foregoing shall be construed to require establishment of a system of records in order to render in good faith the certification required by this clause. The knowledge and information of a participant is not required to exceed that which is normally possessed by a prudent person in the ordinary course of business dealings.
10. Except for transactions authorized under paragraph 6 of these instructions, if a participant in a covered transaction knowingly enters into a lower tier covered transaction with a person who is proposed for debarment under 49 CFR part 9, subpart 9.4, suspended, debarred, ineligible, or voluntarily excluded from participation in this transaction, in addition to other remedies available to the Federal Government, the department or agency may terminate this transaction for cause or default.

### CERTIFICATION

- (1) The prospective primary participant certifies to the best of its knowledge and belief, that it and its principals:
- (a) Are not presently debarred, suspended, proposed for debarment, declared ineligible, or voluntarily excluded by any Federal department or agency.
  - (b) Have not within a three-year period preceding this proposal been convicted of or had a civil judgment rendered against them for commission of fraud or a criminal offense in connection with obtaining, attempting to obtain, or performing a public (Federal, State or local) transaction or contract under a public transaction; violation of Federal or State antitrust statutes or commission of embezzlement, theft, forgery, bribery, falsification or destruction of records, making false statements, or receiving stolen property;
  - (c) Are not presently indicted for or otherwise criminally or civilly charged by a governmental entity (Federal, State or local) with commission of any of the offenses enumerated in paragraph (1)(b) of this certification; and
  - (d) Have not within a three-year period preceding this application/proposal had one or more public transactions (Federal, State or local) terminated for cause or default.
- (2) Where the prospective primary participant is unable to certify to any of the statements in this certification, such prospective participant shall attach an explanation to this proposal.

---

Organization Name

---

PR/Award or Project Name

---

Name and Title

---

Signature

---

Date

## AGREEMENT

THIS AGREEMENT, made this \_\_\_\_\_ day of \_\_\_\_\_, 2026, by and between the Meriwether County Board of Commissioners, hereinafter called "OWNER" and \_\_\_\_\_ doing business as (an individual), or a (partnership), or a (corporation) hereinafter called "CONTRACTOR".

WITNESSETH: That for and in consideration of the payments and agreements herein-after mentioned:

1. The CONTRACTOR will commence and complete the delivery of materials for 2026 MERIWETHER COUNTY LMIG PROJECT

2. The CONTRACTOR will furnish all of the materials, tools, equipment, labor and other services necessary for the construction and completion of the PROJECT described herein.

3. The CONTRACTOR will commence the work required by the CONTRACT DOCUMENTS within 10 calendar days after the date of the NOTICE TO PROCEED and will complete the same within 120 calendar days unless the period for completion is extended otherwise by the CONTRACT DOCUMENTS.

4. The CONTRACTOR agrees to perform all of the WORK described in the CONTRACT DOCUMENTS and comply with the terms therein for the sum of \$ \_\_\_\_\_, or as shown in the BID schedule.

5. The term "CONTRACT DOCUMENTS" means and includes the following:

(A) Advertisement for BIDS

(B) Information For BIDDERS

(C) BID

(E) Agreement

(F) General Conditions

(G) SUPPLEMENTAL GENERAL CONDITIONS

(J) NOTICE OF AWARD

(K) NOTICE TO PROCEED

(L) CHANGE ORDER

(M) DRAWINGS prepared by EMC Engineering Services, Inc. labeled:

MERIWETHER COUNTY 2026 LMIG EXHIBIT

dated May, 2026.

(N) SPECIFICATIONS prepared or issued by  
EMC Engineering Services, Inc. dated May, 2026.

(O) ADDENDA

NO. \_\_\_\_\_, dated \_\_\_\_\_, 20 \_\_\_\_\_

NO. \_\_\_\_\_, dated \_\_\_\_\_, 20 \_\_\_\_\_

NO. \_\_\_\_\_, dated \_\_\_\_\_, 20 \_\_\_\_\_

NO. \_\_\_\_\_, dated \_\_\_\_\_, 20 \_\_\_\_\_

NO. \_\_\_\_\_, dated \_\_\_\_\_, 20 \_\_\_\_\_

NO. \_\_\_\_\_, dated \_\_\_\_\_, 20 \_\_\_\_\_

6. The OWNER will pay to the CONTRACTOR in the manner and at such times as set forth in the General Conditions such amounts as required by the CONTRACT DOCUMENTS.

7. This Agreement shall be binding upon all parties hereto and their respective heirs, executors, administrators, successors, and assigns.

IN WITNESS WHEREOF, the parties hereto have executed, or caused to be executed by

their duly authorized officials, this Agreement in ( \_\_\_\_\_ 3 \_\_\_\_\_ ) each of  
(Number of Copies)

which shall be deemed an original on the date first above written.

OWNER:

Meriwether County Board of

Commissioners

BY \_\_\_\_\_

Name Emmett Collins  
(Please Type)

Title Chairman, Board of Commissioners

(SEAL)

ATTEST:

\_\_\_\_\_

Name Allyson Stephens  
(Please Type)

Title County Clerk

CONTRACTOR:

\_\_\_\_\_

BY \_\_\_\_\_

Name \_\_\_\_\_  
(Please Type)

(SEAL)

ATTEST:

\_\_\_\_\_

Name \_\_\_\_\_  
(Please Type)

Title \_\_\_\_\_

## PAYMENT BOND

KNOW ALL MEN BY THESE PRESENTS: that

\_\_\_\_\_  
(Name of Contractor)

\_\_\_\_\_  
(Name of Contractor)

a \_\_\_\_\_, hereinafter called Principal,  
Corporation, Partnership, or Individual)

and \_\_\_\_\_  
(Name of Surety)

\_\_\_\_\_  
(Address of Surety)

hereinafter called Surety, are held and firmly bound unto \_\_\_\_\_

Meriwether County Board of Commissioners  
(Name of Owner)

17234 Roosevelt Highway Building B  
(Address of Owner)

hereinafter called OWNER, in the penal sum of \_\_\_\_\_ Dollars,  
\$(\_\_\_\_\_)

in lawful money of the United States, for the payment of which sum well and truly to be made, we  
bind ourselves, successors, and assigns, jointly and severally, firmly by these presents.

THE CONDITION OF THIS OBLIGATION is such that whereas, the Principal entered into a  
certain contract with the OWNER, dated the \_\_\_\_\_ day of \_\_\_\_\_  
20\_\_\_\_\_, a copy of which is hereto attached and made a part hereof for the construction  
of:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_  
NOW, THEREFORE, if the Principal shall promptly make payment to all persons, firms,  
SUBCONTRACTORS, and corporations furnishing materials for or performing labor in the  
prosecution of the WORK provided for in such contract, and any authorized extension or  
modification thereof, including all amounts due for materials, lubricants, oil, gasoline, coal and  
coke, repairs on machinery, equipment and tools, consumed or used in connection with the  
construction of such WORK, and all insurance premiums on said WORK, and for all labor,  
performed in such WORK whether by SUBCONTRACTOR or otherwise, then this obligation shall  
be void; otherwise to remain in full force and effect.

PROVIDED, FURTHER, that the said Surety for value received hereby stipulates and agrees that  
no change, extension of time, alteration or addition to the terms of the contract or to the WORK to  
be performed thereunder or the SPECIFICATIONS accompanying the same shall in any wise  
affect its obligation on this BOND, and it does hereby waive notice of any such change, extension  
of time, alteration or addition to the terms of the contract or to the WORK or to the  
SPECIFICATIONS.

PROVIDED, FURTHER, that no final settlement between the OWNER and the CONTRACTOR shall abridge the right of any beneficiary hereunder, whose claim may be unsatisfied.

IN WITNESS WHEREOF, this instrument is executed in \_\_\_\_\_ counterparts, each  
(number)  
one of which shall be deemed an original, this the \_\_\_\_\_ day of \_\_\_\_\_, 20 \_\_\_\_\_.

ATTEST:

\_\_\_\_\_  
principal  
\_\_\_\_\_  
(Principle) Secretary

BY \_\_\_\_\_(s)  
\_\_\_\_\_  
(Address)  
\_\_\_\_\_

\_\_\_\_\_  
Witness as to Principal  
\_\_\_\_\_  
(Address)  
\_\_\_\_\_

\_\_\_\_\_  
(Address)  
BY \_\_\_\_\_  
Principal  
\_\_\_\_\_

Attest:

\_\_\_\_\_  
Witness as to Surety  
\_\_\_\_\_  
(Address)

NOTE: Date of BOND must not be prior to date of Contract.  
If CONTRACTOR is Partnership, all partners should execute BOND.

IMPORTANT: Surety companies executing BONDS must appear on the Treasury Department's most current list (Circular 570 as amended) and be authorized to transact business in the State where the PROJECT is located.

## PERFORMANCE BOND

KNOW ALL MEN BY THESE PRESENTS: that

\_\_\_\_\_  
(Name of Contractor)

\_\_\_\_\_  
(Address of Contractor)

a \_\_\_\_\_, hereinafter called Principal, and  
(Corporation, Partnership, or Individual)

\_\_\_\_\_  
(Name of Surety)

\_\_\_\_\_  
(Address of Surety)

hereinafter called SURETY, are held and firmly bound unto \_\_\_\_\_

Meriwether County Board of Commissioners

(Name of Owner)

17234 Roosevelt Highway Building B

(Address of Owner)

hereinafter called OWNER, in the penal sum of \_\_\_\_\_

Dollars, \$(\_\_\_\_\_)

in lawful money of the United States, for their payment of which sum well and truly to be made, we bind ourselves, successors, and assigns, jointly and severally, firmly by these presents.

THE CONDITION OF THIS OBLIGATION is such that whereas, the Principal entered into a certain contract with the OWNER, dated the \_\_\_\_\_ day of \_\_\_\_\_,

20\_\_\_\_, a copy of which is hereto attached and made a part hereof for the construction of:

\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

NOW, THEREFORE, if the Principal shall well, truly and faithfully perform its duties, all the undertakings, covenants, terms, conditions, and agreements of said contract during the original term thereof, and any extensions thereof which may be granted by the OWNER, with or without notice to the Surety and during the one year guaranty period, and if he shall satisfy all claims and demands incurred under such contract, and shall fully indemnify and save harmless the OWNER from all costs and damages which it may suffer by reason of failure to do so, and shall reimburse and repay the OWNER all outlay and expense which the OWNER may incur in making good any default, then this obligation shall be void; otherwise to remain in full force and effect.

PROVIDED, FURTHER, that the said surety, for value received hereby stipulates and agrees that no change, extension of time, alteration or addition to the terms of the contract or to WORK to be performed thereunder or the SPECIFICATIONS accompanying the same shall in any wise affect its obligation on this BOND, and it does hereby waive notice of any such change, extension of time, alteration or addition to the terms of the contract or to the WORK or to the SPECIFICATIONS.

PROVIDED, FURTHER, that no final settlement between the OWNER and the CONTRACTOR shall abridge the right of any beneficiary hereunder, whose claim may be unsatisfied.

In WITNESS WHEREOF, this instrument is executed in \_\_\_\_\_ counterparts, each one of which shall be deemed an original, this the \_\_\_\_\_ day of \_\_\_\_\_ 20\_\_\_\_.

ATTEST:

\_\_\_\_\_  
(Principal) Secretary

(SEAL)

\_\_\_\_\_  
(Witness as to Principal)

\_\_\_\_\_  
(Address)

ATTEST:

\_\_\_\_\_

(Surety) Secretary

(SEAL)

\_\_\_\_\_  
Witness as to Surety

\_\_\_\_\_  
(Address)

NOTE: Date of BOND must not be prior to date of CONTRACT. If CONTRACTOR is Partnership, all partners should execute BOND.

IMPORTANT: Surety companies executing BONDS must appear on the Treasury Department's most current list (Circular 570 as amended) and be authorized to transact business in the state where the PROJECT is located.

\_\_\_\_\_  
Principal

By \_\_\_\_\_

\_\_\_\_\_  
(Address)

\_\_\_\_\_  
Surety

By \_\_\_\_\_  
Attorney-in-Fact

\_\_\_\_\_  
(Address)

## NOTICE OF AWARD

To: \_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_  
\_\_\_\_\_

PROJECT Description: 2026 Meriwether County LMIG Project

The OWNER has considered the BID submitted by you for the above-described WORK in response to its Advertisement for Bids dated\_\_\_\_\_, 2026, and Information for Bidders.

You are hereby notified that your BID has been accepted for items in the amount of \$\_\_\_\_\_.

You are required by the Information for Bidders to execute the Agreement within ten (10) calendar days from the date of this Notice to you.

If you fail to execute said Agreement within ten (10) days from the date of this Notice, said OWNER will be entitled to consider all your rights arising out of the OWNER'S acceptance of your BID as abandoned. The OWNER will be entitled to such other rights as may be granted by law.

You are required to return an acknowledgment copy of this NOTICE OF AWARD to the OWNER.

Dated this\_\_\_\_\_ day of\_\_\_\_\_, 2026.

\_\_\_\_\_  
By \_\_\_\_\_

Title \_\_\_\_\_

## ACCEPTANCE OF NOTICE

Receipt of the above NOTICE OF AWARD is hereby acknowledged.

By: \_\_\_\_\_

this the\_\_\_\_\_ day of\_\_\_\_\_, 20\_\_\_\_\_

By: \_\_\_\_\_

Title \_\_\_\_\_

## NOTICE TO PROCEED

To: \_\_\_\_\_ Date: \_\_\_\_\_

Project: 2025 Meriwether County LMIG Resurfacing Project

You are hereby notified to commence WORK in accordance with the Agreement dated \_\_\_\_\_, 2026, on or before \_\_\_\_\_, 2026, and you are to complete the WORK within 180 consecutive calendar days thereafter. The date of completion of all WORK is \_\_\_\_\_, therefore \_\_\_\_\_, 2026.

Meriwether County Board of Commissioners

By John Gorton

Title County Administrator

## ACCEPTANCE OF NOTICE

Receipt of the above NOTICE TO PROCEED

is hereby acknowledged by \_\_\_\_\_

this the \_\_\_\_\_ day of \_\_\_\_\_, 2026

Company \_\_\_\_\_

Signature \_\_\_\_\_

Title \_\_\_\_\_

# **GENERAL CONDITIONS**

1. Definitions
2. Additional Instructions & Detail Drawings
3. Schedules, Reports & Records
4. Drawings & Specifications
5. Shop Drawings
6. Materials, Services & Facilities
7. Inspection & Testing
8. Substitutions
9. Patents
10. Surveys, Permits, Regulations
11. Protection of Work, Property, Persons
12. Supervision by Contractor
13. Changes in the Work
14. Changes in Contract Price
15. Time for Completion & Liquidated Damages
16. Correction of Work
17. Subsurface Conditions
18. Suspension of Work, Termination and Delay
19. Payments to Contractor
20. Acceptance of Final Payment as Release
21. Insurance
22. Contract Security
23. Assignments
24. Indemnification
25. Separate Contracts
26. Subcontracting
27. Engineer's Authority
28. Land and Rights-of -Way
29. Guarantee
30. Arbitration
31. Taxes

1. DEFINITIONS

1.1 Wherever used in the CONTRACT DOCUMENTS, the following terms shall have the meanings indicated which shall be applicable to both the singular and plural thereof:

1.2 ADDENDA- Written or graphic instruments issued prior to the execution of the Agreement which modify or interpret the CONTRACT DOCUMENTS. DRAWINGS and SPECIFICATIONS, by additions, deletions, clarifications or corrections.

1.3 BID- The offer or proposal or the BIDDER submitted on the prescribed form setting forth the prices for the WORK to be performed.

1.4 BIDDER- Any person, firm or corporation submitted on the prescribed form setting forth the prices for the WORK to be performed.

1.5 BONDS- Bid, Performance, and Payment Bonds and other instruments of security, furnished by the CONTRACTOR and his surety in accordance with the CONTRACT DOCUMENTS.

1.6 CHANGE ORDER- A written order to the CONTRACTOR authorizing an addition, deletion or revision in the WORK within the general scope of the CONTRACT DOCUMENTS, or authorizing an adjustment in the CONTRACT PRICE or CONTRACT TIME.

1.7 CONTRACT DOCUMENTS- The contract, including Advertisement for Bids, Information for Bidders, BID, Bid Bond, Agreement, Payment Bond, Performance Bond, NOTICE OF AWARD, NOTICE TO PROCEED, CHANGE ORDER, DRAWINGS, SPECIFICATIONS & ADDENDA.

1.8 CONTRACT PRICE- The total monies payable to the CONTRACTOR under the terms and conditions of the CONTRACT DOCUMENTS.

1.9 CONTRACT TIME- The number of calendar days stated in the CONTRACT DOCUMENTS for the completion of the WORK.

1.10 CONTRACTOR- The person, firm or corporation with whom the OWNER has executed the Agreement.

1.11 DRAWINGS- The part of the CONTRACT DOCUMENTS which show the characteristics and scope of the WORK to be performed and which have been prepared or approved by the ENGINEER.

1.12 ENGINEER- The person, firm or corporation named as such in the CONTRACT DOCUMENTS.

1.13 FIELD ORDER- A written order effecting a change in the WORK not involving an adjustment in the CONTRACT PRICE or an extension of the CONTRACT TIME, issued by the ENGINEER to the CONTRACTOR during construction.

1.14 NOTICE OF AWARD- The written notice of the acceptance of the BID from the OWNER to the successful BIDDER.

1.15 NOTICE TO PROCEED- Written communication issued by the OWNER to the CONTRACTOR authorizing him to proceed with the WORK and establishing the date of commencement of the WORK.

1.16 OWNER- A public or quasi-public body or authority, corporation, association, partnership, or individual for whom the WORK is to be performed.

1.17 PROJECT- The undertaking to be performed as provided in the CONTRACT DOCUMENTS.

1.18 RESIDENT PROJECT REPRESENTATIVE- The authorized representative of the OWNER who is assigned to the PROJECT site or any part thereof.

1.19 SHOP DRAWINGS- All drawings, diagrams, illustrations, brochures, schedules and other data which are prepared by the CONTRACTOR, a SUBCONTRACTOR, manufacturer, or SUPPLIER or distributor, which illustrate how specific portions or the WORK shall be fabricated or installed.

1.20 SPECIFICATIONS- A part of the CONTRACT DOCUMENTS consisting of written descriptions of a technical nature of materials, equipment, construction systems, standards and workmanship.

1.21 SUBCONTRACTOR- An individual, firm or corporation having a direct contract with the CONTRACTOR or with any

other SUBCONTRACTOR for the performance of a part of the WORK at the site.

1.22 SUBSTANTIAL COMPLETION- That date as certified by the ENGINEER when the construction of the Project or a specified part thereof is sufficiently completed, in accordance with the CONTRACT DOCUMENTS so that the PROJECT or specified part can be utilized for the purpose for which it is intended.

1.23 SUPPLEMENTAL GENERAL CONDITIONS- Modifications to General Conditions required by a Federal agency for participation in the PROJECT and approved by the agency in writing prior to inclusion in the CONTRACT DOCUMENTS, or such requirements that may be imposed by applicable state laws.

1.24 SUPPLIER- Any person or organization who supplies materials or equipment for the WORK, including that fabricated to a special design, but who does not perform labor at the site.

1.25 WORK- All labor necessary to produce the construction required by the CONTRACT DOCUMENTS and all materials and equipment incorporated or to be incorporated in the PROJECT.

1.26 WRITTEN NOTICE- Any notice to any party of the Agreement relative to any part of this Agreement in writing and considered delivered and the service thereof completed, when posted by certified or registered mail to the said party at his last given address, or delivered in person to said party or his authorized representative on the WORK.

## 2. ADDITIONAL INSTRUCTIONS AND DETAIL DRAWINGS

2.1 The CONTRACTOR may be furnished additional instructions and detail drawings by the ENGINEER as necessary to carry out the WORK required by the CONTRACT DOCUMENTS.

2.2 The additional drawings and instructions thus supplied will become a part of the CONTRACT DOCUMENTS. The CONTRACTOR shall carry out the WORK in accordance with the additional detail drawings and instructions.

## 3. SCHEDULES, REPORTS AND RECORDS

3.1 The CONTRACTOR shall submit to the OWNER such schedule of quantities and costs progress schedules, payrolls, reports, estimates, records and other data where applicable as are required by the CONTRACT DOCUMENTS for the WORK performed.

3.2 Prior to the first partial payment estimate the CONTRACTOR shall submit construction progress schedules showing the order in which he proposes to carry on the WORK, estimated date of completion of each part and as applicable:

3.2.1 The dates at which special detail drawings will be required.

3.2.2 Respective dates for submission of SHOP DRAWINGS, the beginning of manufacture, the testing and the installation of materials, supplies and equipment.

3.3 The CONTRACTOR shall also submit a schedule of payments that he anticipates he will earn during the course of the WORK.

## 4. DRAWINGS AND SPECIFICATIONS

4.1 The intent of the DRAWINGS and SPECIFICATIONS is that the CONTRACTOR shall furnish all labor, materials, tools, equipment, and transportation necessary for the proper execution of the WORK in accordance with the CONTRACT DOCUMENTS and all incidental work necessary to complete the PROJECT in an acceptable manner, ready for use, occupancy or operation by the OWNER.

4.2 In case of conflict between the DRAWINGS and SPECIFICATIONS, the SPECIFICATIONS shall govern. Figure dimensions on DRAWINGS shall govern over scale dimensions, and detailed DRAWINGS shall govern over general DRAWINGS.

4.3 Any discrepancies found between the DRAWINGS and SPECIFICATIONS and site conditions or any inconsistencies or ambiguities in the DRAWINGS or SPECIFICATIONS shall be immediately reported to the ENGINEER, in writing, who shall promptly correct such inconsistencies or ambiguities in writing. WORK done by the CONTRACTOR after his discovery of such discrepancies, inconsistencies or ambiguities shall be done at the CONTRACTOR'S risk.

## 5. SHOP DRAWINGS

5.1 The CONTRACTOR shall provide SHOP DRAWINGS as may be necessary for the prosecution of the WORK as required by the CONTRACT DOCUMENTS. The ENGINEER shall promptly review all SHOP DRAWINGS. The ENGINEER'S approval of any SHOP DRAWING shall not release the CONTRACTOR from responsibility for deviations from the CONTRACT DOCUMENTS. The approval of any SHOP DRAWING which substantially deviates from the requirement of the CONTRACT DOCUMENTS shall be evidenced by a CHANGE ORDER.

5.2 When submitted for the ENGINEER'S review, SHOP DRAWINGS shall bear the CONTRACTOR'S certification that he has reviewed, checked and approved the SHOP DRAWINGS and that they are in conformance with the requirements of the CONTRACT DOCUMENTS.

5.3 Portions of the WORK requiring a SHOP DRAWING or sample submission shall not begin until the SHOP DRAWING or submission has been approved by the ENGINEER. A copy of each approved SHOP DRAWING and each approved sample shall be kept in good order by the CONTRACTOR at the site and shall be available to the ENGINEER.

## 6. MATERIALS, SERVICES AND FACILITIES

6.1 It is understood that except as otherwise specifically stated in the CONTRACT DOCUMENTS, the CONTRACTOR shall provide and pay for all materials, labor, tools, equipment, water, light, power, transportation, supervision, temporary construction of any nature whatsoever necessary to execute, complete, and deliver the WORK within the specified time.

6.2 Materials and equipment shall be so stored as to insure the preservation of their quality and fitness for the WORK. Stored materials and equipment to be incorporated in the WORK shall be located so as to facilitate prompt inspection.

6.3 Manufactured articles, materials and equipment shall be applied, installed, connected, erected, used, cleaned and conditioned as directed by the manufacturer.

6.4 Materials, supplies or equipment to be incorporated into the WORK shall not be purchased by the CONTRACTOR or the SUBCONTRACTOR subject to a chattel mortgage or under a conditional sale contract or other agreement by which an interest is retained by the seller.

## 7 INSPECTION AND TESTING

7.1 All materials and equipment used in the construction of the PROJECT shall be subject to adequate inspection and testing in accordance with generally accepted standards, as required and defined in the CONTRACT DOCUMENTS.

7.2 The OWNER shall provide all inspection and testing services not required by the CONTRACTOR DOCUMENTS.

7.3 The CONTRACTOR shall provide at his expense the testing and inspection services required by the CONTRACT DOCUMENTS.

7.4 If the CONTRACT DOCUMENTS, laws, ordinances, rules, regulations or orders of any public authority having jurisdiction require any WORK to specifically be inspected, tested, or approved by someone other than the CONTRACTOR, the CONTRACTOR will give the ENGINEER timely notice of readiness. The CONTRACTOR will then furnish the ENGINEER the required certificates of inspection, testing or approval.

7.5 Inspection, tests or approvals by the engineer or others shall not relieve the CONTRACTOR from his obligations to perform the WORK in accordance with the requirements of the CONTRACT DOCUMENTS.

7.6 The ENGINEER and his representatives will at all times have access to the WORK. In addition, authorized representatives and agents of any participating Federal or state agency shall be permitted to inspect all work, materials, payrolls, records of personnel, invoices of materials, and other relevant data and records. The CONTRACTOR will provide proper facilities for such access and observation of the WORK and also for any inspection, or testing thereof.

7.7 If any WORK is covered contrary to the written instructions of the ENGINEER it must, if requested by the ENGINEER, be uncovered for his observation and replaced at the CONTRACTOR'S expense.

7.8 In the ENGINEER considers it necessary or advisable that covered WORK be inspected or tested by others, the CONTRACTOR, at the ENGINEER'S request, will uncover, expose or otherwise make available for observation, inspection or testing as the ENGINEER may require, that portion of the WORK in question, furnishing all necessary labor, materials, tools, and equipment. If it is found that such WORK is defective, the CONTRACTOR will bear all the expenses of such uncovering, exposure, observation, inspection and testing and of satisfactory reconstruction. If, however, such WORK is not found to be defective, the CONTRACTOR will be allowed an increase in the CONTRACT PRICE or an extension of the CONTRACT TIME, or both, directly attributable to such uncovering, exposure, observation, inspection, testing and reconstruction and an appropriate CHANGE ORDER shall be issued.

## 8 SUBSTITUTIONS

8.1 Whenever a material, article or piece of equipment is identified on the DRAWINGS or SPECIFICATIONS by reference to brand name or catalogue number, it shall be understood that this is referenced for the purpose of defining the performance or other salient requirements of equal capacities, quality and function shall be considered. The CONTRACTOR may recommend the substitution of a material, article, or piece of equipment of equal substance and function to that specified, the ENGINEER may approve its substitution and use by the CONTRACTOR. If the CONTRACTOR wishes to substitute any specific item, that item is subject to review and approval by the ENGINEER, and must be submitted for review at least 7 days before BID DATE, or may be subject to denial by ENGINEER. Any cost differential shall be deductible from the CONTRACT PRICE and the CONTRACT DOCUMENTS shall be appropriately modified by CHANGE ORDER. The CONTRACTOR warrants that if substitutes are approved, no major changes in the function or general design of the PROJECT will result. Incidental changes or extra component parts required to accommodate the substitute will be made by the CONTRACTOR without a change in the CONTRACT PRICE, or CONTRACT TIME.

## 9 PATENTS

9.1 The CONTRACTOR shall pay all applicable royalties and license fees. He shall defend all suits of claims for infringement of any patent rights and save the OWNER harmless from loss on account thereof, except that the OWNER shall be responsible for any such loss when a particular process, design, or the product of a particular manufacturer or manufacturers is specified, however if the CONTRACTOR has reason to believe that the design process or product specified is an infringement of a patent, he shall be responsible for such loss unless he promptly gives such information to the ENGINEER.

## 10 SURVEYS, PERMITS, REGULATIONS

10.1 The OWNER shall furnish all boundary surveys and establish all base lines for locating the principal component parts of the WORK together with a suitable number of

benchmarks adjacent to the WORK as shown in the CONTRACT DOCUMENTS. From the information provided by the OWNER, unless otherwise specified in the CONTRACT DOCUMENTS, the CONTRACTOR shall develop and make all detail surveys needed for construction such as slope stakes, batter boards, stakes for pile locations and other working points, lines, elevations and cut sheets.

10.2 The CONTRACTOR shall carefully preserve bench marks, reference points and stakes and in case of willful or careless destruction, he shall be charged with the resulting expense and shall be responsible for any mistakes that may be caused by their unnecessary loss or disturbance.

10.3 Permits and licenses of a temporary nature necessary for the prosecution of the WORK shall be secured and paid for by the CONTRACTOR unless otherwise stated in the SUPPLEMENTAL GENERAL CONDITIONS. Permits, licenses and easements for permanent structures or permanent changes in existing facilities shall be secured and paid for by the OWNER, unless otherwise specified. The CONTRACTOR shall give all notices and comply with all laws, ordinances, rules and regulations bearing on the conduct of the WORK as drawn and specified. If the CONTRACTOR observes that the CONTRACT DOCUMENTS are at variance therewith, he shall promptly notify the ENGINEER in writing, and any necessary changes shall be adjusted as provided in Section 13, CHANGES IN THE WORK.

## 11 PROTECTION OF WORK, PROPERTY AND PERSONS

11.1 The CONTRACTOR will be responsible for initiating, maintaining and supervising all safety precautions and programs in connection with the WORK. He will take all necessary precautions for the safety of, and will provide the necessary protection to prevent damage, injury or loss to all employees on the WORK and other persons who may be affected thereby, all the WORK and all materials or equipment to be incorporated therein, whether in storage on or off the site, and other property at the site or adjacent thereto, including trees, shrubs, lawns, walks, pavements, roadways, structures and utilities not designated for removal, relocation or replacement in the course of construction.

11.2 The CONTRACTOR will comply with all applicable laws, ordinances, rules, regulations and orders of any public body having jurisdiction. He will erect and maintain, as required by the conditions and progress of the WORK all necessary safeguards for safety and protection. He will notify owners of adjacent utilities when prosecution of the WORK may affect them. The CONTRACTOR will remedy all damage, injury or loss to any property caused directly or indirectly, in whole or in part, by the CONTRACTOR, any SUBCONTRACTOR or anyone directly or indirectly employed by any of them or anyone for whose acts any of the be liable, except damage or loss attributable to the fault of the CONTRACT DOCUMENTS or to the acts or omissions of the OWNER or the ENGINEER or anyone employed by either of them or anyone for whose acts either of them may be liable, and not attributable, directly or indirectly, in whole or in part to the fault or negligence of the CONTRACTOR.

11.3 In emergencies affecting the safety of persons or the WORK or property at the site or adjacent thereto, the CONTRACTOR without special instruction or authorization from the ENGINEER or OWNER, shall act to prevent threatened damage, injury or loss. He will give the ENGINEER prompt WRITTEN NOTICE of any significant changes in the WORK or deviations from the CONTRACT DOCUMENTS caused thereby, and a CHANGE ORDER shall thereupon be issued covering the changes and deviations involved.

## 12 SUPERVISION BY CONTRACTOR

12.1 The CONTRACTOR will supervise and direct the WORK. He will be solely responsible for the means, methods, techniques, sequences and procedures of construction. The CONTRACTOR will employ and maintain on the WORK a qualified supervisor or superintendent who shall have been designated in writing by the CONTRACTOR as the CONTRACTOR'S representative at the site. The supervisor shall have full authority to act on behalf of the CONTRACTOR and all communications given to the supervisor shall be as binding as if given to the CONTRACTOR. The supervisor shall be present on the site at all times as required to perform adequate supervision and coordination of the WORK.

## 13 CHANGES IN THE WORK

13.1 The OWNER may at any time, as the need arises, order changes within the scope of the WORK without invalidating the Agreement. If such changes increase or decrease the amount due under the CONTRACT DOCUMENTS, or in the time required for performance of the WORK, an equitable adjustment shall be authorized by the CHANGE ORDER.

13.2 The ENGINEER, also, may at any time, by issuing a FIELD ORDER, make changes in the details of the WORK. The CONTRACTOR shall proceed with the performance of any changes in the WORK so ordered by the ENGINEER, unless the CONTRACTOR believes that such FIELD ORDER entitles him to a change in CONTRACT PRICE or TIME, or both, in which event he shall give the ENGINEER WRITTEN NOTICE thereof within seven (7) days after the receipt of the ordered change. Thereafter the CONTRACTOR shall document the basis for the change in CONTRACT PRICE or TIME within thirty (30) days. The CONTRACTOR shall not execute such changes pending the receipt of an executed CHANGE ORDER or further instruction from the OWNER.

## 14 CHANGES IN CONTRACT PRICE

14.1 The CONTRACT PRICE may be changed only by a CHANGE ORDER. The value of any WORK covered by a CHANGE ORDER or of any claim for increase or decrease in the CONTRACT PRICE shall be determined by one or more of the following methods in the order or precedence listed below:

- (a) Unit prices previously approved.
- (b) An agreed lump sum.
- (c) The actual cost for labor, direct overhead, materials, supplies, equipment, and other services necessary to complete the work. In addition, there shall be added an amount to be agreed upon but not to exceed fifteen (15) percent of the actual

cost of the WORK to cover the cost of general overhead and profit.

## 15 TIME FOR COMPLETION AND LIQUIDATED DAMAGES

15.1 The date of beginning and the time for completion of the WORK are essential conditions of the CONTRACT DOCUMENTS and the WORK embraced shall be commenced on a date specified in the NOTICE TO PROCEED.

15.2 The CONTRACTOR will proceed with the WORK at such rate of progress to insure full completion within the CONTRACT TIME. It is expressly understood and agreed, by and between the CONTRACTOR and the OWNER, the CONTRACT TIME for the completion of the WORK described herein is a reasonable time, taking into consideration the average climatic and economic conditions and other factors prevailing in the locality of the WORK.

15.3 If the CONTRACTOR shall fail to complete the WORK within the CONTRACT TIME, or extension of time granted by the OWNER, then the CONTRACTOR will pay to the OWNER, the amount for liquidated damages as specified in the BID for each calendar day that the CONTRACTOR shall be in default after the time stipulated in the CONTRACT DOCUMENTS.

15.4 The CONTRACTOR shall not be charged with liquidated damages or any excess cost when the delay in completion of the WORK is due to the following, and the CONTRACTOR has promptly given WRITTEN NOTICE of such delay to the OWNER or ENGINEER.

15.4.1 To any preference, priority, or allocation order duly issued by the OWNER.

15.4.2 To unforeseeable causes beyond the control and without the fault or negligence of the CONTRACTOR, including but not restricted to acts of God, or of the public enemy, acts of the OWNER, acts of another CONTRACTOR in the performance of a contract with the OWNER, fires, floods, epidemics, quarantine restrictions, strikes, freight, embargoes, and abnormal and unforeseeable weather; and

15.4.3 To any delays of SUBCONTRACTORS occasioned by any of the causes specified in paragraphs 15.4.1 and 15.4.2 of this article.

## 16. CORRECTION OF WORK

16.1 The CONTRACTOR shall promptly remove from the premises all WORK rejected by the ENGINEER for failure to comply with the CONTRACT DOCUMENTS, whether incorporated in the construction or not, and the CONTRACTOR shall promptly replace and reexecute the WORK in accordance with the CONTRACT DOCUMENTS and without expense to the OWNER and shall bear the expense of making good all WORK of other CONTRACTORS destroyed or damaged by such removal or replacement.

16.2 All removal and replacement WORK shall be done at the CONTRACTOR'S expense. If the CONTRACTOR does not take action to remove such rejected WORK within ten (10) days after receipt of WRITTEN NOTICE, the OWNER may remove such WORK and store the materials at the expense of the CONTRACTOR.

## 17. SUBSURFACE CONDITIONS

17.1 The CONTRACTOR shall promptly, and before such conditions are disturbed, except in the event of an emergency, notify the OWNER by WRITTEN NOTICE of:

17.1.1 Subsurface or latent physical conditions at the site differing materially from those indicated in the CONTRACT DOCUMENTS: or

17.1.2 Unknown physical conditions at the site, of an unusual nature, differing materially from those ordinarily encountered and generally recognized as inherent in WORK of the character provided for in the CONTRACT DOCUMENTS.

17.2 The OWNER shall promptly investigate the conditions, and if he finds that such conditions do so materially differ and cause an increase or decrease in the cost of, or in the time required for, performance of the WORK, an equitable adjustment shall be made and the CONTRACT DOCUMENTS shall be modified by a CHANGE ORDER. Any claim of the CONTRACTOR for adjustment hereunder shall not be allowed unless he has given the required WRITTEN NOTICE; provided that the OWNER may, if he determines the facts so justify, consider and adjust any such claims asserted before the date of final payment.

## 18. SUSPENSION OF WORK, TERMINATION AND DELAY

18.1 The OWNER may suspend the WORK or any portion thereof for a period of not more than ninety days or such further time as agreed upon by the CONTRACTOR, by WRITTEN NOTICE to the CONTRACTOR and the ENGINEER which notice shall fix the date on which WORK shall be resumed. The CONTRACTOR will resume that WORK on the date so fixed. The CONTRACTOR will be allowed an increase in the CONTRACT PRICE or an extension of the CONTRACT TIME, or both, directly attributable to any suspension.

18.2 If the CONTRACTOR is adjudged a bankrupt or insolvent, or if he makes a general assignment for the benefit of his creditors, or if a trustee or receiver is appointed for the CONTRACTOR or for any of his property, or if he files a petition to take advantage of any debtor's act, or to reorganize under the bankruptcy or applicable laws, or if he repeatedly fails to supply sufficient skilled workmen or suitable materials or equipment, or if he repeatedly fails to make prompt payments to SUBCONTRACTORS or for labor, materials or equipment or if he disregards laws, ordinances, rules, regulations or orders of any public body having jurisdiction of the WORK or if he disregards the authority of the ENGINEER, or if he otherwise violates any provision of the CONTRACT DOCUMENTS, then the OWNER may, without prejudice to any other right or remedy and after giving the CONTRACTOR and his surety a minimum of ten (10) days from delivery of a WRITTEN NOTICE, terminate the services of the CONTRACTOR and take possession of the PROJECT and of all materials, equipment, tools, construction equipment and machinery thereon owned by the CONTRACTOR, and finish the WORK by whatever method he may deem expedient. In such case the CONTRACTOR shall not be entitled to receive any further payment until the WORK is finished. If the unpaid balance of

the CONTRACT PRICE exceeds the direct and indirect costs of completing the PROJECT, including compensation for additional professional services, such excess SHALL BE PAID TO THE CONTRACTOR. If such costs exceed such unpaid balance, the CONTRACTOR will pay the difference to the OWNER. Such costs incurred by the OWNER will be determined by the ENGINEER and incorporated in a CHANGE ORDER.

18.3 Where the CONTRACTOR'S services have been so terminated by the OWNER, said termination shall not affect any right of the OWNER against the CONTRACTOR then existing or which may thereafter accrue. Any retention or payment of monies by the OWNER due the CONTRACTOR will not release the CONTRACTOR from compliance with the CONTRACT DOCUMENTS.

18.4 After ten (10) days from delivery of a WRITTEN NOTICE to the CONTRACTOR and the ENGINEER, the OWNER may, without cause and without prejudice to any other right or remedy, elect to abandon the PROJECT and terminate the Contract. In such case, the CONTRACTOR shall be paid for all WORK executed and any expense sustained plus reasonable profit.

18.5 If, through no act or fault of the CONTRACTOR, the WORK is suspended for a period of more than ninety (90) days by the OWNER or under an order of court or other public authority, or the ENGINEER fails to act on any request for payment within thirty (30) days after it is submitted, or the OWNER fails to pay the CONTRACTOR substantially the sum approved by the ENGINEER or awarded by arbitrators within thirty (30) days of its approval and presentation, then the CONTRACTOR may, after ten (10) days from delivery of a WRITTEN NOTICE to the OWNER and the ENGINEER, terminate the CONTRACT and recover from the OWNER payment for all WORK executed and all expenses sustained. In addition and in lieu of terminating the CONTRACT, if the ENGINEER has failed to act on a request for payment or if the OWNER has failed to make any payment as aforesaid, the CONTRACTOR may upon ten (10) days written notice to the OWNER and the ENGINEER stop the WORK until he has been paid all amounts then due, in which event and upon resumption of the WORK, CHANGE ORDERS shall be issued for adjusting the CONTRACT PRICE or extending the CONTRACT TIME or both to compensate for the costs and delays attributable to the stoppage of the WORK.

18.6 If the performance of all or any portion of the WORK is suspended, delayed, or interrupted as a result of a failure of the OWNER or ENGINEER to act within the time specified in the CONTRACT DOCUMENTS, or if no time is specified, within reasonable time, an adjustment in the CONTRACT PRICE or an extension of the CONTRACT TIME, or both, shall be made by CHANGE ORDER to compensate the CONTRACTOR for the costs and delays necessarily caused by the failure of the OWNER or ENGINEER.

## 19. PAYMENTS TO CONTRACTOR

19.1 At least ten (10) days before each progress payment falls due (but not more often than once a month), the CONTRACTOR will submit to the ENGINEER a partial

payment estimate filled out and signed by the CONTRACTOR covering the WORK performed during the period covered by the partial payment estimate and supported by such data as the ENGINEER may reasonably require. If payment is requested on the basis of materials and equipment not incorporated in the WORK but delivered and suitably stored at or near the site, the partial payment estimate shall also be accompanied by such supporting data, satisfactory to the OWNER, as will establish the OWNER'S title to the material and equipment and protect his interest therein, including applicable insurance.

The ENGINEER will, within ten (10) days after receipt of each partial payment estimate, either indicate in writing his approval of payment and present the partial payment estimate to the CONTRACTOR indicating in writing his reasons for refusing to approve payment. In the latter case, the CONTRACTOR may make the necessary corrections and resubmit the partial payment estimate.

The OWNER shall retain five (5) percent of the amount of each payment until final completion and acceptance of all work covered by the CONTRACT DOCUMENTS. On completion and acceptance of a part of the WORK on which the price is stated separately in the CONTRACT DOCUMENTS, payment may be made in full, including retained percentages, less authorized deductions.

19.2 The request for payment may also include an allowance for the cost of such major materials and equipment, which are suitably stored either at or near the site.

19.3 Prior to SUBSTANTIAL COMPLETION, the OWNER, with the approval of the ENGINEER and with the concurrence of the CONTRACTOR, may use any completed or substantially completed portions of the WORK. Such use shall not constitute an acceptance of such portions of all WORK.

19.4 The OWNER shall have the right to enter the premises for the purpose of doing work not covered by the CONTRACT DOCUMENTS. This provision shall not be construed as relieving the CONTRACTOR of the sole responsibility for the care and protection of the WORK, or the restoration of any damaged WORK except such as may be caused by agents or employees of the OWNER.

19.5 Upon completion and acceptance of the WORK, the ENGINEER shall issue a certificate attached to the final payment request that the WORK has been accepted by him under the conditions of the CONTRACT DOCUMENTS. The entire balance found to be due the CONTRACTOR, including the retained percentages, but except such sums as may be lawfully retained by the OWNER, shall be paid to the CONTRACTOR within thirty (30) days of completion and acceptance of the WORK.

19.6 The CONTRACTOR will indemnify and save the OWNER or the OWNER'S agents harmless from all claims growing out of the lawful demands of SUBCONTRACTORS, laborers, workmen, mechanics, material, men, and furnishers of machinery and parts thereof, equipment, tools, and all supplies,

incurred in the furtherance of the performance of the WORK. The CONTRACTOR shall, at the OWNER'S request, furnish satisfactory evidence that all obligations of the nature designated above have been paid, discharged, or waived. If the CONTRACTOR fails to do so the OWNER may, after having notified the CONTRACTOR, either pay unpaid bills or withhold from the CONTRACTOR'S unpaid compensation a sum of money deemed reasonably sufficient to pay any and all such lawful claims until satisfactory evidence is furnished that all liabilities have been fully discharged whereupon payment to the CONTRACTOR shall be resumed, in accordance with the terms of the CONTRACT DOCUMENTS, but in no event shall the provisions of this sentence be construed to impose any obligations upon the OWNER to either the CONTRACTOR, his Surety, or any third party. In paying any unpaid bills of the CONTRACTOR, any payment so made by the OWNER shall be considered as payment made under the CONTRACT DOCUMENTS by the OWNER to the CONTRACTOR and the OWNER shall not be liable to the CONTRACTOR for any such payments made in good faith.

19.7 If the OWNER fails to make payment thirty (30) days after approval by the ENGINEER, in addition to other remedies available to the CONTRACTOR, there shall be added to each payment interest at the maximum legal rate commencing on the first day after said payment is due and continuing until the payment is received by the CONTRACTOR.

## 20. ACCEPTANCE OF FINAL PAYMENT AS RELEASE

20.1 The acceptance by the CONTRACTOR of final payment shall be and shall operated as a release to the OWNER of all claims and all liability to the CONTRACTOR other than claims in stated amounts as may be specifically excepted by the CONTRACTOR for all things done or furnished in connection with this WORK and for every act and neglect of the OWNER and others relating to or arising out of this WORK. Any payment, however, final or otherwise, shall not release the CONTRACTOR or his sureties from any obligations under the CONTRACT DOCUMENTS or the Performance BOND and Payment BONDS.

## 21. INSURANCE

21.1 INSURANCE: Contractor shall maintain the following insurance (a) comprehensive general liability, including blanket contractual, covering bodily injuries with limits of no less than \$1,000,000 per occurrence, and property damage with limits of no less than \$1,000,000 per occurrence; and (b) commercial automobile liability, including blanket contractual, covering bodily injuries with limits of no less than \$1,000,000 per occurrence, and property damage with limits of no less than \$1,000,000 per accident (c) statutory worker's compensation insurance, including \$1,000,000 employer's liability insurance (d) employee dishonesty and/or crimes coverage with respect to personnel of Contractor having access to County buildings, with limits of no less than \$50,000 per occurrence. All insurance shall be provided by an insurer(s) acceptable to the County, and shall provide for thirty (30) days prior notice of cancellation to the County. Upon request, Contractor shall deliver to the County a certificate or policy of insurance evidencing Contractor's compliance with this paragraph. Contractor shall abide by all terms and conditions of the insurance and shall do nothing to impair or invalidate the coverage.

21.2 Certificates of Insurance acceptable to the OWNER shall be filed with the OWNER prior to commencement of the WORK. These Certificates shall contain a provision that coverages afforded under the policies will not be canceled unless at least fifteen (15) days prior WRITTEN NOTICE has been given to the OWNER.

21.3 The CONTRACTOR shall procure and maintain, at his own expense, during the CONTRACT TIME, liability insurance as previously specified.

21.3.2 the CONTRACTOR shall acquire and maintain, if applicable, Fire and Extended Coverage insurance upon the PROJECT to the full insurable value thereof for the benefit of the OWNER, the CONTRACTOR, and SUBCONTRACTORS as their interest may appear. This provision shall in no way release the CONTRACTOR or CONTRACTOR'S surety from obligations under the CONTRACT DOCUMENTS to fully complete the PROJECT.

21.4 The CONTRACTOR shall procure and maintain, at his own expense, during the CONTRACT TIME, in accordance with the provisions of the laws of the state in which the work is performed, Workmen's Compensation Insurance, including occupational disease provisions, for all of his employees at the site of the PROJECT and in case any work is sublet, the CONTRACTOR shall require such SUBCONTRACTOR similarly to provide Workmen's Compensation Insurance, including occupational disease provisions for all of the latter's employees unless such employees are covered by the protection afforded by the CONTRACTOR. In case any class of employees engaged in hazardous work under this contract at the site of the PROJECT is not protected under Workmen's Compensation statute, the CONTRACTOR shall provide, and shall cause each SUBCONTRACTOR to provide, adequate and suitable insurance for the protection of his employees not otherwise protected.

21.5 The CONTRACTOR shall secure, if applicable, "All Risk" type Builder's Risk Insurance for WORK to be performed. Unless specifically authorized by the OWNER, the amount of such insurance shall not be less than the CONTRACT PRICE totaled in the BID. The policy shall cover not less than the losses due to fire, explosion, hail, lightning, vandalism, malicious mischief, wind, collapse, riot, aircraft, and smoke during the CONTRACT TIME, and until the WORK is accepted by the OWNER. The policy shall name as the insured the CONTRACTOR, the ENGINEER, and the OWNER.

## 22. CONTRACT SECURITY

22.1 The CONTRACTOR shall within ten (10) days after the receipt of the NOTICE OF AWARD furnish the OWNER with a Performance Bond and a Payment Bond in penal sums equal to the amount of the CONTRACT PRICE, conditioned upon the performance by the CONTRACTOR of all undertakings, covenants, terms, conditions, and agreements of the CONTRACT DOCUMENTS, and upon the prompt payment by the CONTRACTOR to all persons supplying labor and materials in the prosecution of the WORK provided by the CONTRACT DOCUMENTS. Such BONDS shall be executed by the CONTRACTOR and a corporate bonding company licensed to

transact such business in the state in which the WORK is to be performed and named on the current list of "Surety Companies Acceptable on Federal Bonds" as published in the Treasury Department Circular Number 570. The expense of these BONDS shall be borne by the CONTRACTOR. If at any time a surety on any such BOND is declared a bankrupt or loses its right to do business in the state in which the WORK is to be performed or is removed from the list of Surety Companies accepted on Federal BONDS, CONTRACTOR shall within ten (10) days after notice from the OWNER to do so, substitute an acceptable BOND (or BONDS) in such form and sum and signed by such other surety or sureties as may be satisfactory to the OWNER. The premiums on such BOND shall be paid by the CONTRACTOR. No further payments shall be deemed due nor shall be made until the new surety or sureties shall have furnished an acceptable BOND to the OWNER.

### 23. ASSIGNMENTS

23.1 Neither the CONTRACTOR nor the OWNER shall sell, transfer, assign or otherwise dispose of the Contract or any portion thereof, or of his right, title or interest therein, of his obligations hereunder, without written consent of the other party.

### 24. INDEMNIFICATION

24.1 The CONTRACTOR will indemnify and hold harmless the OWNER and the ENGINEER and their agents and employees from and against all claims, damages, losses and expenses including attorney's fees arising out of or resulting from the performance of the WORK, provided that any such claims, damage, loss or expense is attributable to bodily injury, sickness, disease or death, or to injury to or destruction of tangible property including the loss of use resulting there from: and is caused in whole or in part by any negligent or willful act or omission of the CONTRACTOR, and SUBCONTRACTOR, anyone directly or indirectly employed by any of them or anyone for whose acts any of them may be liable.

24.2 In any and all claims against the OWNER or the ENGINEER, or any of their agents or employees, by any employee of the CONTRACTOR, any SUBCONTRACTOR, anyone directly or indirectly employed by any of them, or anyone for whose acts any of them may be liable, the indemnification obligation shall not be limited in any way by any limitation on the amount or type of damages, compensation or benefits payable by or for the CONTRACTOR or any SUBCONTRACTOR under workmen's compensation acts, disability benefit acts or other employee benefits acts.

24.3 The obligation of the CONTRACTOR under this paragraph shall not extend to the liability of the ENGINEER, his agents or employees arising out of the preparation or approval of maps, DRAWINGS, opinions, reports, surveys, CHANGE ORDERS, designs or SPECIFICATIONS.

### 25. SEPARATE CONTRACTS

25.1 The OWNER reserves the right to let other contracts in connection with this PROJECT. The CONTRACTOR shall afford other CONTRACTORS reasonable opportunity for the introduction and storage of their materials and the execution of their WORK, and shall properly connect and coordinate his

WORK with theirs. If the proper execution or results of any part of the CONTRACTOR'S WORK depends upon the WORK of any other CONTRACTOR, the CONTRACTOR shall inspect and promptly report to the ENGINEER any defects in such WORK that render it unsuitable for such proper execution and results.

25.2 The OWNER may perform additional WORK related to the PROJECT by himself, or he may let other contracts containing provisions similar to these. The CONTRACTOR will afford the other CONTRACTORS who are parties to such Contracts (or the OWNER, if he is performing the additional WORK himself), reasonable opportunity for the introduction and storage of materials and equipment and the execution of WORK, and shall properly connect and coordinate his WORK with theirs.

25.3 If the performance of additional WORK by other CONTRACTORS or the OWNER is not noted in the CONTRACT DOCUMENTS prior to the execution of the CONTRACT, written notice thereof shall be given to the CONTRACTOR prior to starting any such additional WORK. If the CONTRACTOR believes that the performance of such additional WORK by the OWNER or others involves him in additional expense or entitles him to an extension of the CONTRACT TIME, he may make a claim therefore as provided in Sections 14 and 15.

### 26. SUBCONTRACTING

26.1 The CONTRACTOR may utilize the services of specialty SUBCONTRACTORS on those parts of the WORK which, under normal contracting practices, are performed by specialty SUBCONTRACTORS.

26.2 The CONTRACTOR shall not award WORK to SUBCONTRACTOR(s), in excess of fifty (50%) percent of the CONTRACT PRICE, without prior written approval of the OWNER.

26.3 The CONTRACTOR shall be fully responsible to the OWNER for the acts and omissions of his SUBCONTRACTORS, and of persons either directly or indirectly employed by them, as he is for the acts and omissions of persons directly employed by him.

26.4 The CONTRACTOR shall cause appropriate provisions to be inserted in all subcontracts relative to the WORK to bind SUBCONTRACTORS to the CONTRACTOR by the terms of the CONTRACT DOCUMENTS insofar as applicable to the WORK of SUBCONTRACTORS and to give the CONTRACTOR the same power as regards terminating any subcontract that the OWNER may exercise over the CONTRACTOR under any provision of the CONTRACT DOCUMENTS.

26.5 Nothing contained in this CONTRACT shall create any contractual relation between any SUBCONTRACTOR and the OWNER.

### 27. ENGINEER'S AUTHORITY

27.1 The ENGINEER shall act as the OWNER'S representative during the construction period. He shall decide questions,

which may arise as to quality and acceptability of materials furnished and WORK performed. He shall interpret the intent of the CONTRACT DOCUMENTS in a fair and unbiased manner. The ENGINEER will make visits to the site and determine if the WORK is proceeding in accordance with the CONTRACT DOCUMENTS.

27.2 The CONTRACTOR will be held strictly to the intent of the CONTRACT DOCUMENTS in regard to the quality of materials, workmanship and execution of the WORK. Inspections may be made at the factory or fabrication plant of the source of material supply.

27.3 The ENGINEER will not be responsible for the construction means, controls, techniques, sequences, procedures, or construction safety.

27.4 The ENGINEER shall promptly make decisions relative to interpretation of the CONTRACT DOCUMENTS.

## 28. LAND AND RIGHTS-OF-WAY

28.1 Prior to issuance of NOTICE TO PROCEED, the OWNER shall obtain all land and rights-of-way necessary for carrying out and for the completion of the WORK to be performed pursuant to the CONTRACT DOCUMENTS, unless otherwise mutually agreed.

28.2 The OWNER shall provide to the CONTRACTOR information, which delineates and describes the lands owned and rights-of-way acquired.

28.3 The CONTRACTOR shall provide at his own expense and without liability to the OWNER any additional land and access thereto that the CONTRACTOR may desire for temporary construction facilities, or for storage of materials.

## 29. GUARANTY

29.1 The CONTRACTOR shall guarantee all materials and equipment furnished and WORK performed for a period of one (1) year from the date of SUBSTANTIAL COMPLETION. The CONTRACTOR warrants and guarantees for a period of one (1) year from the date of SUBSTANTIAL COMPLETION of the system that the completed system is free from all defects due to faulty materials or workmanship and the CONTRACTOR shall promptly make such corrections as may be necessary by reason of such defects including the repairs of any damage to other parts of the system resulting from such defects. The OWNER will give notice of observed defects with reasonable promptness. In the event that the CONTRACTOR should fail to make such repairs, adjustments, or other WORK that may be made necessary by such defects, the OWNER may do so and charge the CONTRACTOR the cost thereby incurred. The Performance BOND shall remain in full force and effect through the guarantee period.

## 30. ARBITRATION

30.1 All claims, disputes and other matters in question arising out of, or relating to, the CONTRACT DOCUMENTS or the breach thereof, except for claims which have been waived by the making and acceptance of final payment as provided by Section 20, shall be decided by arbitration in accordance with the

Construction Industry Arbitration Rules of the American Arbitration Association. This agreement to arbitrate shall be specifically enforceable under the prevailing arbitration law. The award rendered by the arbitrators shall be final, and judgment may be entered upon it in any court having jurisdiction thereof.

30.2 Notice of the demand for arbitration shall be filed in writing with the other party to the CONTRACT DOCUMENTS and with the American Arbitration Association, and a copy shall be filed with the ENGINEER. Demand for arbitration shall in no event be made on any claim, dispute or other matter in question, which would be barred by the applicable statute of limitations.

30.3 The CONTRACTOR will carry on the WORK and maintain the progress schedule during any arbitration proceedings, unless otherwise mutually agreed in writing.

## 31. TAXES

31.1 The CONTRACTOR will pay all sales, consumer, use and other similar taxes required by the law of the place where the WORK is performed.

## **DRAWINGS:**

### **MERIWETHER COUNTY 2026 LMIG ROADWAY IMPROVEMENT PLANS**

2026 RESURFACING AND STRIPING PROJECT PHASE II  
MERIWETHER COUNTY, GEORGIA  
MAY 2026

EMC PROJECT NO. 26-7011

MERIWETHER COUNTY BOARD OF COMMISSIONERS

GENE KING  
JENNIFER SNELSON  
EMMETT COLLINS  
BRYAN THREADGILL  
ADAM WORSLEY

COMMISSIONER DISTRICT 1  
COMMISSIONER DISTRICT 2  
COMMISSIONER DISTRICT 3 - CHAIRMAN  
COMMISSIONER DISTRICT 4  
COMMISSIONER DISTRICT 5

JOHN GORTON

COUNTY ADMINISTRATOR

OWNER/DEVELOPER

MERIWETHER COUNTY BOARD OF COMMISSIONERS  
17234 ROOSEVELT HIGHWAY, BUILDING B  
GREENVILLE, GA 30222



MERIWETHER COUNTY  
GEORGIA



| Sheet List Table |                   |
|------------------|-------------------|
| Sheet Number     | Sheet Title       |
| 1                | COVER             |
| 2                | KEY MAP           |
| 3                | GENERAL NOTES     |
| 4                | DETAILS           |
| 5                | ALVATON ROAD (1)  |
| 6                | ALVATON ROAD (2)  |
| 7                | ALVATON ROAD (3)  |
| 8                | ALVATON ROAD (4)  |
| 9                | ALVATON ROAD (5)  |
| 10               | ALVATON ROAD (6)  |
| 11               | ALVATON ROAD (11) |
| 12               | ALVATON ROAD (12) |
| 13               | ALVATON ROAD (13) |



EMC ENGINEERING SERVICES, INC.  
3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 565-5985  
Fax: (706) 565-5983  
columbus@emc-eng.com  
www.emc-eng.com

C:\2026\26-7011 MERIWETHER COUNTY - 2026 MERIWETHER LMG ROADS\DWG\26-7011C-B01(PHASE II).DWG 6/8/2026 10:13 AM



NOTE:

1. ALL PAVEMENT SURFACES SHALL BE CLEAN OF DEBRIS PRIOR TO RE-STRIPING.
2. STRIPING SHALL CONFORM TO GDOT AND MUTCD CURRENT EDITION, STANDARDS.
3. ALL STRIPING SHALL TERMINATE AT THE NEAREST TANGENT SECTION OUTSIDE THE RADIUS OF THE INTERSECTING ROADS.
4. ALL STOP BARS SHALL BE RE-STRIPED.
5. ALL STRIPING SHALL MATCH THE CURRENT STRIPING PATTERN.
6. BLUE RAISED PAVEMENT MARKERS SHALL BE INSTALLED ALONG THE CENTERLINE OF ROADWAY, PERPENDICULAR TO ANY FIRE HYDRANTS.
7. IF EXISTING ROAD HAS RAISED PAVEMENT MARKINGS (RPMS), THEN NEW RPMS MUST BE INSTALLED.
8. CONTRACTOR SHALL SUBMIT TEMPORARY TRAFFIC CONTROL PLANS TO ENGINEER FOR APPROVAL, PRIOR TO BEGINNING WORK.
9. BACKFILL SHOULDERS ON BOTH SIDES OF THE ROAD, SCARIFY EXISTING SHOULDER AND ADD ADDITIONAL MATERIAL AS REQUIRED. GRADE, COMPACT AND ESTABLISH PERMANENT GRASS. REPAIR WASHES AS REQUIRED UNTIL STAND OF GRASS IS ACHIEVED.
10. PROVIDE TEMPORARY STRIPING OR TEMPORARY MARKING TAPE UNTIL HIGH BUILD PAINT CAN BE INSTALLED AFTER 28 DAY CURE.


| NAME                  | MILEAGE |
|-----------------------|---------|
| ROADS FOR RESURFACING | 3.5     |
| ALVATON ROAD          | 3.5     |

KEY MAP

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA  
Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS

EMC ENGINEERING SERVICES, INC.



CIVIL  
MARINE  
ENVIRONMENTAL  
3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 565-9583  
columbus@emc-eng.com  
www.emc-eng.com

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

| NO. | REVISION DESCRIPTION | DATE |
|-----|----------------------|------|
| -   | -                    | -    |
| -   | -                    | -    |
| -   | -                    | -    |
| -   | -                    | -    |
| -   | -                    | -    |
| -   | -                    | -    |
| -   | -                    | -    |

|              |           |
|--------------|-----------|
| PROJECT NO.: | 26-7011   |
| DRAWN BY:    | TRM       |
| DESIGNED BY: | TRM       |
| SURVEYED BY: |           |
| SURVEY DATE: |           |
| CHECKED BY:  | CEB       |
| SCALE:       | NTS       |
| DATE:        | 5/29/2026 |

C:\2026\26-7011 MERWETHER COUNTY - 2026 MERWETHER LMG ROADS\DWG\26-7011C-B01(PHASE I).DWG 6/8/2026 10:13 AM

|                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                          |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                         |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                             |                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                      |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div>PROJECT DESCRIPTION:</div> <div><div><div>1. THE CLIENT'S INTENT IS TO RESURFACE AND STRIPE THE LISTED ROADS.</div><div>2. ENGINEER OF RECORD:<br/>CHRISTOPHER E. BRAZELL, PE, PLS<br/>EMC ENGINEERING SERVICES INC.<br/>3575 MACON ROAD SUITE 15<br/>COLUMBUS, GA 31907<br/>PHONE: (706) 368-0140<br/>CHRIS_BRAZELL@emc-eng.com</div></div><div>GENERAL NOTES:</div><div><div>1. THE CONTRACTOR SHALL BE RESPONSIBLE FOR SITE SAFETY AND ALL WAYS, MEANS, AND METHODS OF CONSTRUCTION.</div><div>2. THE SAFE AND ORDERLY PASSAGE OF TRAFFIC AND PEDESTRIANS SHALL BE PROVIDED WHERE CONSTRUCTION OPERATIONS ABUT PUBLIC THROUGHFARES AND ADJACENT PROPERTY.</div><div>3. THE CONTRACTOR WILL COORDINATE THE WORK WITH THE UTILITY COMPANIES AND WILL VERIFY ALL EXISTING PIPE INVERTS AND EXISTING ROAD ELEVATIONS PRIOR TO CONSTRUCTION.</div><div>4. IT WILL BE THE RESPONSIBILITY OF THE CONTRACTOR TO INSURE THAT ALL REQUIRED PERMITS ARE OBTAINED AND IN HAND PRIOR TO THE COMMENCEMENT OF CONSTRUCTION.</div><div>5. THE DATA, TOGETHER WITH ALL OTHER INFORMATION SHOWN ON THESE PLANS, OR IN ANY WAY INDICATED THEREBY, WHETHER BY DRAWINGS OR NOTES, OR IN ANY OTHER MANNER, ARE BASED UPON FIELD INVESTIGATIONS AND ARE BELIEVED TO BE INDICATIVE OF ACTUAL CONDITIONS, HOWEVER, THE SAME ARE SHOWN AS INFORMATION ONLY, ARE NOT GUARANTEED AND DO NOT BIND THE ENGINEER IN ANY WAY.</div><div>6. UNDERGROUND UTILITY INFORMATION SHOWN HEREON IS BASED ON GROUND MARKINGS BY OTHERS. NO CERTIFICATION IS MADE AS TO THE ACCURACY OR COMPLETENESS OF THIS INFORMATION. VISIBLE EVIDENCE OF UTILITY STRUCTURES OBSERVED DURING THE COURSE OF THE FIELD SURVEY IS SHOWN HEREON.</div><div>7. PRIOR TO INSTALLATION OF ANY UTILITY LINES, THE CONTRACTOR SHALL GIVE THE UTILITY COMPANIES THREE (3) WORKING DAYS NOTICE TO ALLOW TIME FOR EXISTING UTILITIES TO BE STAKED. BEFORE CALLING (811) THE CONTRACTOR SHALL HAVE THE FOLLOWING INFORMATION READY: COUNTY, TOWN, LOCATION, NEAREST STREET INTERSECTIONS, TYPE OF WORK (SEWER, WATER, PAVING, ETC.) YOUR COMPANY NAME, TELEPHONE NUMBER, OWNER'S NAME, DATE AND TIME YOU EXPECT TO COMMENCE CONSTRUCTION, AND WHERE AND HOW YOU CAN BE REACHED AND THE BEST TIME TO CONTACT YOU. THE CONTRACTOR SHALL EXERCISE CAUTION WHEN WORKING IN THE AREA OF AN UNDERGROUND UTILITY WHETHER OR NOT SHOWN ON THE PLAN OR LOCATED BY THE UTILITY COMPANY. THE CONTRACTOR SHALL NOTIFY ENGINEER PRIOR TO COMMENCEMENT OF WORK OR PURCHASING ANY MATERIALS OF ANY UTILITY DISCREPANCIES OR EXISTING UTILITY INSTALLATIONS THAT NEED RELOCATION. THE CONTRACTOR SHALL COOPERATE WITH THE RESPECTIVE UTILITY COMPANIES TO RELOCATE ALL UTILITIES WHICH INTERFERE WITH THE PROPOSED CONSTRUCTION.</div><div>8. IT IS THE OBLIGATION OF THE CONTRACTOR TO MAKE HIS OWN INTERPRETATION OF ALL SURFACE AND SUBSURFACE DATA THAT IS AVAILABLE AS TO THE NATURE AND EXTENT OF THE MATERIALS TO BE EXCAVATED AND WASTED, AND/OR GRADED AND COMPACTED. THE INFORMATION SHOWN ON THESE PLANS AND SPECIFICATIONS DOES NOT IN ANY WAY GUARANTEE THE AMOUNT OR NATURE OF THE MATERIAL WHICH MAY BE ENCOUNTERED.</div><div>9. IT IS EXTREMELY IMPORTANT FOR THE CONTRACTOR TO VISIT THE SITE PRIOR TO BEGINNING CONSTRUCTION IN ORDER TO VERIFY THE EXISTING CONDITIONS AS SHOWN ON THE PLANS BEFORE AGREEING TO PERFORM ANY WORK. DISCREPANCIES BETWEEN CONDITIONS SHOWN ON THE PLANS AND ACTUAL CONDITIONS ON SITE MUST BE REPORTED TO EMC ENGINEERING SERVICES, INC. IN A WRITTEN REPORT. FAILURE OF THE CONTRACTOR TO SUBMIT A REPORT TO EMC ENGINEERING SERVICES, INC. OF THE DISCREPANCIES BETWEEN CONDITIONS SHOWN ON THE PLANS AND ACTUAL CONDITIONS ON SITE SHALL BE INTERPRETED AS THE CONTRACTOR HAVING ACCEPTED SUCH CONDITIONS. THEREFORE, ANY COSTS FOR ADJUSTMENTS OR CHANGES IN THE WORK RESULTING FROM ERRORS IN THE LOCATIONS OR DIMENSIONS OF EXISTING OR PROPOSED FEATURES AFTER COMMENCING WORK SHALL BE THE SOLE RESPONSIBILITY OF THE CONTRACTOR AT NO ADDITIONAL COST TO THE OWNER OR ENGINEER.</div><div>10. THE CONTRACTOR SHALL FURNISH EMC ENGINEERING SERVICES, INC. WITH EVERY REASONABLE FACILITY FOR ASCERTAINING WHETHER OR NOT THE WORK PERFORMED AND THE PRODUCTS USED ARE IN ACCORDANCE WITH THE INTENT AND REQUIREMENTS OF THE SPECIFICATIONS AND THE CONTRACT DOCUMENTS AS WELL AS FEDERAL, STATE, AND LOCAL CODES AND SPECIFICATIONS.</div><div>11. INSPECTIONS OF THE ONGOING WORK SHALL NOT RELIEVE THE CONTRACTOR OF ANY OBLIGATION TO FULFILL THIS CONTRACT. DEFECTIVE WORK SHALL BE MADE GOOD REGARDLESS OF WHETHER SUCH WORK HAS BEEN PREVIOUSLY INSPECTED AND ACCEPTED OR APPROVED FOR PAYMENT. THE FAILURE OF EMC ENGINEERING SERVICES, INC. OR ANY OTHER AUTHORIZED INSPECTOR TO REJECT IMPROPER WORK SHALL NOT BE CONSIDERED A WAIVER OF ANY RESPONSIBILITY FOR ANY DEFECT WHICH MAY BE DISCOVERED LATER, OR FOR ANY DEFECTIVE WORK AND THE CONTRACTOR'S RESPONSIBILITY TO MAKE IT GOOD SO AS TO COMPLY WITH CONTRACT DOCUMENTS AND FEDERAL, STATE AND LOCAL CODES.</div><div>12. ALL DISTURBED AREAS, NOT DESIGNATED TO BE PAVED, SHALL BE GRASSED WITH PERMANENT SEEDING OR PLANTED WITH PERMANENT VEGETATION, EXCEPT WHERE PROPOSED CONSTRUCTION INDICATES OTHERWISE.</div><div>13. THE CONTRACTOR IS RESPONSIBLE FOR THE LOCATION AND FURNISHING OF BORROW MATERIAL AS NECESSARY FOR THE CONSTRUCTION OF THIS PROJECT. FILL MATERIAL SHALL BE CLEAN AND FREE OF ALL DEBRIS AND ORGANIC MATERIAL.</div><div>14. ALL ITEMS REMOVED FROM THE PROJECT WHICH ARE NOT TO BE REUSED SHALL BE MOVED TO A LOCATION APPROVED BY THE OWNER.</div><div>15. ALL STRIPING AND SIGNS SHALL BE IN CONFORMITY WITH THE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES FOR STREETS AND HIGHWAYS, LATEST EDITION.</div><div>16. ANY SURVEY MARKER OR MONUMENTS DISTURBED DURING CONSTRUCTION REQUIRES RE-ESTABLISHMENT BY A SURVEYOR LICENSED IN THE STATE THE PROJECT RESIDES IN AT THE CONTRACTOR'S EXPENSE.</div><div>17. ANY INFORMATION BY THE GOVERNING AGENCY, INCLUDING BUT NOT LIMITED TO STANDARDS, REQUIREMENTS, SPECIFICATIONS, NOTES, AND DETAILS, SHALL SUPERCEDE IF THERE IS ANY CONFLICTING INFORMATION HEREIN.</div><div>18. IF ANY CONFLICTS, DISCREPANCIES, OR OTHER UNSATISFACTORY CONDITIONS ARE DISCOVERED, EITHER ON THE CONSTRUCTION DOCUMENTS OR THE FIELD CONDITIONS, THE CONTRACTOR MUST NOTIFY THE ENGINEER IMMEDIATELY IN WRITING, AND SHALL NOT COMMENCE OPERATION UNTIL CONFLICTS, DISCREPANCIES, OR OTHER UNSATISFACTORY CONDITIONS ARE RESOLVED.</div></div></div> | <div>SITE LAYOUT AND STAKING NOTES</div> <div><div>1. THE CONTRACTOR SHALL PROVIDE THREE WORKING DAYS NOTICE TO THE UTILITIES PROTECTION CENTER BY CALLING 811 IN ORDER TO LOCATE UTILITIES PRIOR TO STARTING ANY EXCAVATION OR CONSTRUCTION.</div><div>2. THE SIZES AND/OR LOCATIONS OF UNDERGROUND UTILITIES, IF NOTED ON THE DRAWINGS, ARE BASED ON INFORMATION AVAILABLE. NO EXCAVATIONS WERE MADE TO LOCATE OR IDENTIFY BURIED UTILITIES OR STRUCTURES, AS SUCH LOCATIONS OF UNDERGROUND UTILITIES AND STRUCTURES ARE FOR INFORMATIONAL PURPOSES ONLY AND MAY VARY FROM LOCATIONS SHOWN ON THE DRAWINGS. NO CERTIFICATION IS MADE AS TO THE ACCURACY OR COMPLETENESS OF THIS INFORMATION. CONTRACTOR SHALL DETERMINE THE ACTUAL LOCATION AND DEPTH OF ALL EXISTING UTILITIES PRIOR TO STARTING ANY WORK THAT MAY CAUSE DAMAGE TO UTILITIES.</div><div>3. CONTRACTOR SHALL BE RESPONSIBLE FOR DAMAGE TO ANY UTILITY LINE OR STRUCTURE ENCOUNTERED, WHETHER OR NOT SHOWN ON THE DRAWINGS AND/OR LOCATED IN THE FIELD. CONTRACTOR SHALL BE RESPONSIBLE FOR REPAIRING ANY UTILITIES DAMAGED DURING DEMOLITION AND/OR CONSTRUCTION AT NO ADDITIONAL COST TO THE OWNER.</div><div>4. THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS AND EXISTING CONDITIONS PRIOR TO STARTING WORK AND SHALL BE RESPONSIBLE FOR THE PROPER FIT OF ALL COMPONENTS. SOME DIMENSIONS AND CONDITIONS MAY VARY. NOTIFY ENGINEER IN WRITING OF ANY DISCREPANCIES OR CONFLICTS.</div><div>5. CONTRACTOR SHALL BE RESPONSIBLE FOR VERIFICATION OF ALL SETBACKS, EASEMENTS, BUFFERS, ETC. PRIOR TO COMMENCEMENT OF CONSTRUCTION.</div><div>6. CONTRACTOR SHALL CAREFULLY EXAMINE ALL DOCUMENTS AND THE CONSTRUCTION SITE TO OBTAIN FIRST HAND KNOWLEDGE OF EXISTING CONDITIONS.</div><div>7. ALL DIMENSIONS ARE MEASURED TO BACK OF CURB WHERE CURB &amp; GUTTER IS PRESENT. ALL OTHER DIMENSIONS ARE MEASURED TO EDGE OF PAVEMENT UNLESS NOTED OTHERWISE. CONTRACTOR IS TO COORDINATE WITH THE ARCHITECTURAL PLANS AS TO THE BUILDING LAYOUT AND DIMENSIONS.</div><div>8. ALL NEW ASPHALT AND/OR CONCRETE PAVING SHALL HAVE A SMOOTH TRANSITION TO EXISTING PAVEMENT.</div><div>9. ALL SIGNS AND UTILITY MARKERS REMOVED/DISTURBED DURING CONSTRUCTION SHALL BE REINSTALLED UNLESS NOTED OTHERWISE ON PLANS.</div><div>10. ALL HANDICAP ACCESSIBLE SITE IMPROVEMENTS INCLUDING HANDICAP PARKING SPACES AND ACCESSIBLE ROUTES SHALL CONFORM WITH THE AMERICANS WITH DISABILITY ACT DESIGN GUIDELINES AND SPECIFICATIONS, LATEST EDITION, AND ANY ADDITIONAL FEDERAL, STATE, AND LOCAL CODES, REQUIREMENTS, AND REGULATIONS.</div><div>11. ALL PARKING STRIPING SHALL BE 5" PAINTED WHITE UNLESS NOTED OTHERWISE. ALL PAINT TO BE WATERBORNE TRAFFIC PAINT THAT IS ENVIRONMENTALLY FRIENDLY.</div><div>12. ALL STRIPING AND SIGNS SHALL CONFORM WITH THE STATE'S DEPARTMENT OF TRANSPORTATION AND THE MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (MUTCD), LATEST EDITION.</div><div>13. AT THE END OF EACH DAY'S WORK, REMOVE/RELOCATE ANY DEBRIS AND/OR CONSTRUCTION MATERIALS THAT IS NOT WITHIN THE CONTRACTOR CONSTRUCTION LIMITS.</div><div>14. ALL PROPOSED AND EXISTING PAVEMENT AND CURB TO REMAIN SHALL BE PROTECTED. IF DAMAGED, IT SHALL BE REPLACED PROMPTLY TO MEET STATE AND LOCAL REQUIREMENTS AT THE CONTRACTOR'S EXPENSE.</div><div>15. CONTRACTOR IS REQUIRED TO NOTIFY ENGINEER IN WRITING OF ANY DISCREPANCIES OR CONFLICTS ENCOUNTERED DURING CONSTRUCTION ACTIVITIES.</div></div> | <div>GRADING AND DRAINAGE NOTES</div> <div><div>1. THE CONTRACTOR SHALL PROVIDE THREE WORKING DAYS NOTICE TO THE UTILITIES PROTECTION CENTER BY CALLING 811 IN ORDER TO LOCATE UTILITIES PRIOR TO STARTING ANY EXCAVATION OR CONSTRUCTION.</div><div>2. THE SIZES AND/OR LOCATIONS OF UNDERGROUND UTILITIES, IF NOTED ON THE DRAWINGS, ARE BASED ON INFORMATION AVAILABLE. NO EXCAVATIONS WERE MADE TO LOCATE OR IDENTIFY BURIED UTILITIES OR STRUCTURES, AS SUCH LOCATIONS OF UNDERGROUND UTILITIES AND STRUCTURES ARE FOR INFORMATIONAL PURPOSES ONLY AND MAY VARY FROM LOCATIONS SHOWN ON THE DRAWINGS. NO CERTIFICATION IS MADE AS TO THE ACCURACY OR COMPLETENESS OF THIS INFORMATION. CONTRACTOR SHALL DETERMINE THE ACTUAL LOCATION AND DEPTH OF ALL EXISTING UTILITIES PRIOR TO STARTING ANY WORK THAT MAY CAUSE DAMAGE TO UTILITIES.</div><div>3. CONTRACTOR SHALL BE RESPONSIBLE FOR DAMAGE TO ANY UTILITY LINE OR STRUCTURE ENCOUNTERED, WHETHER OR NOT SHOWN ON THE DRAWINGS AND/OR LOCATED IN THE FIELD. CONTRACTOR SHALL BE RESPONSIBLE FOR REPAIRING ANY UTILITIES DAMAGED DURING DEMOLITION AND/OR CONSTRUCTION AT NO ADDITIONAL COST TO THE OWNER.</div><div>4. THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS AND EXISTING CONDITIONS PRIOR TO STARTING WORK AND SHALL BE RESPONSIBLE FOR THE PROPER FIT OF ALL COMPONENTS. SOME DIMENSIONS AND CONDITIONS MAY VARY. NOTIFY ENGINEER IN WRITING OF ANY DISCREPANCIES OR CONFLICTS.</div><div>5. ALL SUITABLE FILL MATERIAL SHALL BE PLACED IN LIFTS NOT TO EXCEED 8 INCHES &amp; COMPACTED TO 95% OF MAX. DRY DENSITY OF STANDARD PROCTOR.</div><div>6. FILL MATERIAL SHALL BE CLEAN AND FREE OF ALL DEBRIS AND ORGANIC MATERIAL.</div><div>7. CONTRACTOR TO FILL AND/OR EXCAVATE AS REQUIRED FOR INSTALLATION OF ALL PROPOSED FEATURES. FINAL GRADES SHALL BE FLUSH WITH EDGE OF ASPHALT, SIDEWALK, AND/OR BACK OF CURB AND GRADED TO ENSURE POSITIVE DRAINAGE. PONDING OF STORMWATER SHALL NOT OCCUR.</div><div>8. ADJUST ALL TOP OF STRUCTURES ELEVATIONS (MANHOLES, CLEANOUTS, VALVE BOXES, ETC.) TO FINISH GRADE ELEVATIONS. FAILURE TO NOTE SUCH WORK SHALL NOT BE THE BASIS FOR CONTRACT MODIFICATIONS OR ADDITIONS.</div><div>9. ALL PROPOSED AND EXISTING PAVEMENT AND CURB TO REMAIN SHALL BE PROTECTED. IF DAMAGED, IT SHALL BE REPLACED PROMPTLY TO MEET STATE AND LOCAL REQUIREMENTS AT THE CONTRACTOR'S EXPENSE.</div><div>10. CARE SHALL BE TAKEN NEAR EXISTING TREES, SHRUBS, AND OTHER VEGETATION WHICH ARE TO REMAIN SO AS TO NOT CAUSE INJURY TO ROOT SYSTEMS OR TRUNKS.</div><div>11. AT THE END OF EACH DAY'S WORK, REMOVE ANY DEBRIS, MATERIAL, ETC. (RESULTING FROM CONTRACTOR'S GRADING OPERATIONS) THAT IS NOT WITHIN THE CONTRACTOR CONSTRUCTION LIMITS.</div><div>12. ALL DISTURBED AREAS OF THE SITE SHALL BE DRESSED TO UNIFORM, WELL DRAINED AND VISUALLY APPEALING SURFACE WITH A MINIMUM TOPSOIL LAYER OF FOUR INCHES.</div><div>13. IT SHALL BE THE CONTRACTOR'S RESPONSIBILITY TO ENSURE THE SITE IS ADA ACCESSIBLE AS REQUIRED BY FEDERAL, STATE AND LOCAL GOVERNMENT.</div><div>14. FINISH GRADE ELEVATIONS INDICATE EDGE OF PAVEMENT/TOP OF PAVEMENT UNLESS OTHERWISE NOTED.</div><div>15. REFER TO DETAILS FOR PAVEMENT TYPICAL SECTION.</div><div>16. SITE SHALL BE GRADED UNIFORMLY FOR POSITIVE DRAINAGE AS SHOWN FROM THE PROPOSED ELEVATIONS, CONTOURS, AND THE DRAINAGE SLOPE ARROWS.</div><div>17. MAXIMUM SIDEWALK CROSS SLOPE IS 2%. MAXIMUM LONGITUDINAL SLOPE ALONG AN ACCESSIBLE SIDEWALK IS 5%. MAXIMUM PAVEMENT SLOPE IN HANDICAP PARKING AREA AND ACCESS AISLE IS 2% IN ANY DIRECTION. MAXIMUM HANDICAP RAMP SLOPE IS 1:2H:1V.</div><div>18. CONTRACTOR IS REQUIRED TO NOTIFY ENGINEER IN WRITING OF ANY DISCREPANCIES OR CONFLICTS ENCOUNTERED DURING CONSTRUCTION ACTIVITIES.</div></div> | <div>DEMOLITION AND EXISTING CONDITIONS NOTES</div> <div><div>1. THE CONTRACTOR SHALL PROVIDE THREE WORKING DAYS NOTICE TO THE UTILITIES PROTECTION CENTER BY CALLING 811 IN ORDER TO LOCATE UTILITIES PRIOR TO STARTING ANY EXCAVATION OR CONSTRUCTION.</div><div>2. THE SIZES AND/OR LOCATIONS OF UNDERGROUND UTILITIES, IF NOTED ON THE DRAWINGS, ARE BASED ON INFORMATION AVAILABLE. NO EXCAVATIONS WERE MADE TO LOCATE OR IDENTIFY BURIED UTILITIES OR STRUCTURES, AS SUCH LOCATIONS OF UNDERGROUND UTILITIES AND STRUCTURES ARE FOR INFORMATIONAL PURPOSES ONLY AND MAY VARY FROM LOCATIONS SHOWN ON THE DRAWINGS. NO CERTIFICATION IS MADE AS TO THE ACCURACY OR COMPLETENESS OF THIS INFORMATION. CONTRACTOR SHALL DETERMINE THE ACTUAL LOCATION AND DEPTH OF ALL EXISTING UTILITIES PRIOR TO STARTING ANY WORK THAT MAY CAUSE DAMAGE TO UTILITIES.</div><div>3. CONTRACTOR SHALL BE RESPONSIBLE FOR DAMAGE TO ANY UTILITY LINE OR STRUCTURE ENCOUNTERED, WHETHER OR NOT SHOWN ON THE DRAWINGS AND/OR LOCATED IN THE FIELD. CONTRACTOR SHALL BE RESPONSIBLE FOR REPAIRING ANY UTILITIES DAMAGED DURING DEMOLITION AND/OR CONSTRUCTION AT NO ADDITIONAL COST TO THE OWNER.</div><div>4. THE CONTRACTOR SHALL VERIFY ALL DIMENSIONS AND EXISTING CONDITIONS PRIOR TO STARTING WORK AND SHALL BE RESPONSIBLE FOR THE PROPER FIT OF ALL COMPONENTS. SOME DIMENSIONS AND CONDITIONS MAY VARY. NOTIFY ENGINEER IN WRITING OF ANY DISCREPANCIES OR CONFLICTS.</div><div>5. CONTRACTOR SHALL PROVIDE ADEQUATE TEMPORARY BARRIERS &amp; WARNINGS TO LIMIT ACCESS TO PROJECT AREA TO ONLY THOSE PERSONNEL AUTHORIZED BY THE CONTRACTOR. SAFE PASSAGE SHALL BE MAINTAINED FOR PEDESTRIANS TO AREAS ADJACENT TO THE PROJECT SITE AS REQUIRED.</div><div>6. ALL ITEMS REMOVED OR DEMOLISHED BY THE CONTRACTOR, WHICH ARE NOT LISTED BY THE SPECIAL PROVISIONS, OR HEREIN, TO BE TURNED OVER TO THE OWNER, SHALL BECOME THE PROPERTY OF THE CONTRACTOR &amp; SHALL BECOME THE CONTRACTOR'S RESPONSIBILITY FOR PROPER DISPOSAL.</div><div>7. DEMOLITION ACTIVITIES ARE NOT EXPECTED TO INCLUDE THE REMOVAL OF HAZARDOUS MATERIALS. IN THE EVENT THAT THAT HAZARDOUS MATERIALS ARE ENCOUNTERED OR SUSPECTED, CONTRACTOR SHALL NOTIFY ENGINEER IN WRITING OF THE MATERIAL AND LOCATION.</div><div>8. CONTRACTOR SHALL COORDINATE WITH APPROPRIATE UTILITY COMPANIES TO SCHEDULE ALL UTILITY &amp; SERVICE INTERRUPTIONS TO OCCUPIED PORTIONS OF THE SITE.</div><div>9. CONTRACTOR SHALL REMOVE TREES AS INDICATED ON CIVIL PLANS. CONTRACTOR SHALL USE CAUTION DURING ALL CONSTRUCTION ACTIVITIES TO PROTECT ALL TREES, SHRUBS AND OTHER VEGETATION THAT ARE NOT INDICATED TO BE REMOVED. CONTRACTOR SHALL BE RESPONSIBLE FOR ALL SITE CLEAN-UP, CLEARING AND GRUBBING PER SPECIFICATIONS. ALL TREES THAT HAVE A MARKETABLE VALUE SHALL BE SALVAGED. CONTRACTOR SHALL COORDINATE WITH OWNER AS TO THE TREES TO BE RELOCATED OR SOLD.</div><div>10. ALL TREE SAVE AREAS SHALL BE CLEARLY IDENTIFIED WITH TREE PROTECTION FENCING AS INDICATED ON THE CIVIL PLANS PRIOR TO COMMENCEMENT OF ANY LAND DISTURBANCE. NO ABOVE OR BELOW-GROUND DISTURBANCE OF ANY KIND SHALL OCCUR WITHIN THE TREE PROTECTION FENCING, NOR ANY PARKING, STOCK-PILING, BURNING ETC. SEE PLANS FOR TREE PROTECTION FENCING.</div><div>11. REQUIRED DEMOLITION IS NOTED ON PLANS, SECTIONS AND DETAILS. ADDITIONAL DEMOLITION AND REPAIR MAY BE REQUIRED. FAILURE TO NOTE SUCH WORK SHALL NOT BE THE BASIS FOR CONTRACT MODIFICATIONS OR ADDITIONS.</div><div>12. WHERE ASPHALT OR CONCRETE DEMOLITION IS REQUIRED, CONTRACTOR SHALL USE A SAW CUT AT THE LIMITS OF DEMOLITION OR NEAREST JOINT TO OBTAIN A CLEAN EDGE.</div><div>13. AT THE END OF EACH DAY'S WORK, REMOVE ANY DEBRIS (RESULTING FROM CONTRACTOR'S DEMOLITION OPERATIONS) THAT IS NOT WITHIN THE CONTRACTOR CONSTRUCTION LIMITS.</div><div>14. ALL PROPOSED AND EXISTING PAVEMENT AND CURB TO REMAIN SHALL BE PROTECTED. IF DAMAGED, IT SHALL BE REPLACED OR REPAIRED PROMPTLY TO MEET STATE AND LOCAL REQUIREMENTS AT THE CONTRACTOR'S EXPENSE.</div><div>15. CONTRACTOR IS REQUIRED TO NOTIFY ENGINEER IN WRITING OF ANY DISCREPANCIES OR CONFLICTS ENCOUNTERED DURING CONSTRUCTION ACTIVITIES.</div></div> | <div>GENERAL NOTES</div> <div>2026 RESURFACING AND STRIPING PROJECT PHASE II</div> <div>EMC ENGINEERING SERVICES, INC.<br/>3575 Macon Rd., Suite 15<br/>Columbus, GA 31907<br/>Ph: (706) 368-0140<br/>columbus@emc-eng.com<br/>www.emc-eng.com<br/>CIVIL MARINE ENVIRONMENTAL<br/>ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS<br/>GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA</div> <div>PROJECT NO.: 26-7011<br/>DRAWN BY: TRM<br/>DESIGNED BY: TRM<br/>SURVEYED BY: ----<br/>CHECKED BY: CEB<br/>SCALE: NO SCALE<br/>DATE: 5/29/2026</div> <div>SHEET 3</div> <div>OF 13</div> |
|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|



ALVATON ROAD RESURFACING (3.5 MILES; , 24.5 FT WIDE, ASPHALT - 2 MILES WEST OF HWY 85 TO LUTHERSVILLE RD)

**MERIWETHER COUNTY, GEORGIA****MERIWETHER COUNTY BOARD OF COMMISSIONERS**

| NO.                             | ITEM NO. | ITEM DESCRIPTION                                                                                          | QTY  | UNIT | UNIT PRICE | TOTAL |
|---------------------------------|----------|-----------------------------------------------------------------------------------------------------------|------|------|------------|-------|
| 1                               | 150-1000 | TRAFFIC CONTROL                                                                                           | 1    | LS   |            | \$ -  |
| 2                               | 210-1000 | SHOULDER BACKFILLING (BOTH SIDES), GRADE, COMPACT, TEMP & PERM GRASS                                      | 3.5  | ML   |            | \$ -  |
| 3                               | 432-0205 | MILL ASPH CONC PVMT, AT TRANSITIONS & BRIDGES (150 FT ON EACH SIDE)                                       | 1000 | SY   |            | \$ -  |
| 4                               | 402-9901 | RECYCLED ASPHALT CONCRETE PATCHING COURSE (19 MM SP, 440 LBS/ SY MAX) - MISCELLANEOUS AS NECESSARY        | 50   | TN   |            | \$ -  |
| 4                               | 402-1812 | RECYCLED ASPHALT CONCRETE LEVELING COURSE (OGI) INCL BITUM MATERIAL, H LIME, TYPE I (85 LBS/SY)           | 2150 | TN   |            | \$ -  |
| 5                               | 402-3121 | 1.5" RECYCLED ASPHALT CONCRETE WEARING COURSE (12.5 MM TYPE II) INCL BITUM MATERIAL, H LIME, (165 LBS/SY) | 4200 | TN   |            | \$ -  |
| 6                               | 652-2501 | SINGLE WHITE SOLID STRIPE, 5" HIGH BUILD PAINT                                                            | 7    | LM   |            | \$ -  |
| 7                               | 652-2502 | CENTERLINE YELLOW SOLID STRIPE, 5" HIGH BUILD PAINT                                                       | 3.5  | RM   |            | \$ -  |
| 8                               | 413-1000 | BITUMINOUS TACK COAT                                                                                      | 8000 | GL   |            | \$ -  |
| 9                               | 653-1000 | THERMO PLASTIC SOLID TRAFFIC STRIPE, 24 INCH, WHITE                                                       | 3    | EA   |            | \$ -  |
| <b>BASE CONSTRUCTION TOTAL:</b> |          |                                                                                                           |      |      |            | \$ -  |

| NO. | REVISION DESCRIPTION | DATE |
|-----|----------------------|------|
| 1   |                      | 1    |
| 2   |                      | 1    |
| 3   |                      | 1    |
| 4   |                      | 1    |
| 5   |                      | 1    |
| 6   |                      | 1    |
| 7   |                      | 1    |

|  |
|--|
|  |
|--|



EMC ENGINEERING SERVICES, INC.

3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 565-5983  
Fax: (706) 565-5983  
[www.emc-eng.com](http://www.emc-eng.com)


CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUSTIN • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

| DETAILS                                                                                             |  |
|-----------------------------------------------------------------------------------------------------|--|
| 2026 RESURFACING AND STRIPING PROJECT PHASE II                                                      |  |
| <p>MERIWETHER CO., GEORGIA</p> <p>Prepared for:</p> <p>MERIWETHER COUNTY BOARD OF COMMISSIONERS</p> |  |

|              |           |
|--------------|-----------|
| PROJECT NO.: | 26-7011   |
| DRAWN BY:    | TRM       |
| DESIGNED BY: | TRM       |
| SURVEYED BY: |           |
| SURVEY DATE: |           |
| CHECKED BY:  | CEB       |
| SCALE:       | NO SCALE  |
| DATE:        | 5/29/2026 |

SHEET  
4  
OF 13

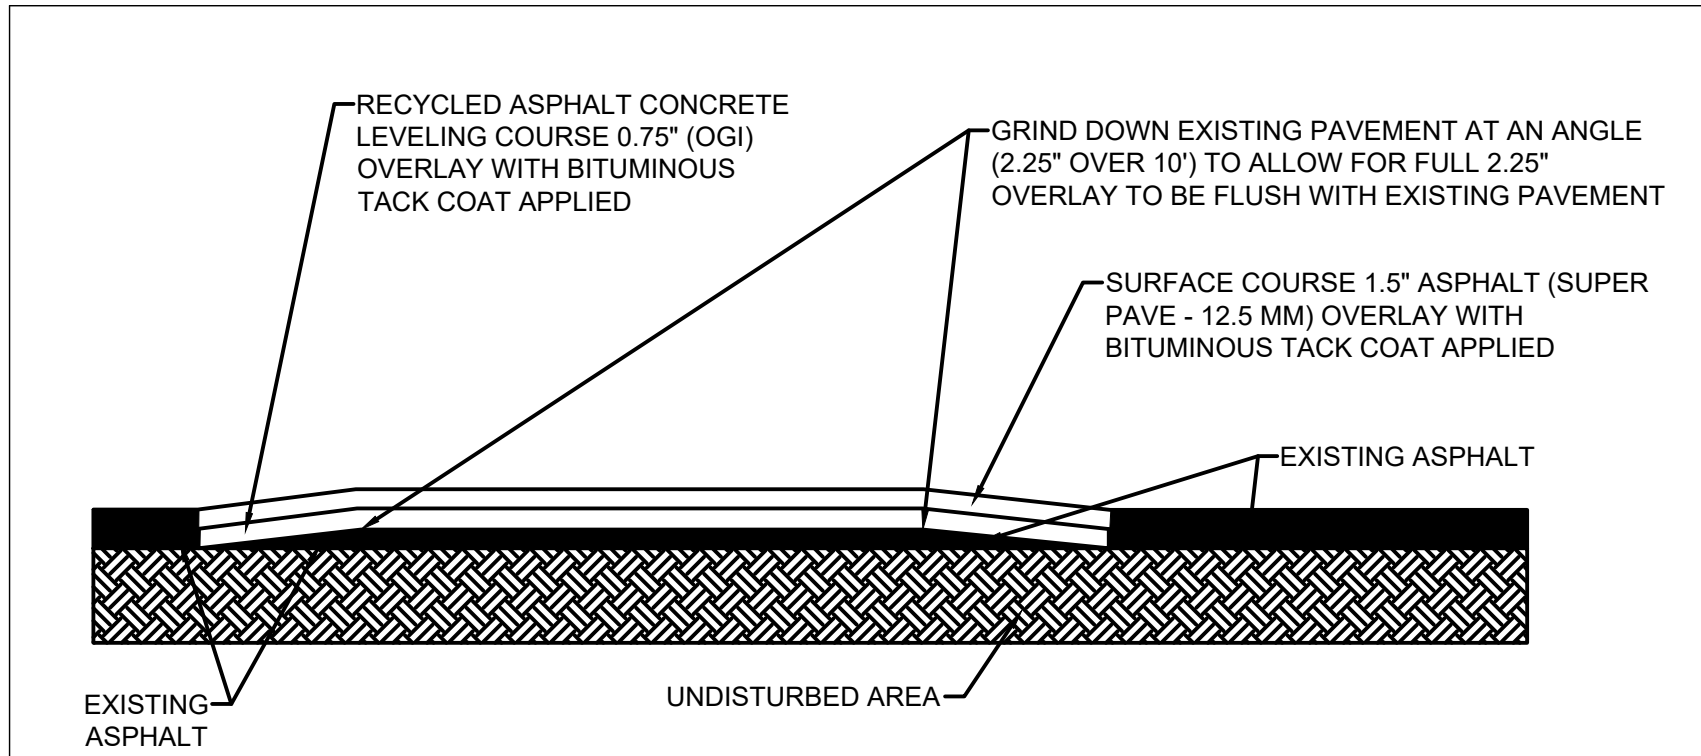

**NOT TO SCALE**

1.5" PAVING OVERLAY CONNECTION TO EXISTING PAVEMENT WITH OG

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES



| NO. |   | REVISION DESCRIPTION | DATE |
|-----|---|----------------------|------|
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |

40'20'0'40'

GRAPHIC SCALE: 1" = 40'

EMC ENGINEERING SERVICES, INC.

3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 965-9983  
Fax: (706) 965-9983  
columbus@emc-eng.com  
www.emc-eng.com

emc

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (1)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA

Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS

PROJECT NO.: 26-7011

DRAWN BY: TRM

DESIGNED BY: TRM

SURVEYED BY: ----

SURVEY DATE: ----

CHECKED BY: CEB

SCALE: 1" = 40'

DATE: 5/29/2026

SHEET

5



OF 13

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES

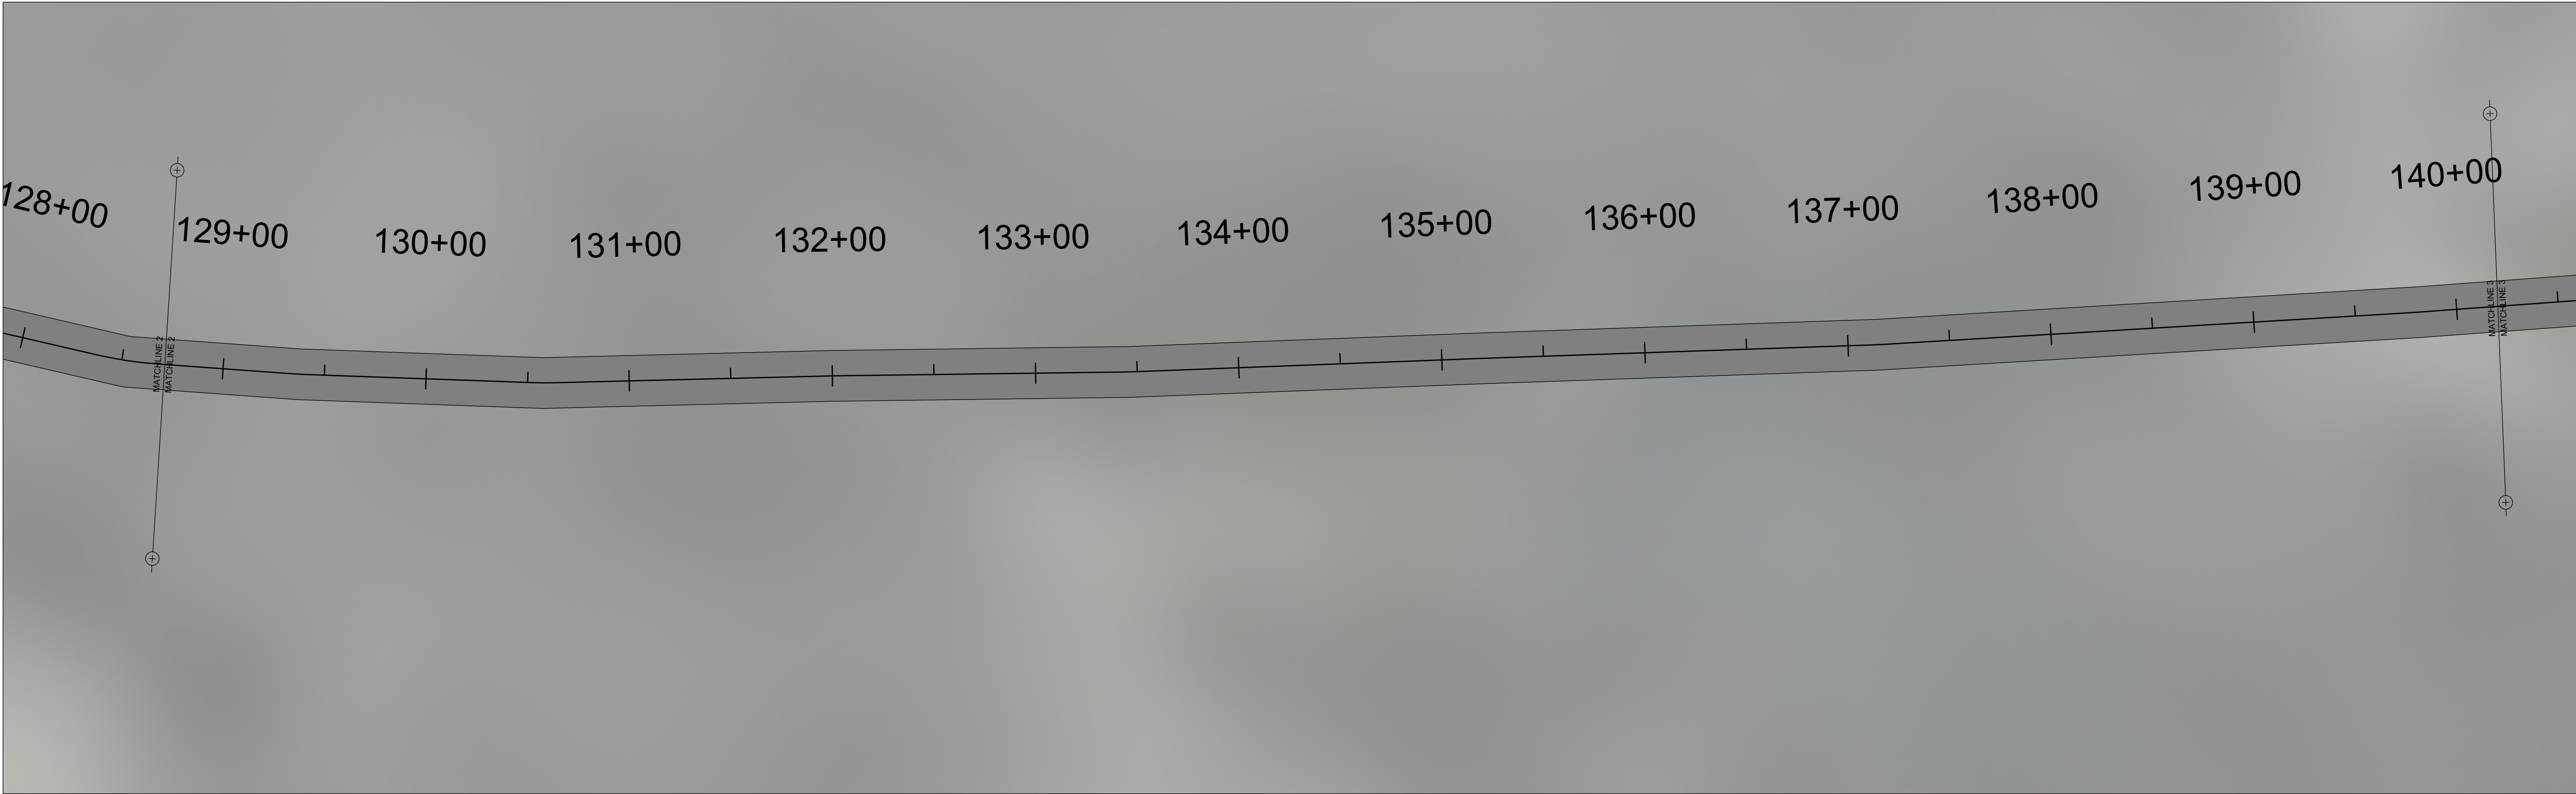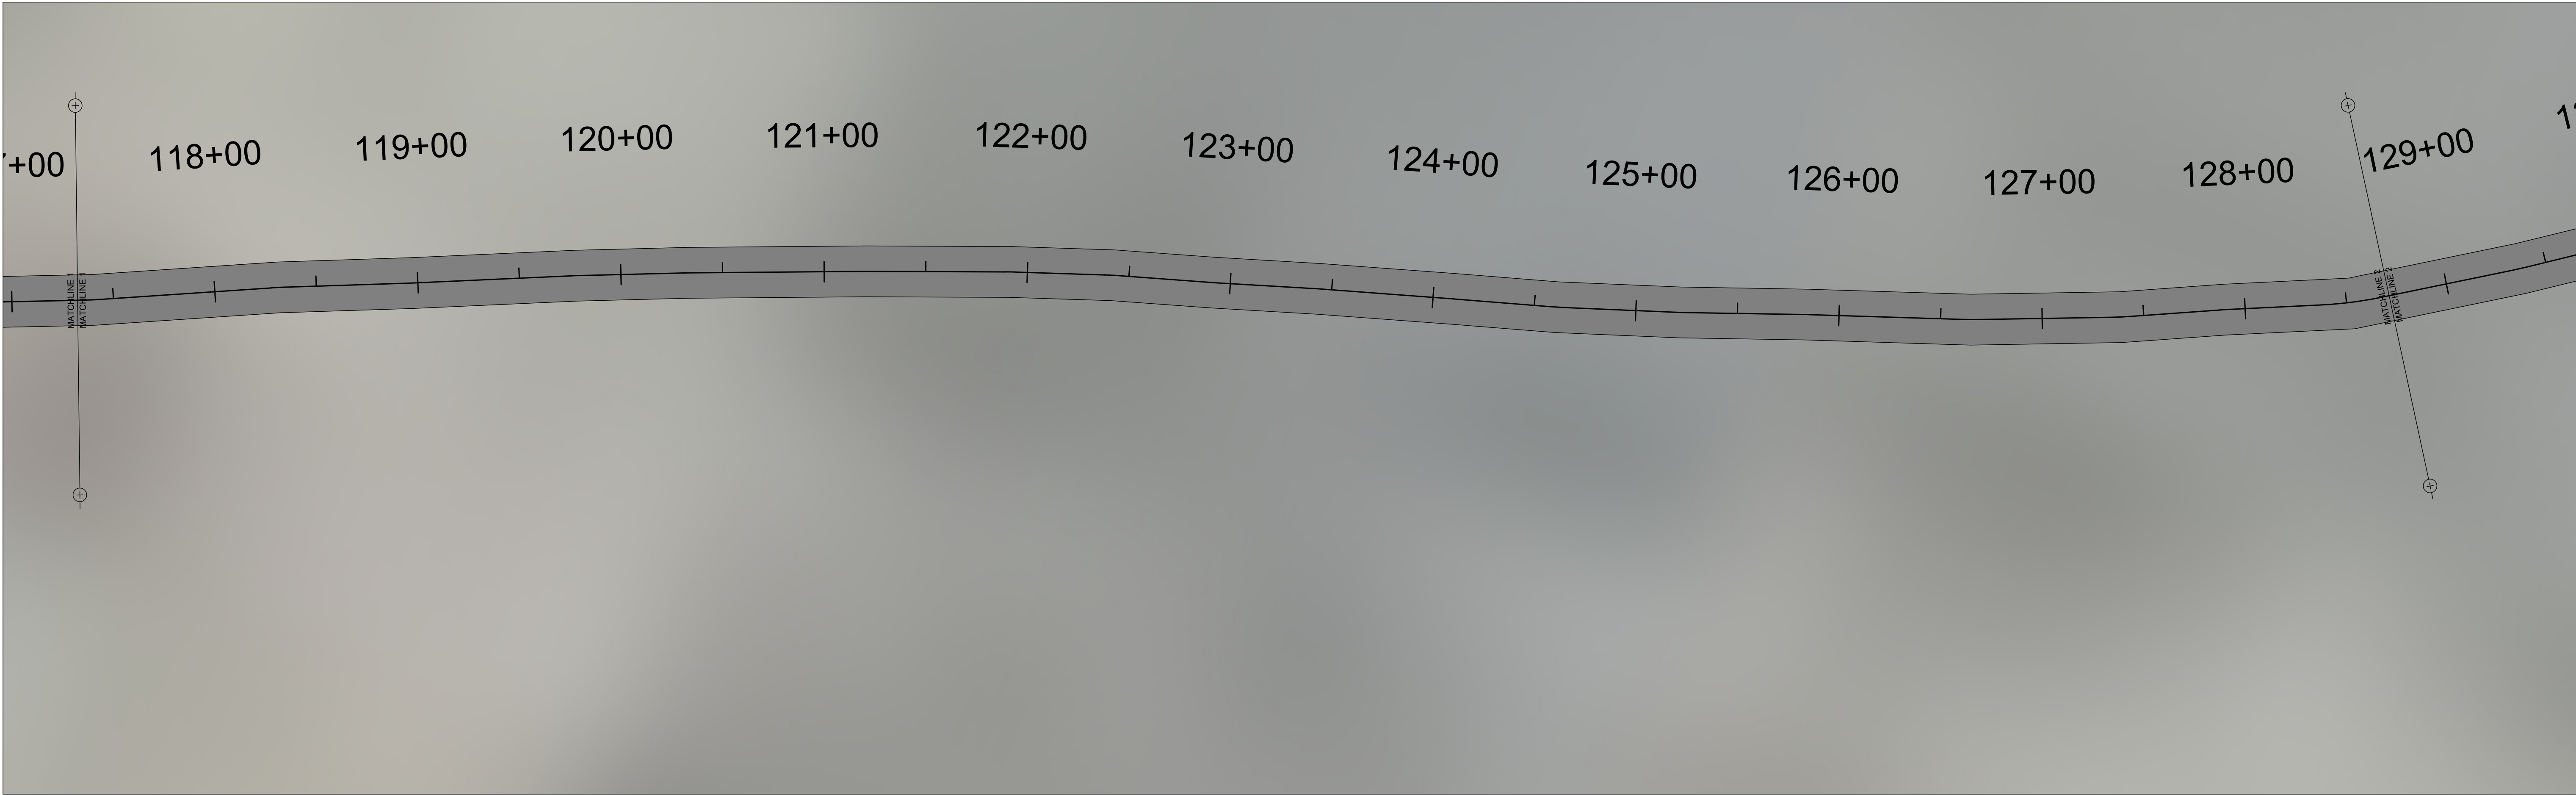

| NO. |  | REVISION DESCRIPTION | DATE |
|-----|--|----------------------|------|
| -   |  | -                    | -    |
| -   |  | -                    | -    |
| -   |  | -                    | -    |
| -   |  | -                    | -    |
| -   |  | -                    | -    |
| -   |  | -                    | -    |



EMC ENGINEERING SERVICES, INC.  
3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 965-9583  
Fax: (706) 965-9583  
columbus@emc-eng.com  
www.emc-eng.com

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (2)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA  
Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS

|              |           |
|--------------|-----------|
| PROJECT NO.: | 26-7011   |
| DRAWN BY:    | TRM       |
| DESIGNED BY: | TRM       |
| SURVEYED BY: | ----      |
| SURVEY DATE: | ----      |
| CHECKED BY:  | CEB       |
| SCALE:       | 1" = 40'  |
| DATE:        | 5/29/2026 |



SHEET  
6  
OF 13

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES

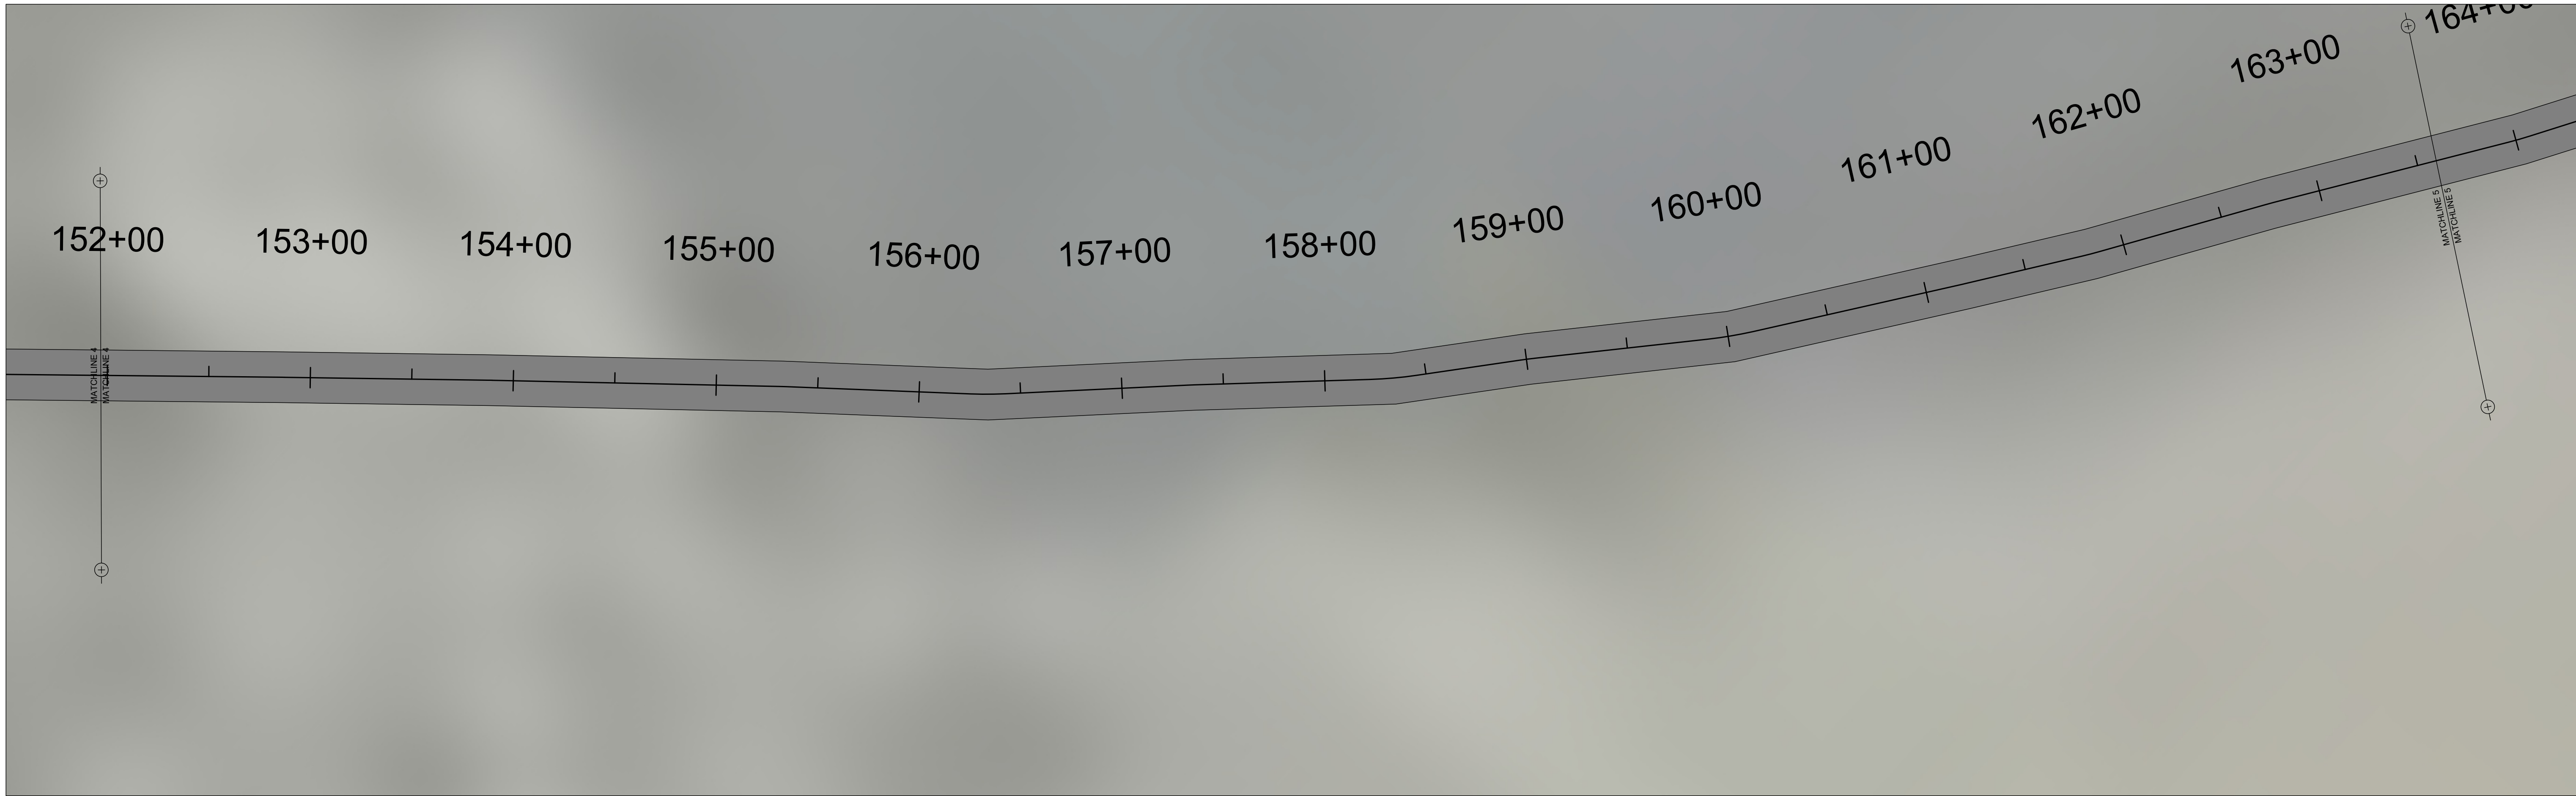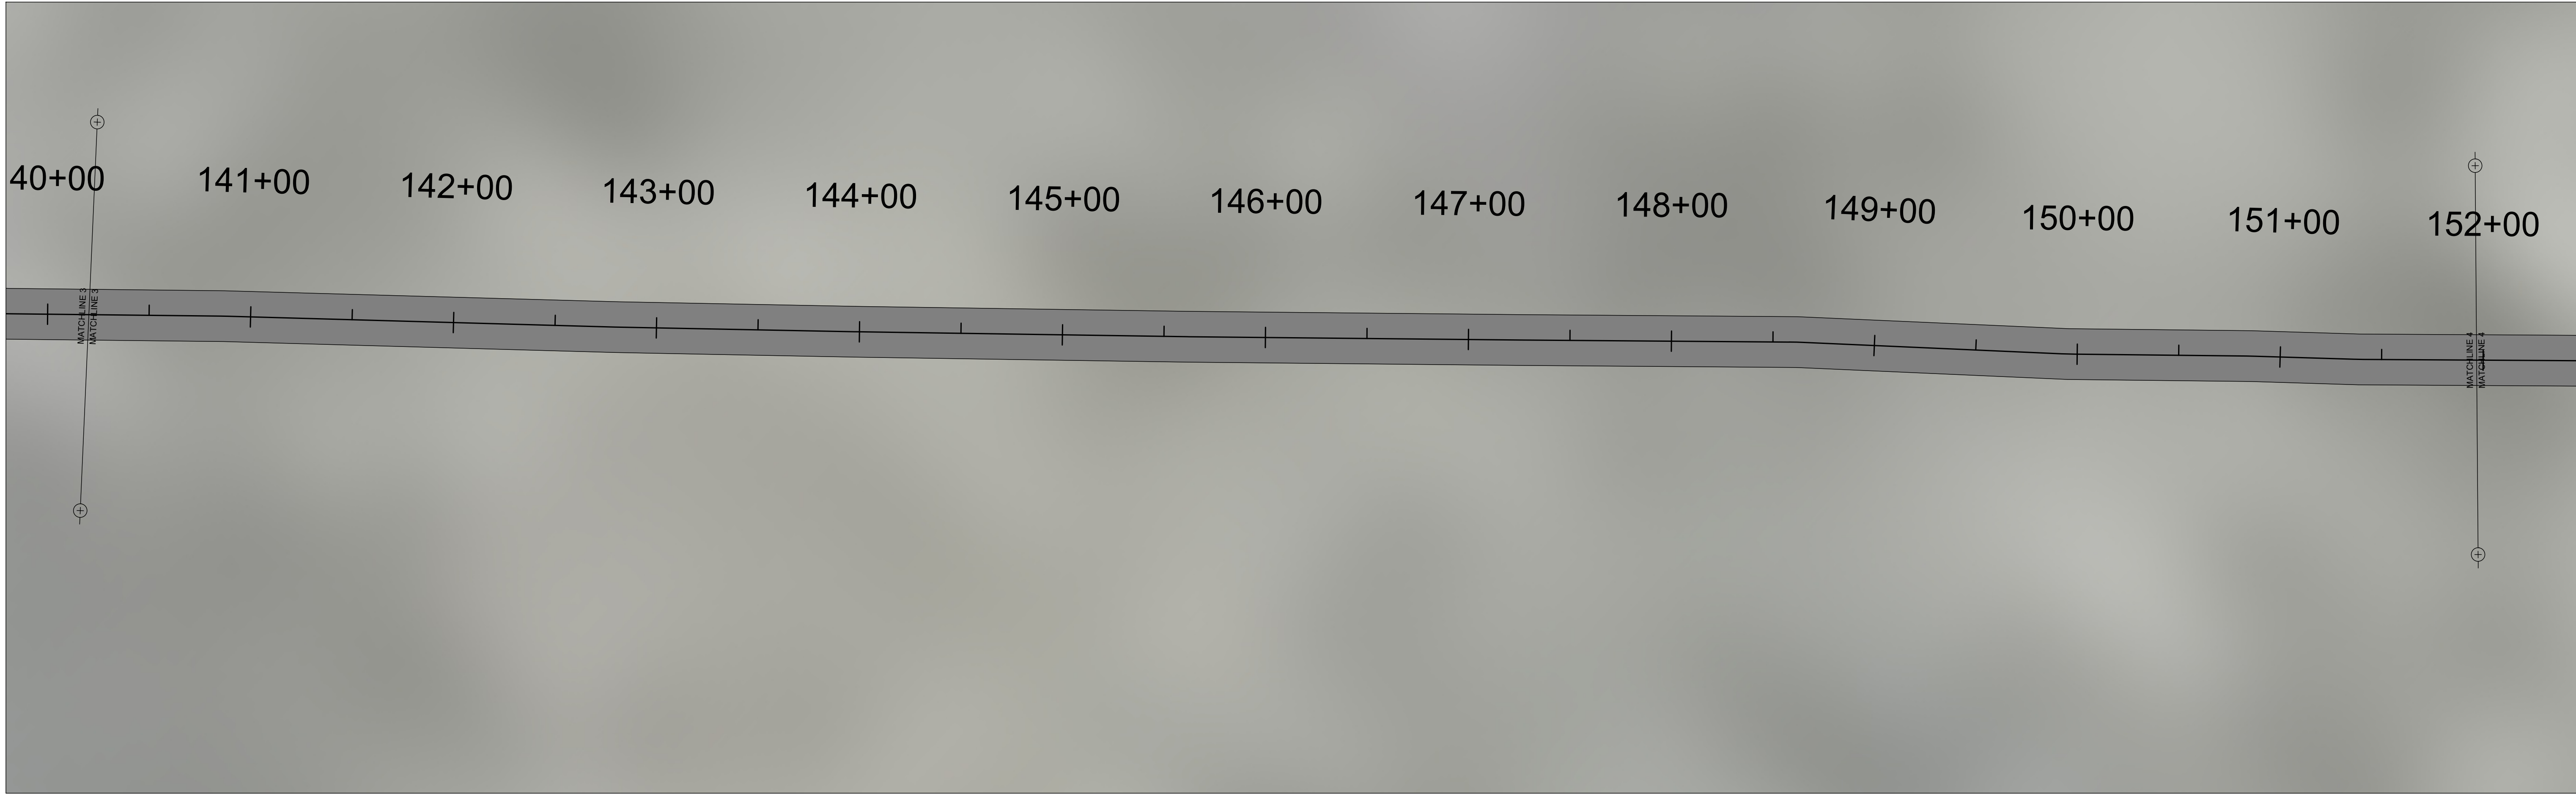

| NO. | REVISION DESCRIPTION | DATE |
|-----|----------------------|------|
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |

40'20'0'40'

GRAPHIC SCALE: 1" = 40'

EMC ENGINEERING SERVICES, INC.

3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 966-9983  
Fax: (706) 966-9983  
columbus@emc-eng.com  
www.emc-eng.com

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (3)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA

Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS

PROJECT NO.: 26-7011

DRAWN BY: TRM

DESIGNED BY: TRM

SURVEYED BY: ----

SURVEY DATE: ----

CHECKED BY: CEB

SCALE: 1" = 40'

DATE: 5/29/2026

SHEET

7



OF 13

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES

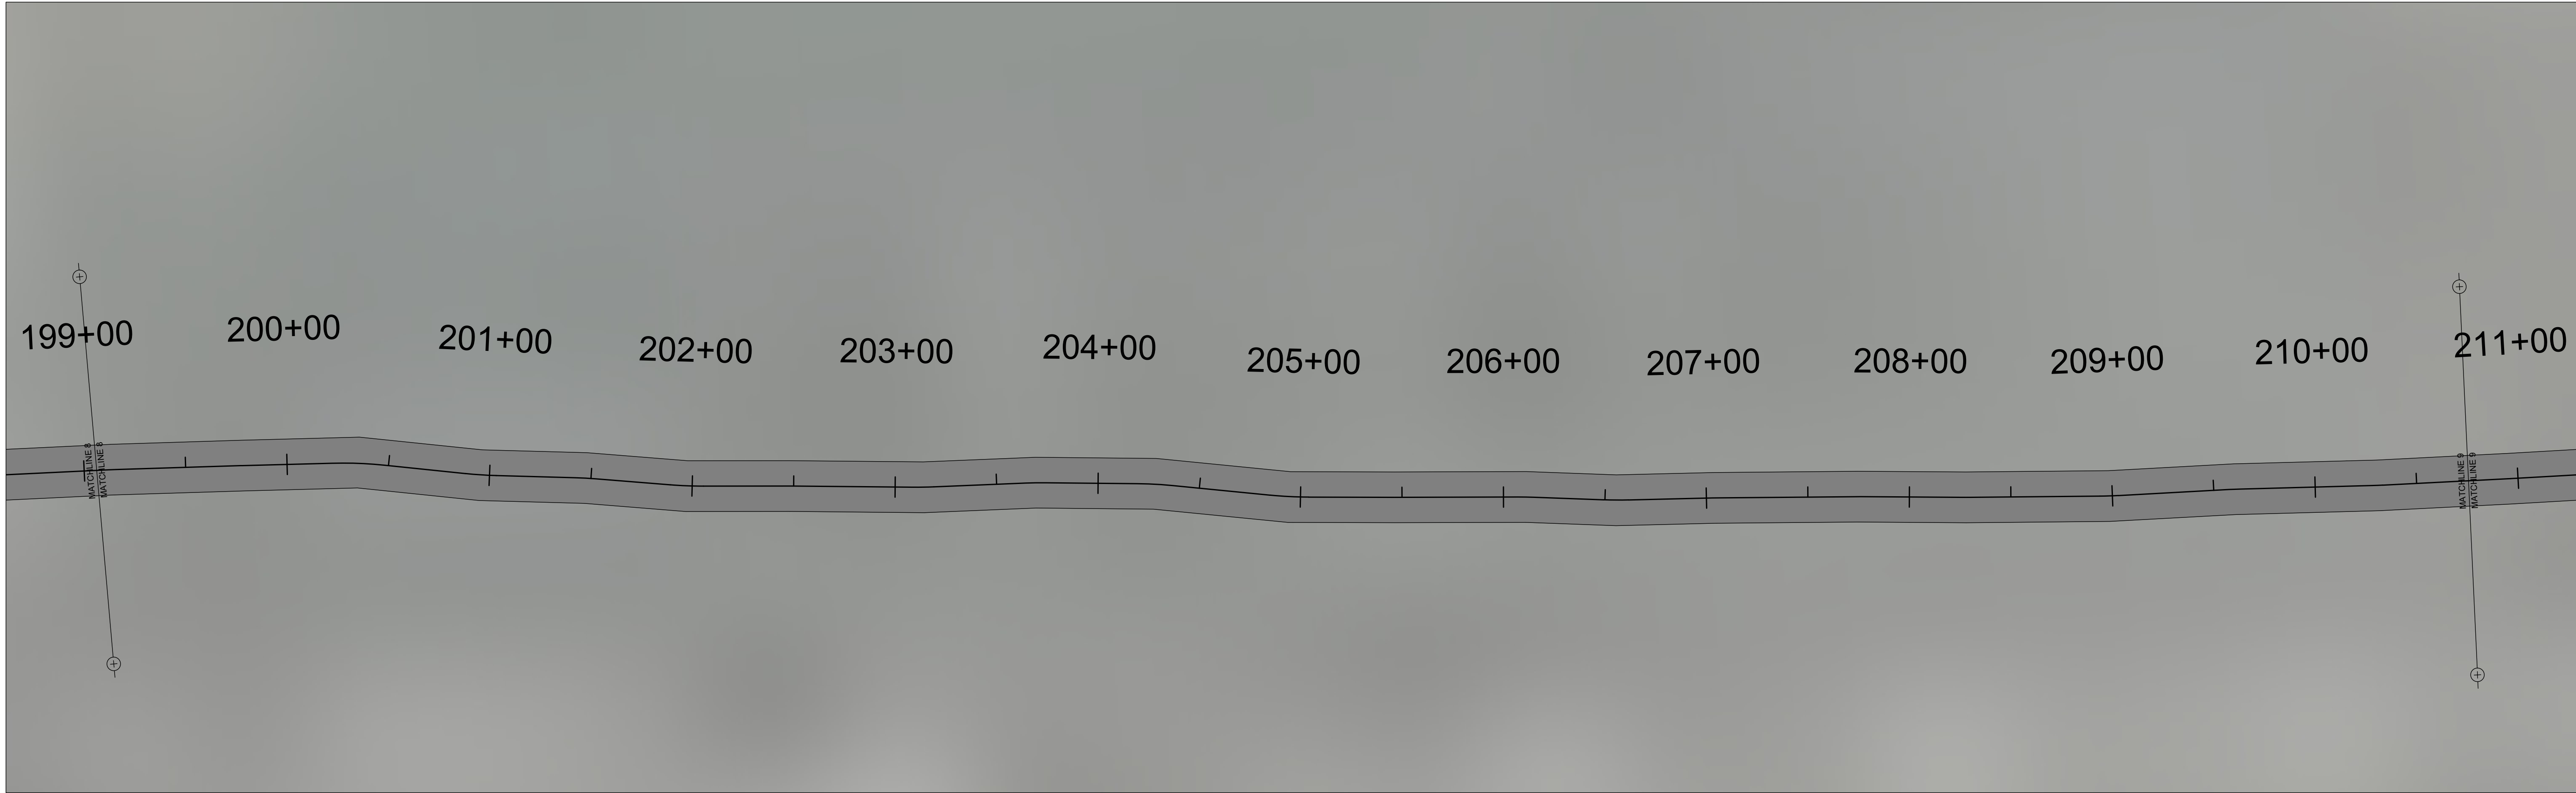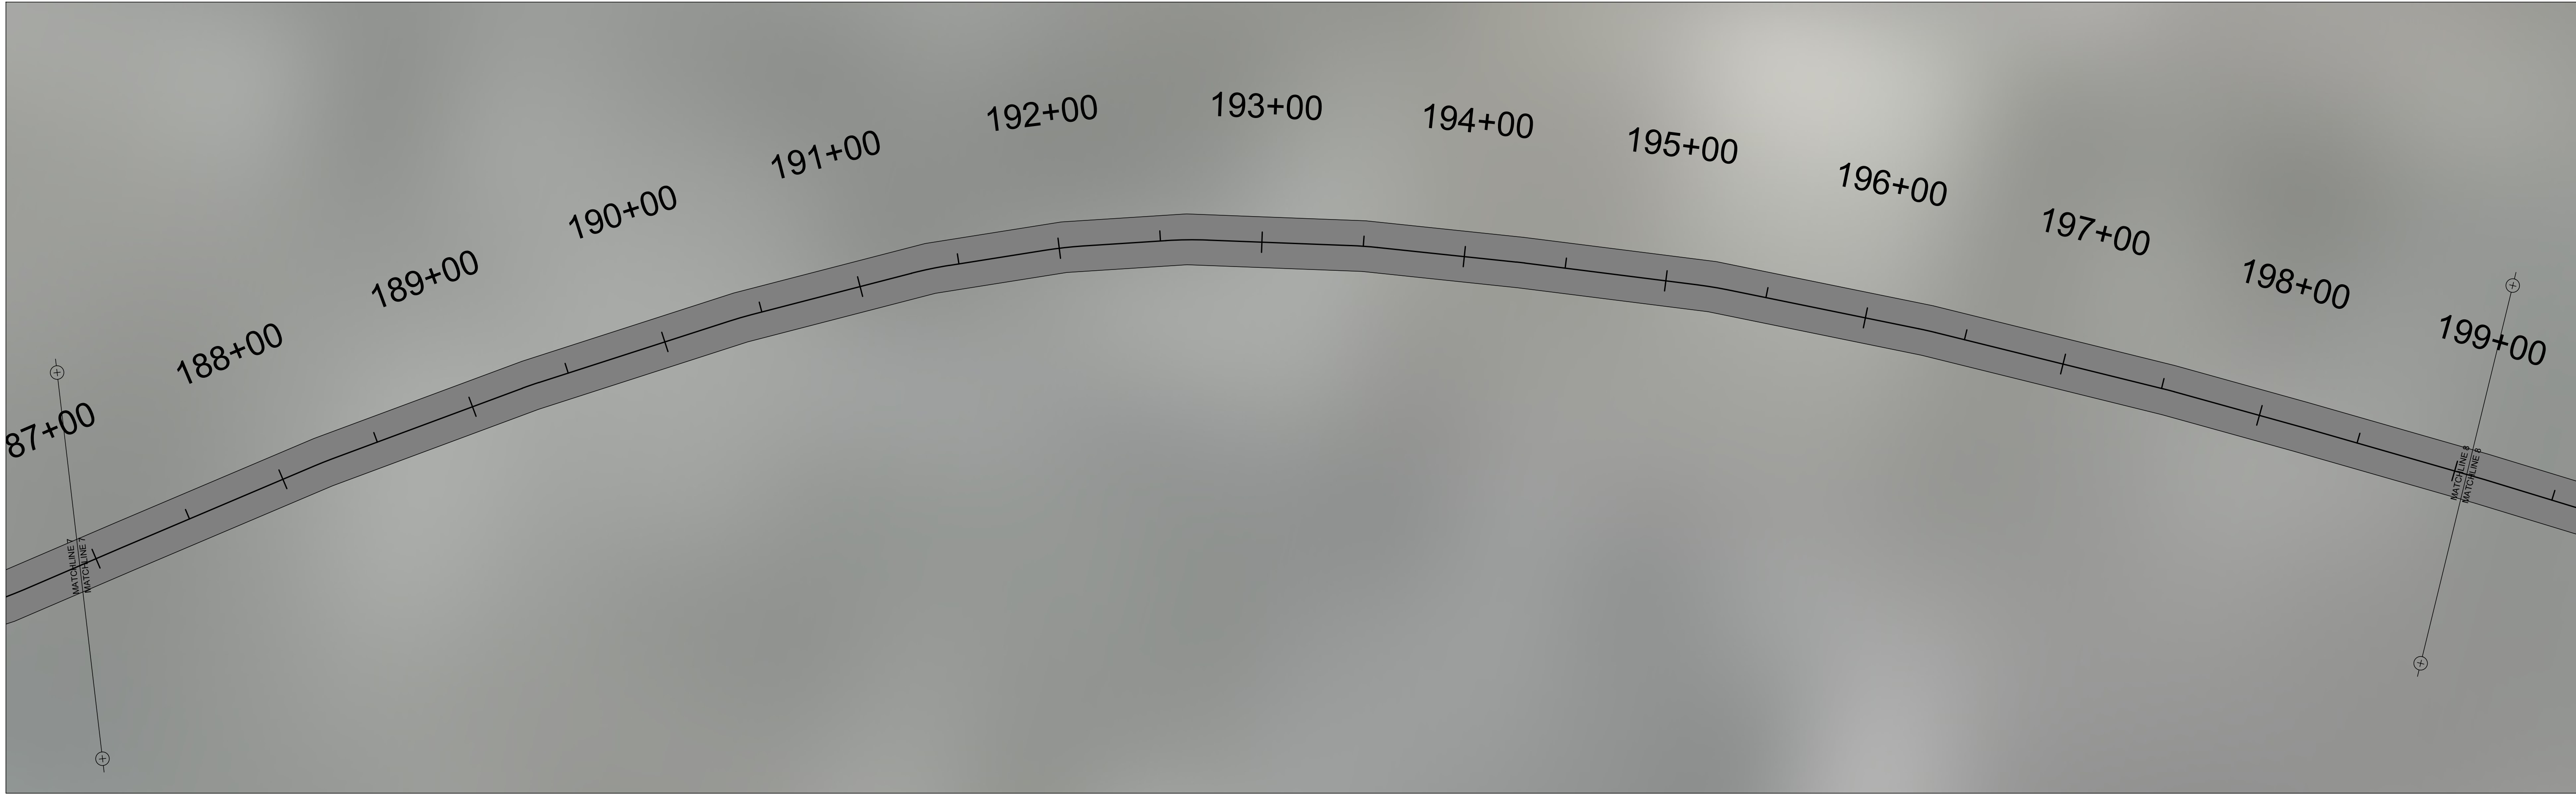

| NO. | REVISION DESCRIPTION | DATE |
|-----|----------------------|------|
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |



GRAPHIC SCALE: 1" = 40'

EMC ENGINEERING SERVICES, INC.  
3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 965-9583  
Fax: (706) 965-9583  
columbus@emc-eng.com  
www.emc-eng.com

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (4)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA  
Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS



|              |           |
|--------------|-----------|
| PROJECT NO.: | 26-7011   |
| DRAWN BY:    | TRM       |
| DESIGNED BY: | TRM       |
| SURVEYED BY: | ----      |
| SURVEY DATE: | ----      |
| CHECKED BY:  | CEB       |
| SCALE:       | 1" = 40'  |
| DATE:        | 5/29/2026 |

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES

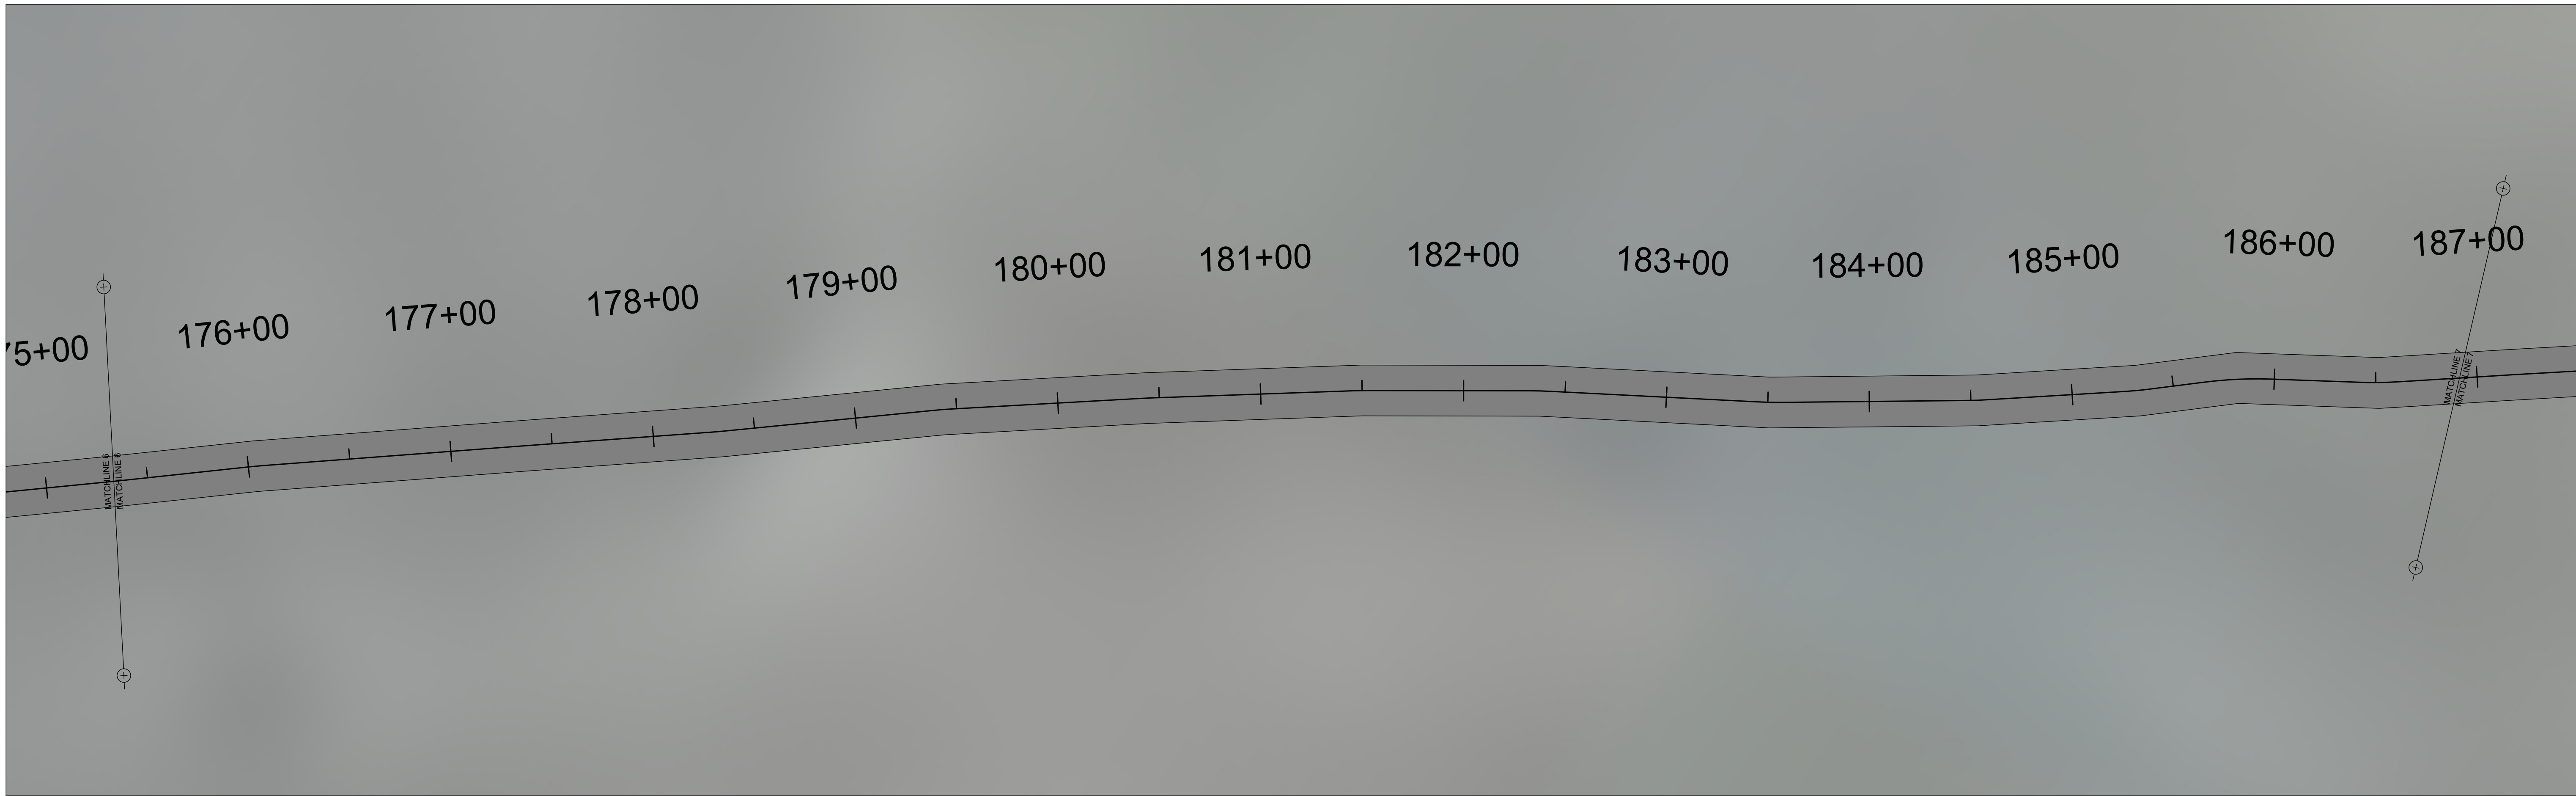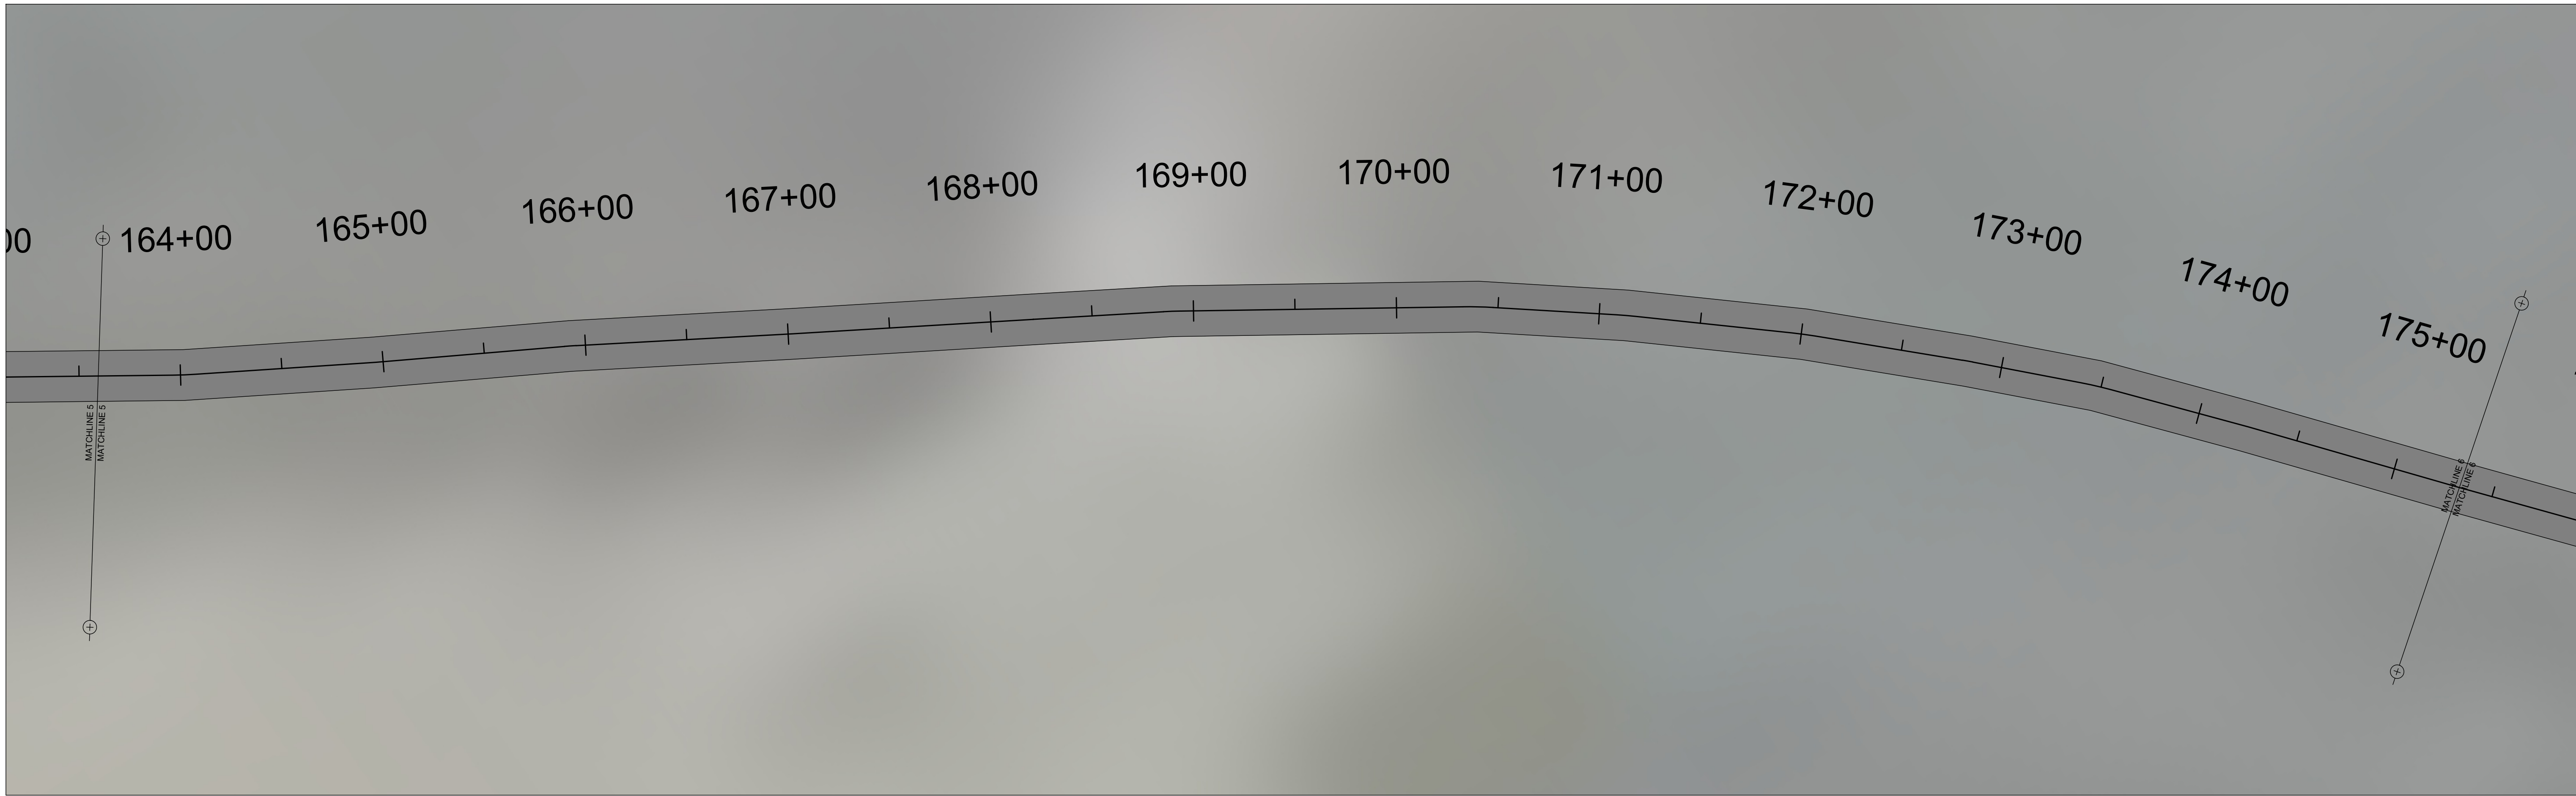

| REVISION DESCRIPTION |  | DATE |
|----------------------|--|------|
| NO.                  |  |      |
| 1                    |  |      |
| 2                    |  |      |
| 3                    |  |      |
| 4                    |  |      |
| 5                    |  |      |
| 6                    |  |      |
| 7                    |  |      |

40'20'0'40'

GRAPHIC SCALE: 1" = 40'

EMC ENGINEERING SERVICES, INC.

3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 965-9583  
Fax: (706) 965-9583  
columbus@emc-eng.com  
www.emc-eng.com

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (5)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA  
Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS

PROJECT NO.: 26-7011

DRAWN BY: TRM

DESIGNED BY: TRM

SURVEYED BY: ----

SURVEY DATE: ----

CHECKED BY: CEB

SCALE: 1" = 40'

DATE: 5/29/2026

SHEET

9



OF 13

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES

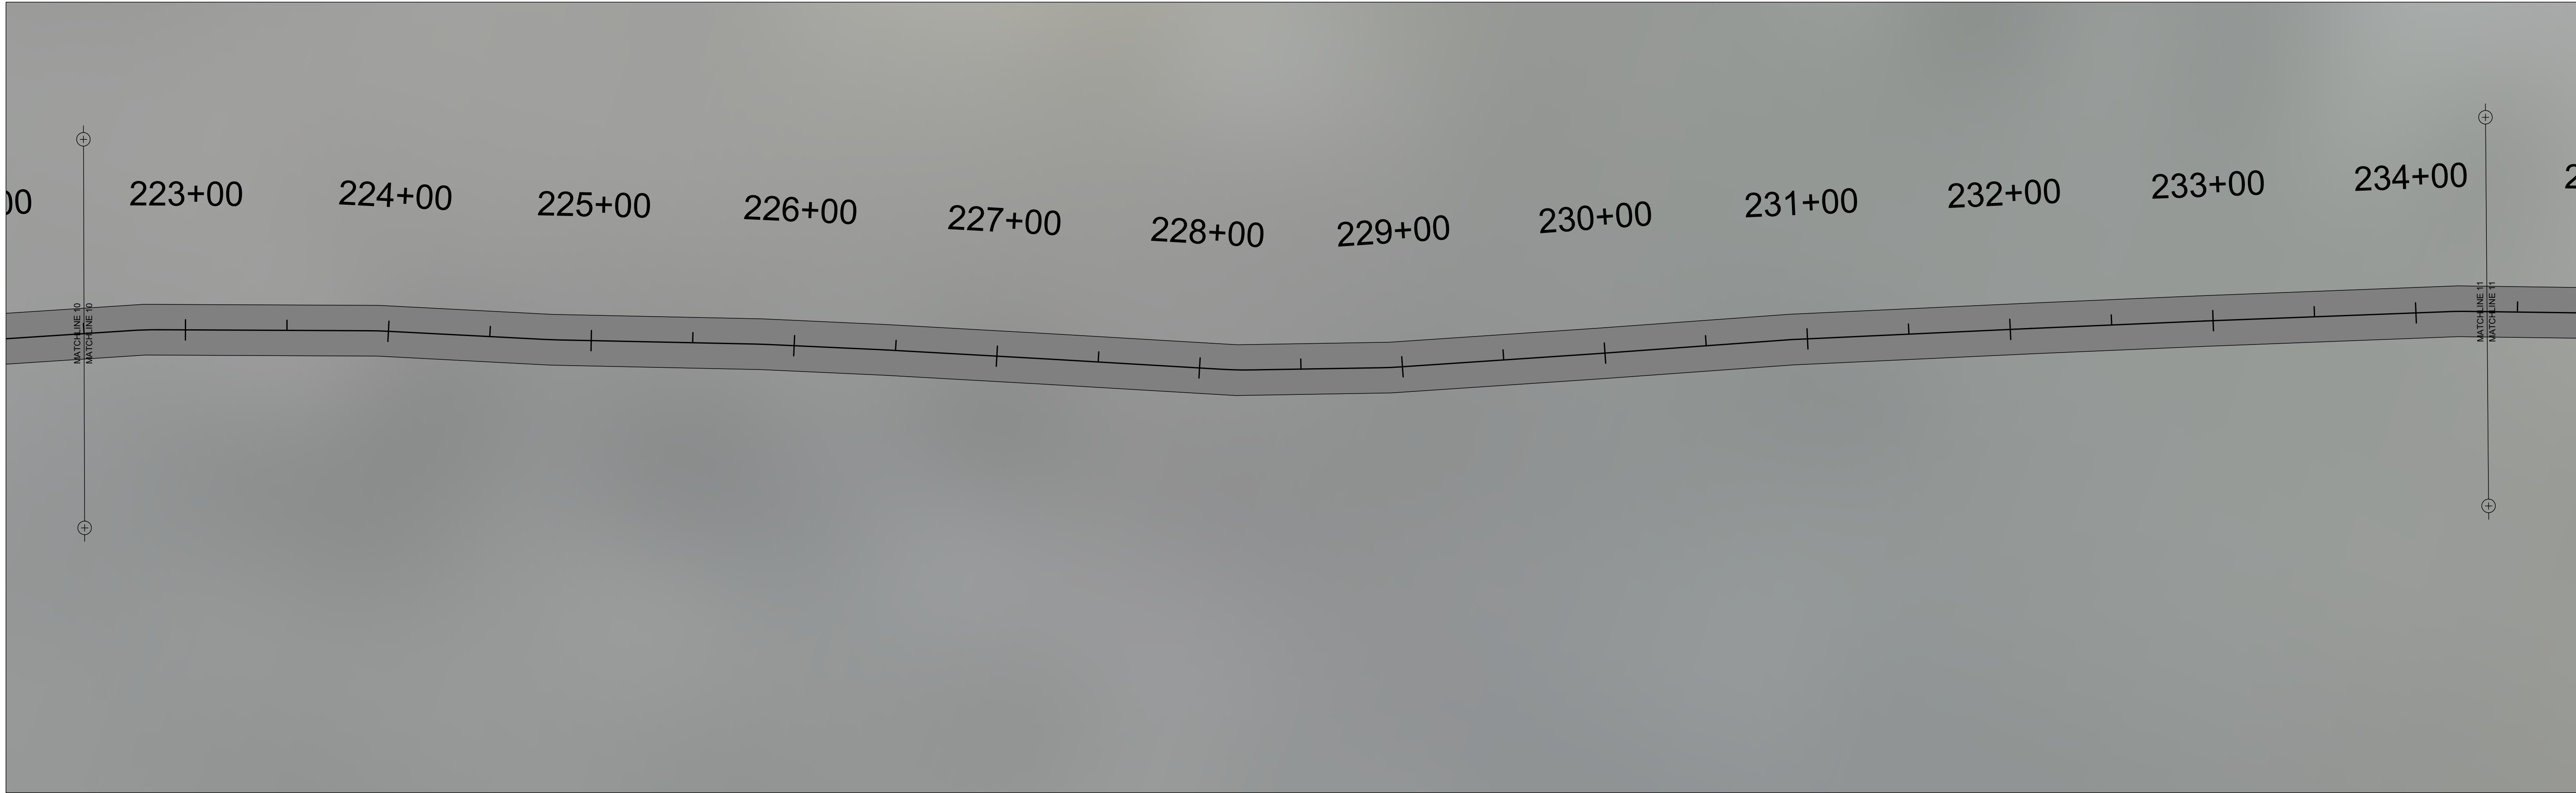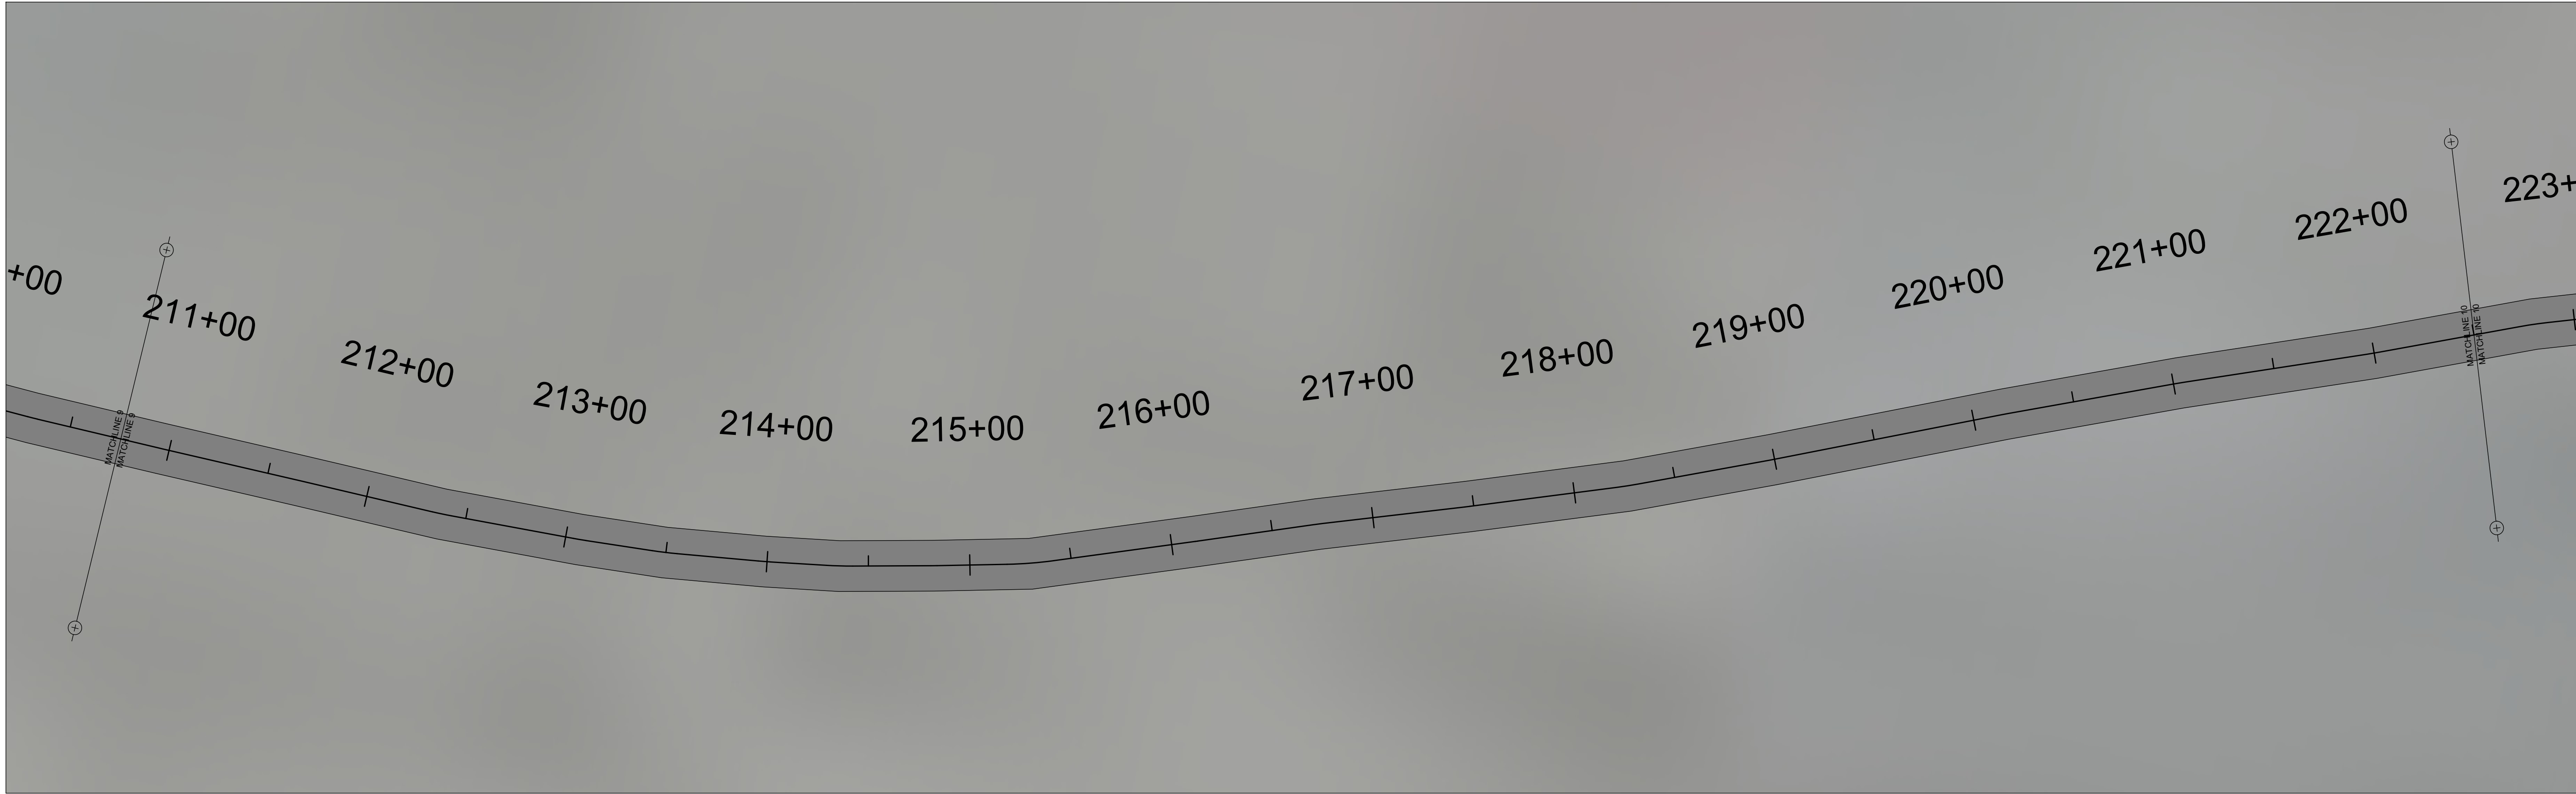

| REVISION DESCRIPTION |  | DATE |
|----------------------|--|------|
| NO.                  |  |      |
| 1.                   |  |      |
| 2.                   |  |      |
| 3.                   |  |      |
| 4.                   |  |      |
| 5.                   |  |      |
| 6.                   |  |      |
| 7.                   |  |      |

40'20'0'40'

GRAPHIC SCALE: 1" = 40'

EMC ENGINEERING SERVICES, INC.

3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 965-9583  
Fax: (706) 965-9583  
columbus@emc-eng.com  
www.emc-eng.com

emc

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (6)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA

Prepared for:

MERIWETHER COUNTY BOARD OF COMMISSIONERS

|              |           |
|--------------|-----------|
| PROJECT NO.: | 26-7011   |
| DRAWN BY:    | TRM       |
| DESIGNED BY: | TRM       |
| SURVEYED BY: | ----      |
| SURVEY DATE: | ----      |
| CHECKED BY:  | CEB       |
| SCALE:       | 1" = 40'  |
| DATE:        | 5/29/2026 |

SHEET

10



OF13

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES

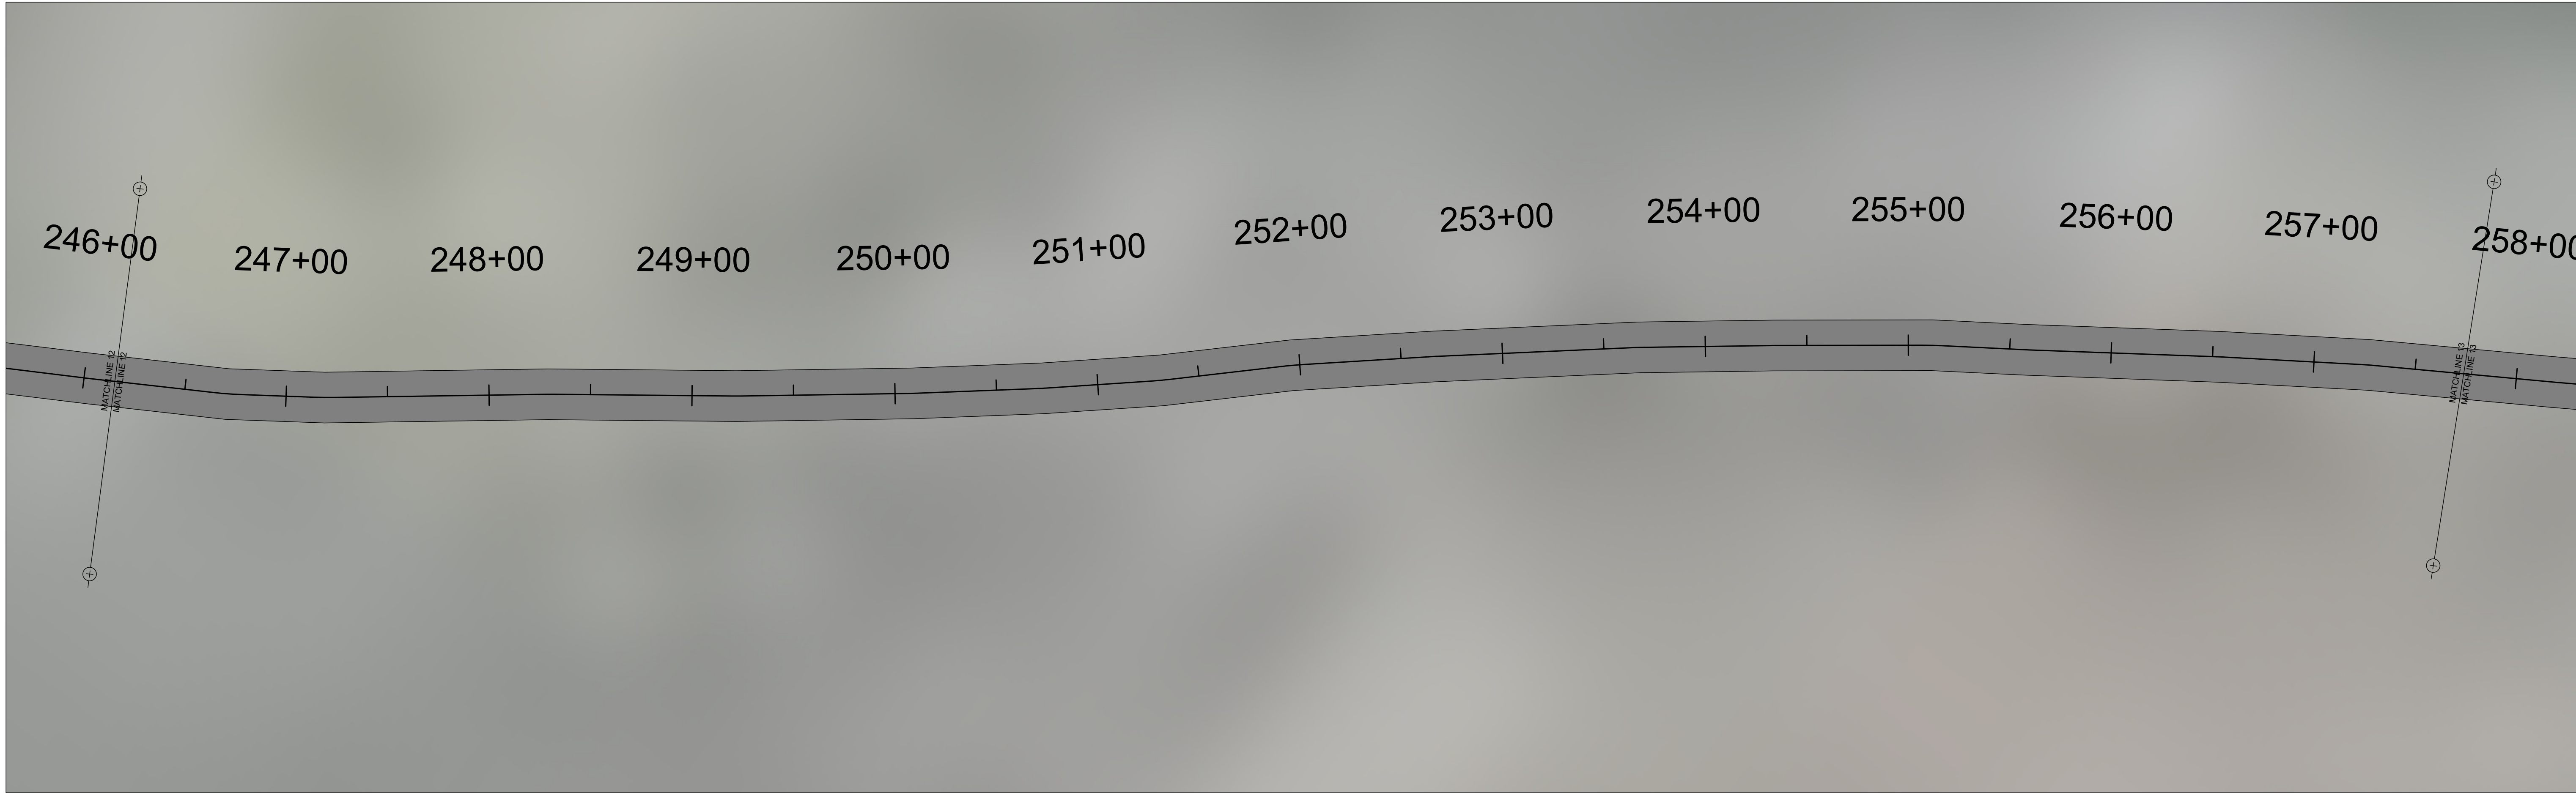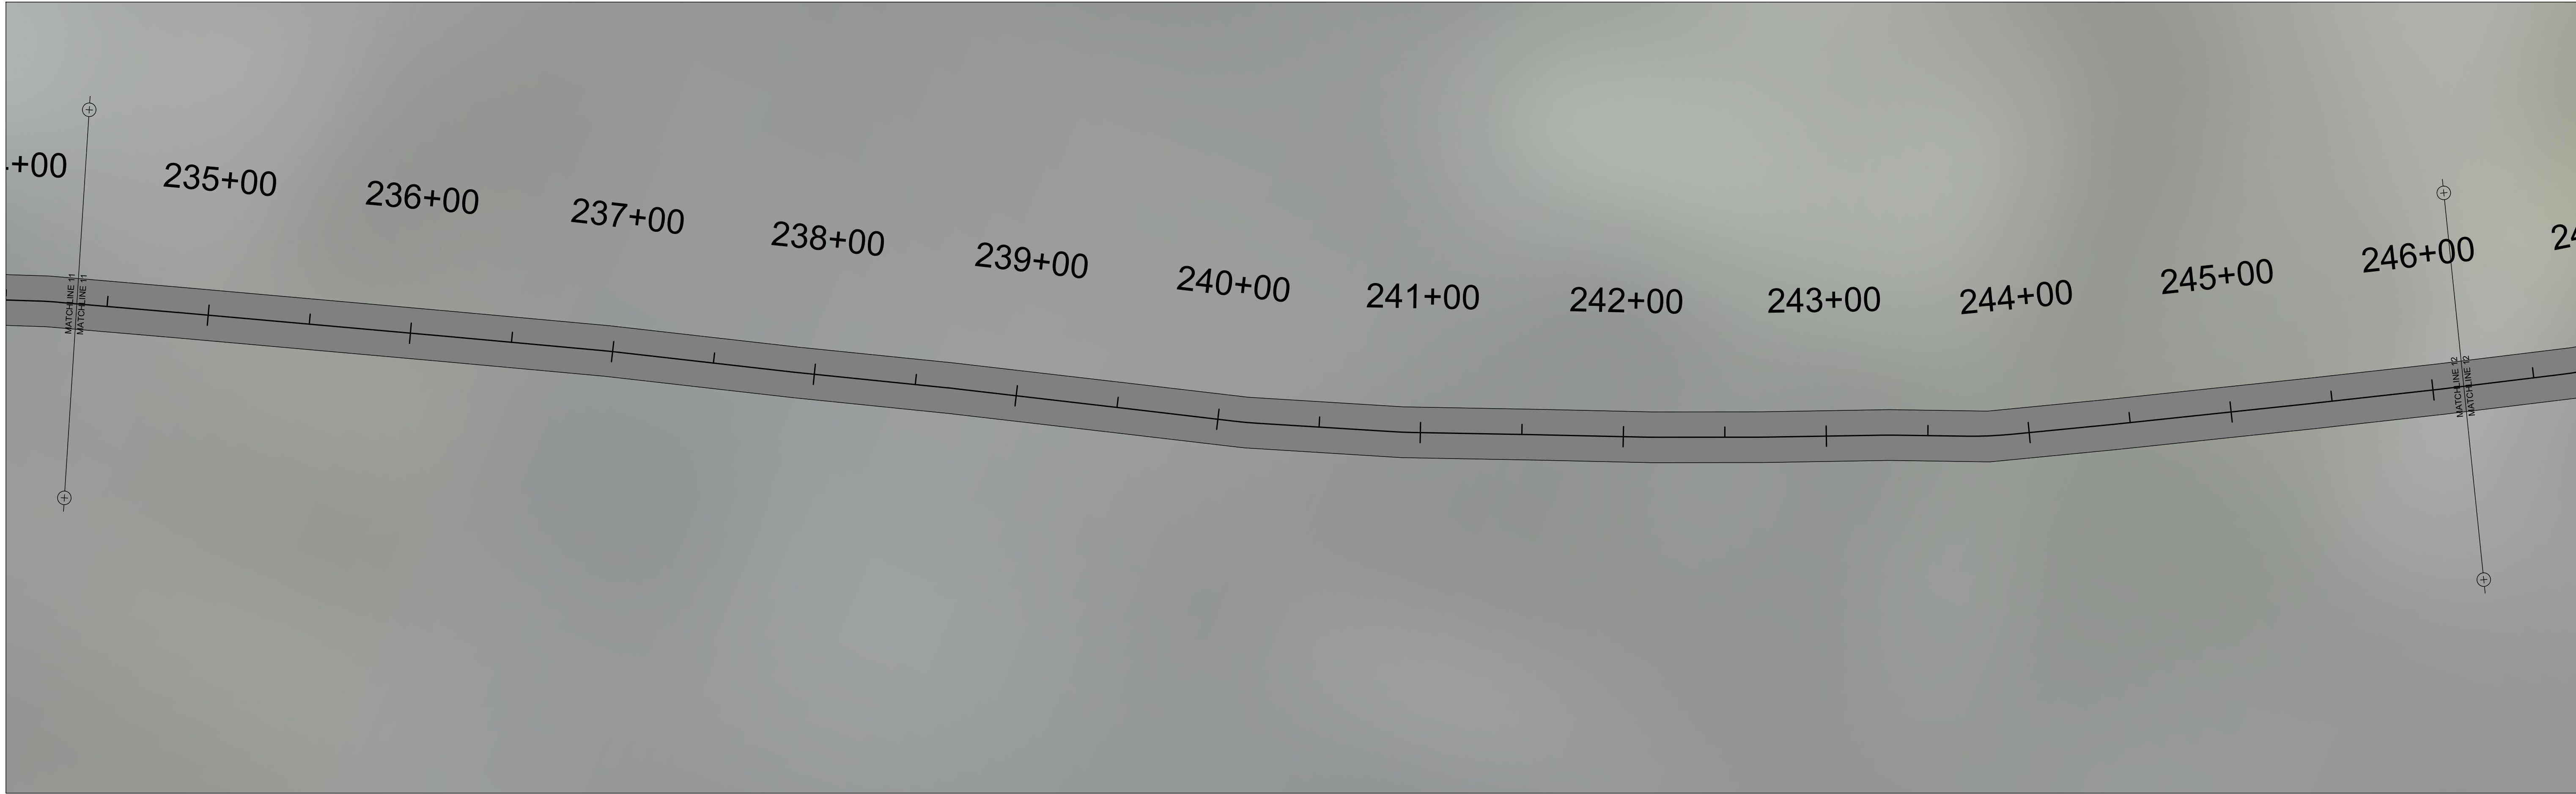

| NO. | REVISION DESCRIPTION | DATE |
|-----|----------------------|------|
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |

40'20'0'40'

GRAPHIC SCALE: 1" = 40'

EMC ENGINEERING SERVICES, INC.

3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 965-5583  
Fax: (706) 965-5583  
columbus@emc-eng.com  
www.emc-eng.com

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (11)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA  
Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS

PROJECT NO.: 26-7011

DRAWN BY: TRM

DESIGNED BY: TRM

SURVEYED BY: ----

SURVEY DATE: ----

CHECKED BY: CEB

SCALE: 1" = 40'

DATE: 5/29/2026

SHEET

11



OF 13

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES

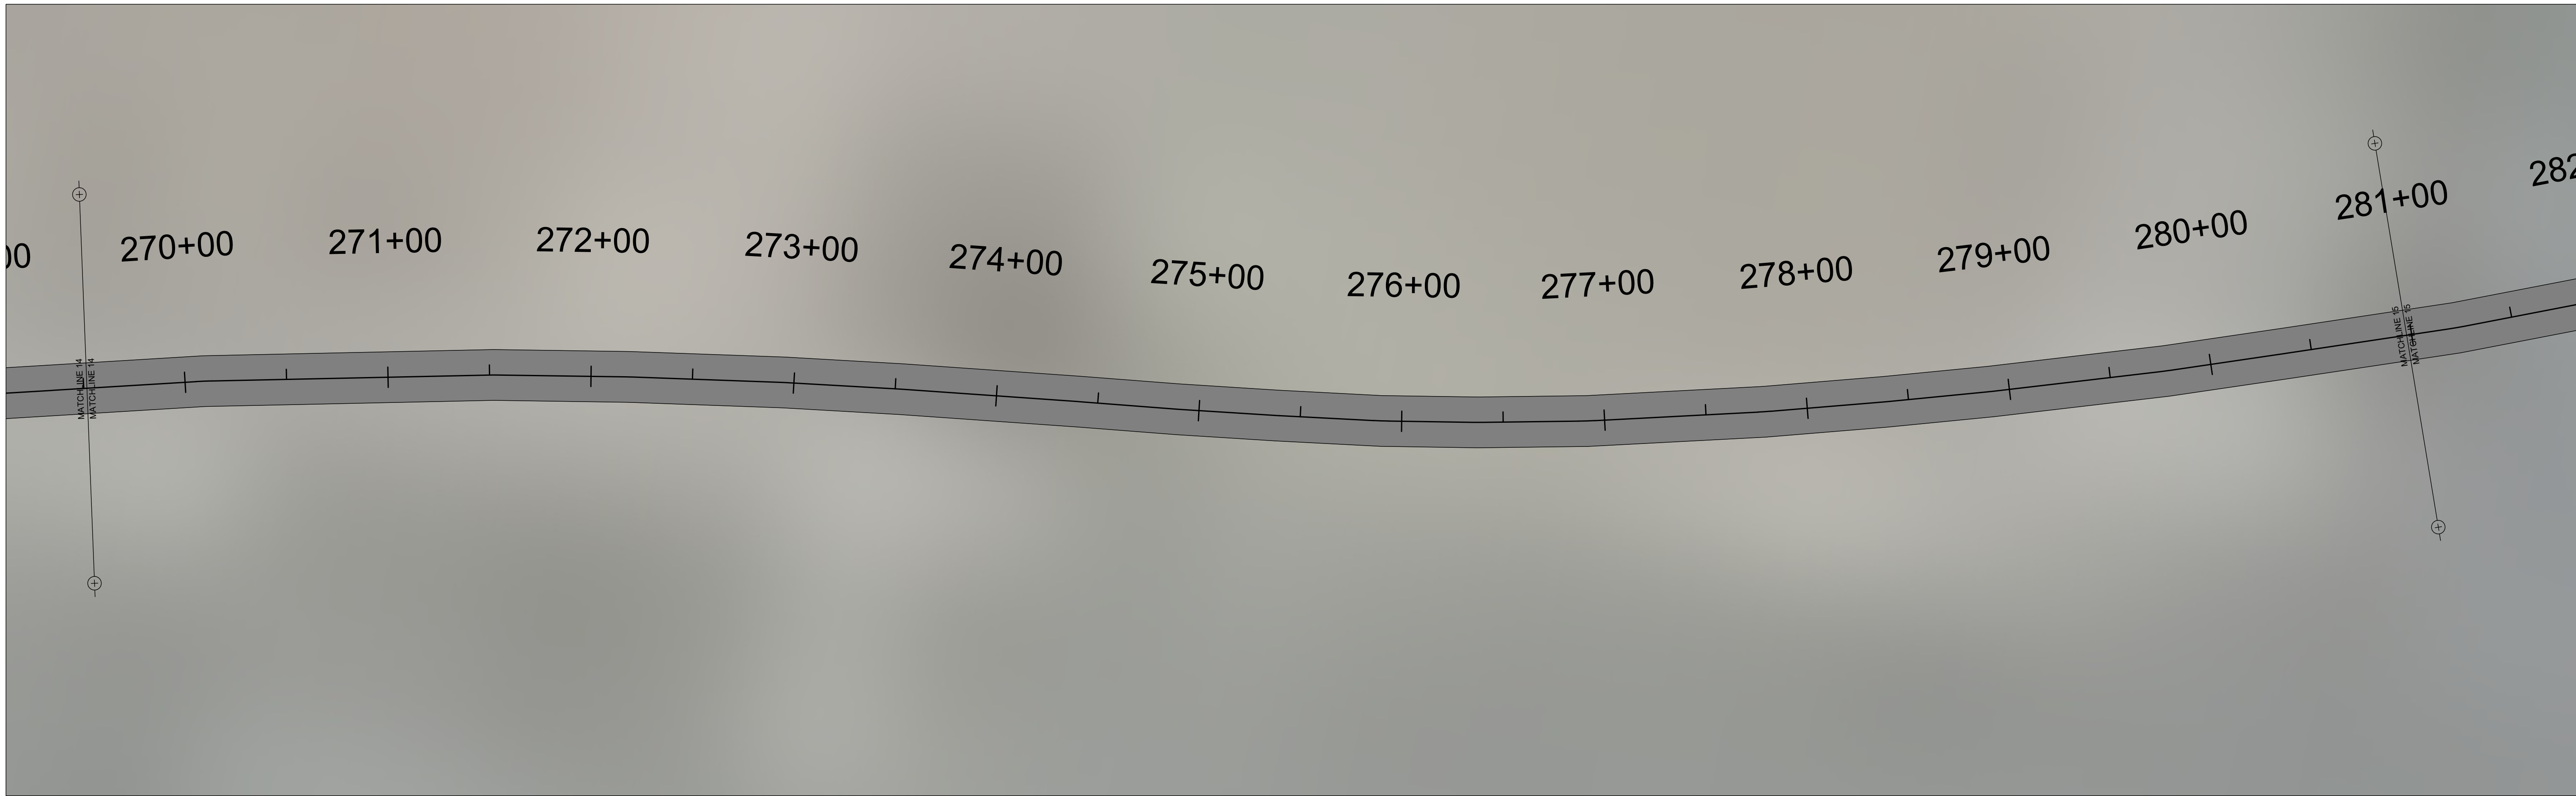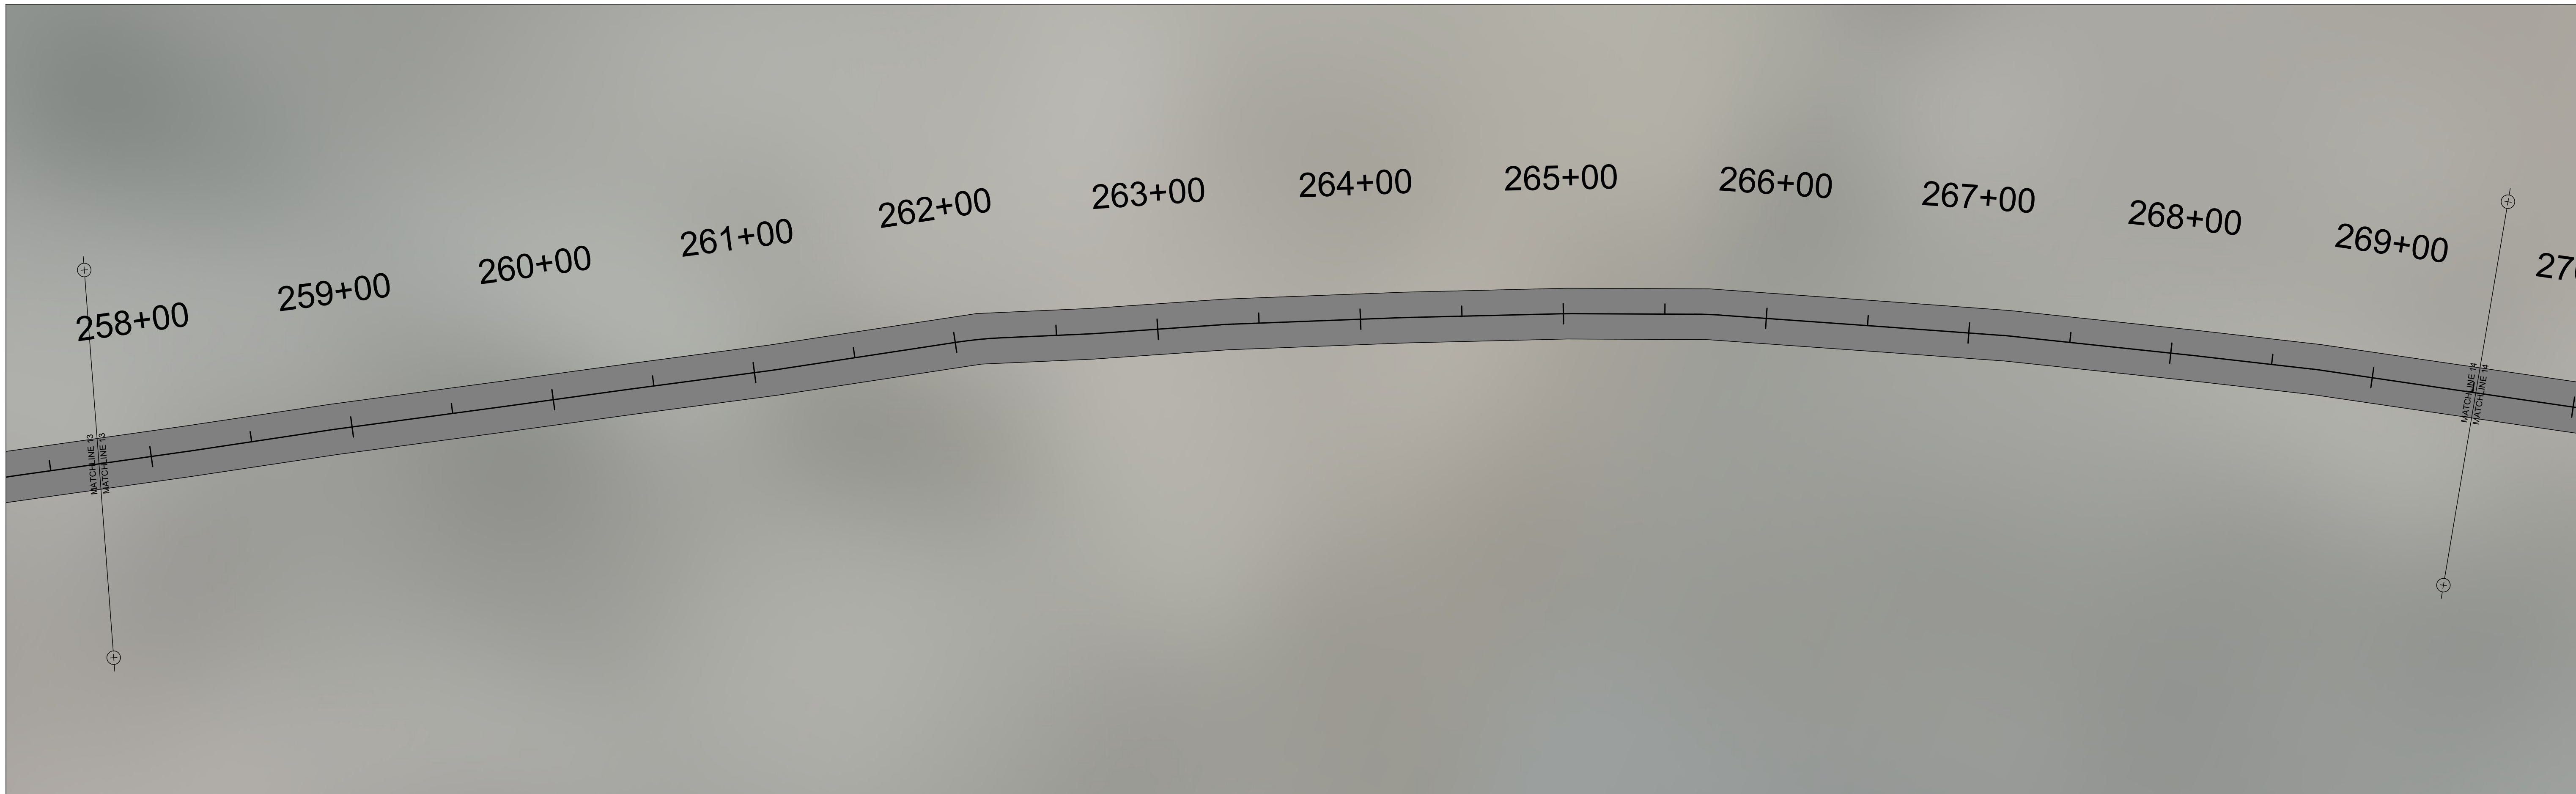

| NO. | REVISION DESCRIPTION | DATE |
|-----|----------------------|------|
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |
|     |                      |      |

40'20'0'40'

GRAPHIC SCALE: 1" = 40'

EMC ENGINEERING SERVICES, INC.

3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 965-9583  
Fax: (706) 965-9583  
columbus@emc-eng.com  
www.emc-eng.com

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (12)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA  
Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS

PROJECT NO.: 26-7011

DRAWN BY: TRM

DESIGNED BY: TRM

SURVEYED BY: ----

SURVEY DATE: ----

CHECKED BY: CEB

SCALE: 1" = 40'

DATE: 5/29/2026

SHEET

12

OF 13

PROJECT DESCRIPTION: RESURFACING OF ALVATON ROAD FROM 2 MILES WEST OF HWY 85 TO LUTHERVILLE ROAD (3.5 MI).  
ALVATON ROAD IS 24.5 FT WIDE.

- PROJECT NOTES:
1. BACKFILL SHOULDER, GRADE, COMPACT, TEMP AND PERMANENT GRASS
  2. INSTALL MILL ASPHALT CONCRETE PAVEMENT AT EXISTING ROAD TRANSITIONS AND BRIDGES
  3. INSTALL 85 LBS/SY OGI LEVELING COURSE
  4. INSTALL 165 LBS/SY 12.5 MM SUPERPAVE WEARING COURSE.
  5. INSTALL BITUMINOUS TACK COAT
  6. PAINT SOLID WHITE LINE ON BOTH SIDES, YELLOW TRAFFIC, AND YELLOW CENTERLINE
  7. PAVE SIDE ROADS TO BACK OF THE RIGHT OF WAY AND PROVIDE A 2 FT ASPHALT APRON FOR ALL DRIVEWAYS

# ALVATON ROAD

3.5 MILES



| NO. |   | REVISION DESCRIPTION | DATE |
|-----|---|----------------------|------|
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |
| -   | - | -                    | -    |

GRAPHIC SCALE: 1" = 40'

40' 20' 0' 40'

EMC ENGINEERING SERVICES, INC.

3575 Macon Rd., Suite 15  
Columbus, GA 31907  
Ph: (706) 966-5883  
Fax: (706) 966-5883  
columbus@emc-eng.com  
www.emc-eng.com

emc

CIVIL  
MARINE  
ENVIRONMENTAL

ALBANY • ATLANTA • AUGUSTA • BRUNSWICK • COLUMBUS  
GREENVILLE • SAVANNAH • STATESBORO • THOMASTON • VALDOSTA

ALVATON ROAD (13)

2026 RESURFACING AND STRIPING PROJECT PHASE II

MERIWETHER CO., GEORGIA

Prepared for:  
MERIWETHER COUNTY BOARD OF COMMISSIONERS

PROJECT NO.: 26-7011

DRAWN BY: TRM

DESIGNED BY: TRM

SURVEYED BY: ----

SURVEY DATE: ----

CHECKED BY: CEB

SCALE: 1" = 40'

DATE: 5/29/2026

SHEET

13

OF 13
